


HANDOUT 12A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 50)

JUNE 22, 2022 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2021				2022				2023				2024					
							Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4			
1	IM Installation (Note that IM3 is currently in operation and will remain in operation until directed otherwise by agencies)	512 days	Thu 1/22/04	Tue 12/20/05	Thu 1/22/04	Tue 12/20/05																		
32	IM3 Cultural Resources Management Plan (IM3 CRMP)	986 days	Thu 7/1/04	Mon 3/10/08	Thu 7/1/04	Mon 3/10/08																		
37	Extraction Well PE-1/Facilities	230 days	Mon 3/21/05	Fri 1/27/06	Mon 3/21/05	Fri 1/27/06																		
47	Supplemental Extraction Well and Facilities	127 days	Fri 7/29/05	Thu 1/19/06	Fri 7/29/05	Thu 1/19/06																		
55	Decommissioning of IM2 Batch Treatment	1182 days	Fri 8/5/05	Fri 1/29/10	Fri 8/5/05	Fri 1/29/10																		
66	Interim Measures and Treated Water Management	751 days	Mon 5/3/04	Fri 2/16/07	Mon 5/3/04	Fri 2/16/07																		
210	Public Participation Plan	578 days	Mon 12/20/04	Fri 2/9/07	Mon 12/20/04	Fri 2/9/07																		
219	Baseline Resources Assessments	897 days	Mon 11/1/04	Mon 3/10/08	Mon 11/1/04	Mon 3/10/08																		
233	Sitewide CEQA Documentation	586 days	Wed 5/17/06	Fri 8/1/08	Wed 5/17/06	Fri 8/1/08																		
237	Programmatic Biological Assessment (PBA)	1920 days	Tue 12/19/06	Tue 4/15/14	Tue 12/19/06	Tue 4/15/14																		
250	REMEDIAL FACILITY INVESTIGATION/REMEDIAL INVESTIGATION (RFI/RI)	7213 days?	Sat 2/24/96	Mon 9/4/23	Sat 2/24/96	NA																		
251	Historical RFI/RI Reports (Feb. 2005 and Prior Versions)	2455 days	Sat 2/24/96	Fri 7/8/05	Sat 2/24/96	Fri 7/8/05																		
269	Site History Report (Vol 1)	466 days	Tue 11/15/05	Wed 8/15/07	Tue 11/15/05	Wed 8/15/07																		
284	RFI/RI Vol 1 Addendum	1829 days	Wed 7/11/07	Tue 7/8/14	Wed 7/11/07	Tue 7/8/14																		
306	Final Groundwater RFI/RI (Vol 2)	1948 days	Mon 6/27/05	Fri 11/16/12	Mon 6/27/05	Fri 11/16/12																		
616	ADEQ Topock Groundwater Study	475 days	Thu 11/18/04	Wed 8/23/06	Thu 11/18/04	Wed 8/23/06																		
620	Final Soil RFI/RI (Vol 3)	4486 days?	Sat 7/15/06	Mon 9/4/23	Sat 7/15/06	NA																		
621	Implementation of Off-site Soil Sampling (Part A Phase 1) and Data Gaps Evaluation	1215 days	Sat 7/15/06	Fri 2/25/11	Sat 7/15/06	Fri 2/25/11																		
770	Draft On-site Soil Sampling (Part B) DQOs	1122 days	Wed 12/6/06	Fri 3/11/11	Wed 12/6/06	Fri 3/11/11																		
825	Soil RFI/RI Work Plan	1211 days	Tue 1/4/11	Mon 8/24/15	Tue 1/4/11	Mon 8/24/15																		
922	Work Plan Implementation/Data Gaps Analysis	594 days	Tue 8/25/15	Thu 11/30/17	Tue 8/25/15	Thu 11/30/17																		
978	Reporting	1623 days?	Tue 6/20/17	Mon 9/4/23	Tue 6/20/17	NA																		
979	Soil Risk Assessment	770 days	Tue 6/20/17	Fri 5/29/20	Tue 6/20/17	Fri 5/29/20																		
1002	Soil Risk Assessment Addendum (After Completion of Soil NTCRA)	176 days	Mon 1/2/23	Mon 9/4/23	NA	NA																		
1003	PG&E prepares/submits Soil Risk Assessment Addendum Report	2 mons	Mon 1/2/23	Tue 2/28/23	NA	NA																		
1004	DTSC review/comment	47 edays	Wed 3/1/23	Mon 4/17/23	NA	NA																		
1005	DOI review/comment	47 edays	Wed 3/1/23	Mon 4/17/23	NA	NA																		
1006	CWG/TWG review/comment	30 days	Wed 3/1/23	Tue 4/11/23	NA	NA																		
1007	Tribes review/comment	30 days	Wed 3/1/23	Tue 4/11/23	NA	NA																		
1008	Review/compile Comment Table	15 edays	Tue 4/18/23	Wed 5/3/23	NA	NA																		
1009	Prepare/send RTC Table (duration to be verified)	2 mons	Thu 5/4/23	Fri 6/30/23	NA	NA																		
1010	RTC Meeting	10 days	Fri 7/14/23	Fri 7/28/23	NA	NA																		
1011	Send agenda (2 wks prior to meeting)	0 days	Fri 7/14/23	Fri 7/14/23	NA	NA																		
1012	Hold Meeting	0 days	Fri 7/28/23	Fri 7/28/23	NA	NA																		
1013	Finalize/Submit Final Soil Risk Assessment Addendum Report with RTC Table	1 mon	Mon 7/31/23	Mon 8/28/23	NA	NA																		
1014	DTSC review/accept report	1 wk	Tue 8/29/23	Mon 9/4/23	NA	NA																		
1015	DOI review/accept report	1 wk	Tue 8/29/23	Mon 9/4/23	NA	NA																		
1016	RFI/RI Volume 3	1375 days?	Fri 7/28/17	Mon 10/31/22	Fri 7/28/17	NA																		
1017	Draft RFI/RI Volume 3 Report	881 days	Fri 7/28/17	Thu 12/10/20	Fri 7/28/17	Thu 12/10/20																		
1029	Revised RFI/RI Volume 3 Report	312 days?	Fri 12/11/20	Thu 2/17/22	Fri 12/11/20	Thu 2/17/22																		
1030	Prepare Revised RFI Volume 3 with RTC Table	5.86 mons	Fri 12/11/20	Mon 5/31/21	Fri 12/11/20	Mon 5/31/21																		
1031	DTSC sends report to CWG/TWG and Tribes	1 day	Tue 6/1/21	Tue 6/1/21	Tue 6/1/21	Tue 6/1/21																		

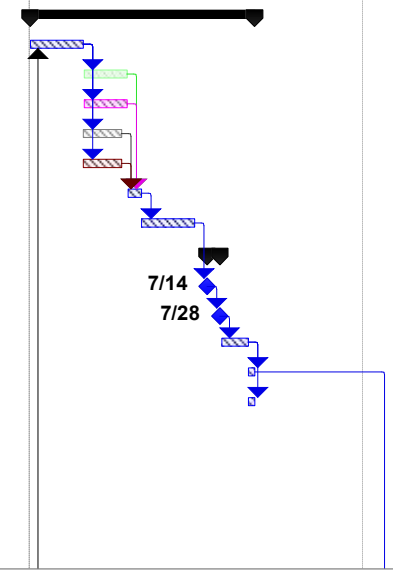

Project: PG&E Topock Remediation Project
 Date: Fri 6/17/22
 Page 1 of 10

Tasks Not Started/In Progress Overall Task Duration Manual Task Start-only

Tasks Finished Inactive Task Duration-only Finish-only

Baseline Schedule Inactive Milestone Manual Summary Rollup

Milestone Inactive Summary Manual Summary

edays = calendar days; days = work days
 Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
 *Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
 PG&E Federal Agencies CWG/TWG Public
 DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
 - Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
 - Actual dates may vary depending on field conditions.

HANDOUT 12A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 50)

JUNE 22, 2022 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2021		2022				2023				2024							
							Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4			
1032	CWG/TWG review/comment	91.38 edays	Tue 6/1/21	Tue 8/31/21	Tue 6/1/21	Tue 8/31/21																		
1033	Tribes review/comment	91.38 edays	Tue 6/1/21	Tue 8/31/21	Tue 6/1/21	Tue 8/31/21																		
1034	DTSC review/comment	115.38 edays	Tue 6/1/21	Fri 9/24/21	Tue 6/1/21	Fri 9/24/21																		
1035	DOI review/comment	115.38 edays	Tue 6/1/21	Fri 9/24/21	Tue 6/1/21	Fri 9/24/21																		
1036	Review/compile Comment Table	25.38 edays	Mon 9/27/21	Fri 10/22/21	Mon 9/27/21	Fri 10/22/21																		
1037	Prepare/send RTC Table	2 mons	Mon 10/25/21	Mon 12/20/21	Mon 10/25/21	Mon 12/20/21																		
1038	RTC Meeting	12 days?	Wed 1/26/22	Thu 2/10/22	Wed 1/19/22	Thu 2/17/22																		
1039	Send agenda (2 wks prior to meeting)	1 day	Wed 1/19/22	Wed 1/19/22	Wed 1/19/22	Wed 1/19/22																		
1040	Hold Meeting #1	1 day	Wed 2/9/22	Wed 2/9/22	Wed 2/9/22	Wed 2/9/22																		
1041	Hold Meeting #2	1 day	Thu 2/10/22	Thu 2/10/22	Thu 2/10/22	Thu 2/10/22																		
1042	Hold Meeting #3	1 day	Thu 2/17/22	Thu 2/17/22	Thu 2/17/22	Thu 2/17/22																		
1043	Finalize report	7.62 mons	Mon 2/21/22	Fri 9/30/22	Mon 2/21/22	NA																		
1044	DTSC review/approve	1 mon	Mon 10/3/22	Mon 10/31/22	NA	NA																		
1045	DOI review/approve	1 mon	Mon 10/3/22	Mon 10/31/22	NA	NA																		
1046	SOIL NON-TIME CRITICAL REMOVAL ACTION (NTCRA)	1302 days	Tue 10/30/18	Fri 10/20/23	Tue 10/30/18	NA																		
1047	DOI's Approval Memorandum for an Engineering Evaluation/Cost Analysis (EE/CA)	0 days	Tue 10/30/18	Tue 10/30/18	Tue 10/30/18	Tue 10/30/18																		
1048	PG&E prepares Draft Soil EE/CA	414 days	Wed 10/31/18	Fri 5/29/20	Wed 10/31/18	Fri 5/29/20																		
1049	BLM sends package to Tribes for Consultation	0 days	Wed 6/3/20	Wed 6/3/20	Wed 6/3/20	Wed 6/3/20																		
1050	Tribal Consultation	254.38 edays	Wed 6/3/20	Fri 2/12/21	Wed 6/3/20	Fri 2/12/21																		
1051	Public Review	63.38 edays	Wed 6/3/20	Wed 8/5/20	Wed 6/3/20	Wed 8/5/20																		
1052	DOI responds to comments received on the Draft Soil EE/CA	50 days	Mon 2/15/21	Fri 4/23/21	Mon 2/15/21	Fri 4/23/21																		
1053	DOI prepares Responsiveness Summary	67.38 edays	Mon 2/15/21	Fri 4/23/21	Mon 2/15/21	Fri 4/23/21																		
1054	PG&E finalizes EE/CA	67.38 edays	Mon 2/15/21	Fri 4/23/21	Mon 2/15/21	Fri 4/23/21																		
1055	DOI prepares Action Memorandum	8.14 mons	Mon 2/15/21	Mon 10/11/21	Mon 2/15/21	Mon 10/11/21																		
1056	DOI approved Action Memorandum	0 days	Tue 10/12/21	Tue 10/12/21	Tue 10/12/21	Tue 10/12/21																		
1057	PG&E submits Non-time Critical Removal (NTCRA) Work Plan	1 day	Fri 10/29/21	Fri 10/29/21	Fri 10/29/21	Fri 10/29/21																		
1058	BLM sends NTCRA Work Plan to Tribes	2 edays	Mon 11/1/21	Wed 11/3/21	Mon 11/1/21	Wed 11/3/21																		
1059	Tribal Consultation	48 edays	Wed 11/3/21	Tue 12/21/21	Wed 11/3/21	Tue 12/21/21																		
1060	DTSC and Stakeholders review/comment	57 edays	Mon 11/1/21	Tue 12/28/21	Mon 11/1/21	Tue 12/28/21																		
1061	DOI review/comment	49.38 edays	Mon 11/1/21	Mon 12/20/21	Mon 11/1/21	Mon 12/20/21																		
1062	PG&E compiles comments/prepares RTCs	87.38 edays	Tue 12/28/21	Fri 3/25/22	Tue 12/28/21	Fri 3/25/22																		
1063	Tribes review RTCs	2.6 wks	Fri 3/25/22	Wed 4/13/22	Fri 3/25/22	Wed 4/13/22																		
1064	DTSC and Stakeholders review RTCs	12 days	Fri 3/25/22	Tue 4/12/22	Fri 3/25/22	Tue 4/12/22																		
1065	Meeting to discuss RTCs	1 day	Tue 4/26/22	Tue 4/26/22	Tue 4/26/22	Tue 4/26/22																		
1066	Meeting to discuss RTCs	1 day	Thu 5/5/22	Thu 5/5/22	Thu 5/5/22	Thu 5/5/22																		
1067	PG&E Submits Redline RTCs	1 day	Tue 5/24/22	Tue 5/24/22	Tue 5/24/22	Tue 5/24/22																		
1068	FMIT provide input to RTC Table	1 day	Fri 6/3/22	Fri 6/3/22	Fri 6/3/22	Fri 6/3/22																		
1069	Quechan Tribe concur with FMIT comments	1 day	Mon 6/6/22	Mon 6/6/22	Mon 6/6/22	Mon 6/6/22																		
1070	PG&E addresses comments/finalizes NTCRA Work Plan	38 days	Wed 4/27/22	Fri 6/17/22	Wed 4/27/22	NA																		
1071	DOI reviews/approves NTCRA Work Plan	1 day	Fri 6/17/22	Fri 6/17/22	NA	NA																		
1072	PG&E implements NTCRA Work Plan (duration to be verified after approval of work pl)	135 days	Mon 6/27/22	Fri 12/30/22	NA	NA																		
1073	Stake corners of Target Action Areas	3 days	Mon 6/27/22	Wed 6/29/22	NA	NA																		
1074	Project Initiation Meeting - Online	1 day	Wed 7/6/22	Wed 7/6/22	NA	NA																		

Project: PG&E Topock Remediation Project
 Date: Fri 6/17/22
 Page 2 of 10

Tasks Not Started/In Progress **Overall Task Duration** **Manual Task** **Start-only**

Tasks Finished **Inactive Task** **Duration-only** **Finish-only**

Baseline Schedule **Inactive Milestone** **Manual Summary Rollup**

Milestone **Inactive Summary** **Manual Summary**

edays = calendar days; days = work days
 Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
 *Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
 PG&E Federal Agencies CWG/TWG Public
 DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
 - Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
 - Actual dates may vary depending on field conditions.

HANDOUT 12A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 50)

JUNE 22, 2022 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2021				2022				2023				2024			
							Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	
1075	Project Initiation Meeting - Face-to-Face	1 day	Wed 7/13/22	Wed 7/13/22	NA	NA																
1076	Collect Soil Samples for waste profiling, XRF/Lab Data comparison, and Dioxin Furan lab comparison	2 days	Wed 7/13/22	Thu 7/14/22	NA	NA																
1077	Mobilization	8 days	Wed 7/13/22	Fri 7/22/22	NA	NA																
1078	Soil Removal Activities	115 days	Mon 7/25/22	Fri 12/30/22	NA	NA																
1079	PG&E prepares/submits the NTCRA Completion Report (incorporate results from the Soil Risk Assessment Addendum Report)	9 mons	Mon 1/2/23	Thu 9/21/23	NA	NA																
1080	DOI review/accept report	1 mon	Fri 9/22/23	Fri 10/20/23	NA	NA																
1081	GROUNDWATER CORRECTIVE MEASURES/REMEDIAL ALTERNATIVE DEVELOPMENT	2835 days	Mon 3/29/04	Wed 12/31/14	Mon 3/29/04	Wed 12/31/14																
1229	CORRECTIVE MEASURE STUDY/FEASIBILITY STUDY (CMS/FS) AND RISK ASSESSMENT	5781 days	Mon 12/16/02	Fri 12/27/24	Mon 12/16/02	NA																
1230	CMS Work Plan	1465 days	Mon 12/16/02	Tue 6/24/08	Mon 12/16/02	Tue 6/24/08																
1249	Risk Evaluation - Scoping and CSM	2326 days	Tue 10/31/06	Tue 9/15/15	Tue 10/31/06	Tue 9/15/15																
1333	CMS/FS Report	4278 days	Mon 8/18/08	Fri 12/27/24	Mon 8/18/08	NA																
1334	Groundwater	350 days	Mon 8/18/08	Fri 12/18/09	Mon 8/18/08	Fri 12/18/09																
1393	Soil CMS/FS (duration to be verified after completion of RFI/RI)	564 days	Tue 11/1/22	Fri 12/27/24	NA	NA																
1394	Prepare Draft Soil CMS/FS Report	394 days	Tue 11/1/22	Fri 5/3/24	NA	NA																
1395	Prepare Discussion Draft Soil CMS/FS Report	308 days	Tue 11/1/22	Thu 1/4/24	NA	NA																
1396	PG&E outreach with Tribes	1 mon	Fri 1/5/24	Fri 2/2/24	NA	NA																
1397	PG&E submits Draft Soil CMS/FS	2 wks	Mon 2/5/24	Fri 2/16/24	NA	NA																
1398	DTSC send Draft Soil CMS/FS to CWG/TWG	0 days	Fri 2/16/24	Fri 2/16/24	NA	NA																
1399	BLM sends package to Tribes for Consultation	3 days	Mon 2/19/24	Wed 2/21/24	NA	NA																
1400	DTSC review and comment	74 edays	Mon 2/19/24	Fri 5/3/24	NA	NA																
1401	DOI review and comment	74 edays	Mon 2/19/24	Fri 5/3/24	NA	NA																
1402	CWG/TWG review and comment	60 edays	Mon 2/19/24	Fri 4/19/24	NA	NA																
1403	Tribal Consultation	60 edays	Thu 2/22/24	Mon 4/22/24	NA	NA																
1404	SHPO for information only	1 day	Thu 2/22/24	Thu 2/22/24	NA	NA																
1405	Response to Comments/Prepare Final Soil CMS/FS Report (duration to be verified after receipt of comments)	170 days	Mon 5/6/24	Fri 12/27/24	NA	NA																
1406	Review/compile Comment Table	1 mon	Mon 5/6/24	Mon 6/3/24	NA	NA																
1407	Comment clarification meeting	0 days	Fri 5/10/24	Fri 5/10/24	NA	NA																
1408	Prepare/send RTC Table	2 mons	Tue 6/4/24	Wed 7/31/24	NA	NA																
1409	RTC Meeting	23 days	Wed 7/31/24	Mon 9/2/24	NA	NA																
1410	Send agenda (2 wks prior to meeting)	0 days	Wed 7/31/24	Wed 7/31/24	NA	NA																
1411	Hold Multiple Meetings	13 days	Thu 8/15/24	Mon 9/2/24	NA	NA																
1412	Prepare Final Soil CMS/FS Report	3 mons	Tue 9/3/24	Thu 11/28/24	NA	NA																
1413	DTSC review and concur	1 mon	Fri 11/29/24	Fri 12/27/24	NA	NA																
1414	DOI review and concur	1 mon	Fri 11/29/24	Fri 12/27/24	NA	NA																
1415	CEQA Evaluation (Place Holder Item only. Details including duration will be provided after the prior steps are better defined)	3 mons	Mon 12/30/24	Wed 3/26/25	NA	NA																
1416	STATEMENT OF BASIS	4040 days	Mon 1/4/10	Tue 6/17/25	Mon 1/4/10	NA																
1417	Groundwater	284 days	Mon 1/4/10	Mon 1/31/11	Mon 1/4/10	Mon 1/31/11																
1424	Soil	121 days	Tue 12/31/24	Tue 6/17/25	NA	NA																
1425	Prepare fact sheet for proposed remedy	1 mon	Tue 12/31/24	Tue 1/28/25	NA	NA																
1426	Prepare public notice package/Statement of Basis	2 mons	Mon 1/6/25	Tue 3/4/25	NA	NA																

Project: PG&E Topock Remediation Project
 Date: Fri 6/17/22
 Page 3 of 10

Tasks Not Started/In Progress Overall Task Duration
 Tasks Finished Inactive Task
 Baseline Schedule Inactive Milestone
 Milestone Inactive Summary

Manual Task
 Duration-only
 Manual Summary Rollup
 Manual Summary

Start-only
 Finish-only

edays = calendar days; days = work days
 Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
 *Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
 PG&E Federal Agencies CWG/TWG Public
 DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
 - Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
 - Actual dates may vary depending on field conditions.

HANDOUT 12A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 50) JUNE 22, 2022 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2021				2022				2023				2024					
							Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4			
1826	Well Buildout - AZ (HNWR-1A) including electrical hook-up/I&C/site improvements	67 days	Mon 4/15/24	Tue 7/16/24	NA	NA																		
1827	Pipeline Installation - Arizona	120 days	Mon 10/30/23	Fri 4/12/24	NA	NA																		
1828	System Integration and Functional Testing	121 days	Thu 8/14/25	Thu 1/29/26	NA	NA																		
1829	Start-up Phase 2B Components	0 days	Thu 1/29/26	Thu 1/29/26	NA	NA																		
1830	Start-up Complete/Start Full Remedy Operations	1 day	Thu 1/29/26	Thu 1/29/26	NA	NA																		
1831	Construction Demobization	6 days	Thu 1/29/26	Thu 2/5/26	NA	NA																		
1832	Reporting	1911 days	Mon 11/19/18	Wed 3/11/26	NA	NA																		
1833	Prepare/submit monthly construction progress reports	91 mons	Mon 11/19/18	Wed 3/11/26	NA	NA																		
1834	Start Operation and Maintenance	0 days	Thu 1/29/26	Thu 1/29/26	NA	NA																		

Project: PG&E Topock Remediation Project
Date: Fri 6/17/22

Page 6 of 10

Tasks Not Started/In Progress	Overall Task Duration	Manual Task	Start-only
Tasks Finished	Inactive Task	Duration-only	Finish-only
Baseline Schedule	Inactive Milestone	Manual Summary Rollup	
Milestone	Inactive Summary	Manual Summary	

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
 - Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
 - Actual dates may vary depending on field conditions.

HANDOUT 12A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 50)

JUNE 22, 2022 CWG MEETING

2025			2026				2027				2028				2029				2030				2031				2032				2033	
Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2				

Project: PG&E Topock Remediation Project Date: Fri 6/17/22	Page 7 of 10	Tasks Not Started/In Progress	Overall Task Duration	Manual Task	Start-only
		Tasks Finished	Inactive Task	Duration-only	Finish-only
		Baseline Schedule	Inactive Milestone	Manual Summary Rollup	
		Milestone	Inactive Summary	Manual Summary	

edays = calendar days; days = work days
 Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
 *Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
 - Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
 - Actual dates may vary depending on field conditions.

HANDOUT 12A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 50)

JUNE 22, 2022 CWG MEETING



Project: PG&E Topock Remediation Project Date: Fri 6/17/22	Page 8 of 10	<table border="0"> <tr> <td>Tasks Not Started/In Progress</td> <td></td> <td>Overall Task Duration</td> <td></td> <td>Manual Task</td> <td></td> <td>Start-only</td> <td></td> </tr> <tr> <td>Tasks Finished</td> <td></td> <td>Inactive Task</td> <td></td> <td>Duration-only</td> <td></td> <td>Finish-only</td> <td></td> </tr> <tr> <td>Baseline Schedule</td> <td></td> <td>Inactive Milestone</td> <td></td> <td>Manual Summary Rollup</td> <td></td> <td></td> <td></td> </tr> <tr> <td>Milestone</td> <td></td> <td>Inactive Summary</td> <td></td> <td>Manual Summary</td> <td></td> <td></td> <td></td> </tr> </table>	Tasks Not Started/In Progress		Overall Task Duration		Manual Task		Start-only		Tasks Finished		Inactive Task		Duration-only		Finish-only		Baseline Schedule		Inactive Milestone		Manual Summary Rollup				Milestone		Inactive Summary		Manual Summary			
Tasks Not Started/In Progress		Overall Task Duration		Manual Task		Start-only																												
Tasks Finished		Inactive Task		Duration-only		Finish-only																												
Baseline Schedule		Inactive Milestone		Manual Summary Rollup																														
Milestone		Inactive Summary		Manual Summary																														

edays = calendar days; days = work days
 Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
 *Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
 - Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
 - Actual dates may vary depending on field conditions.

HANDOUT 12A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 50)

JUNE 22, 2022 CWG MEETING



Project: PG&E Topock Remediation Project Date: Fri 6/17/22	Page 9 of 10	Tasks Not Started/In Progress Tasks Finished Baseline Schedule Milestone	Inactive Task Inactive Milestone Inactive Summary	Overall Task Duration Manual Task Manual Summary Rollup Manual Summary	Manual Task Duration-only Manual Summary Rollup Manual Summary	Start-only Finish-only
---	--------------	---	---	---	---	---------------------------

edays = calendar days; days = work days
 Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
 *Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
 - Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
 - Actual dates may vary depending on field conditions.

HANDOUT 12A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 50)

JUNE 22, 2022 CWG MEETING



Project: PG&E Topock Remediation Project
 Date: Fri 6/17/22
 Page 10 of 10

Tasks Not Started/In Progress	Overall Task Duration	Manual Task	Start-only
Tasks Finished	Inactive Task	Duration-only	Finish-only
Baseline Schedule	Inactive Milestone	Manual Summary Rollup	
Milestone	Inactive Summary	Manual Summary	

edays = calendar days; days = work days
 Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
 *Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
 PG&E Federal Agencies CWG/TWG Public
 DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
 - Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
 - Actual dates may vary depending on field conditions.
