



Handout 6A

Topock Remediation Project Schedule


April 2, 2008 (Revision 2)

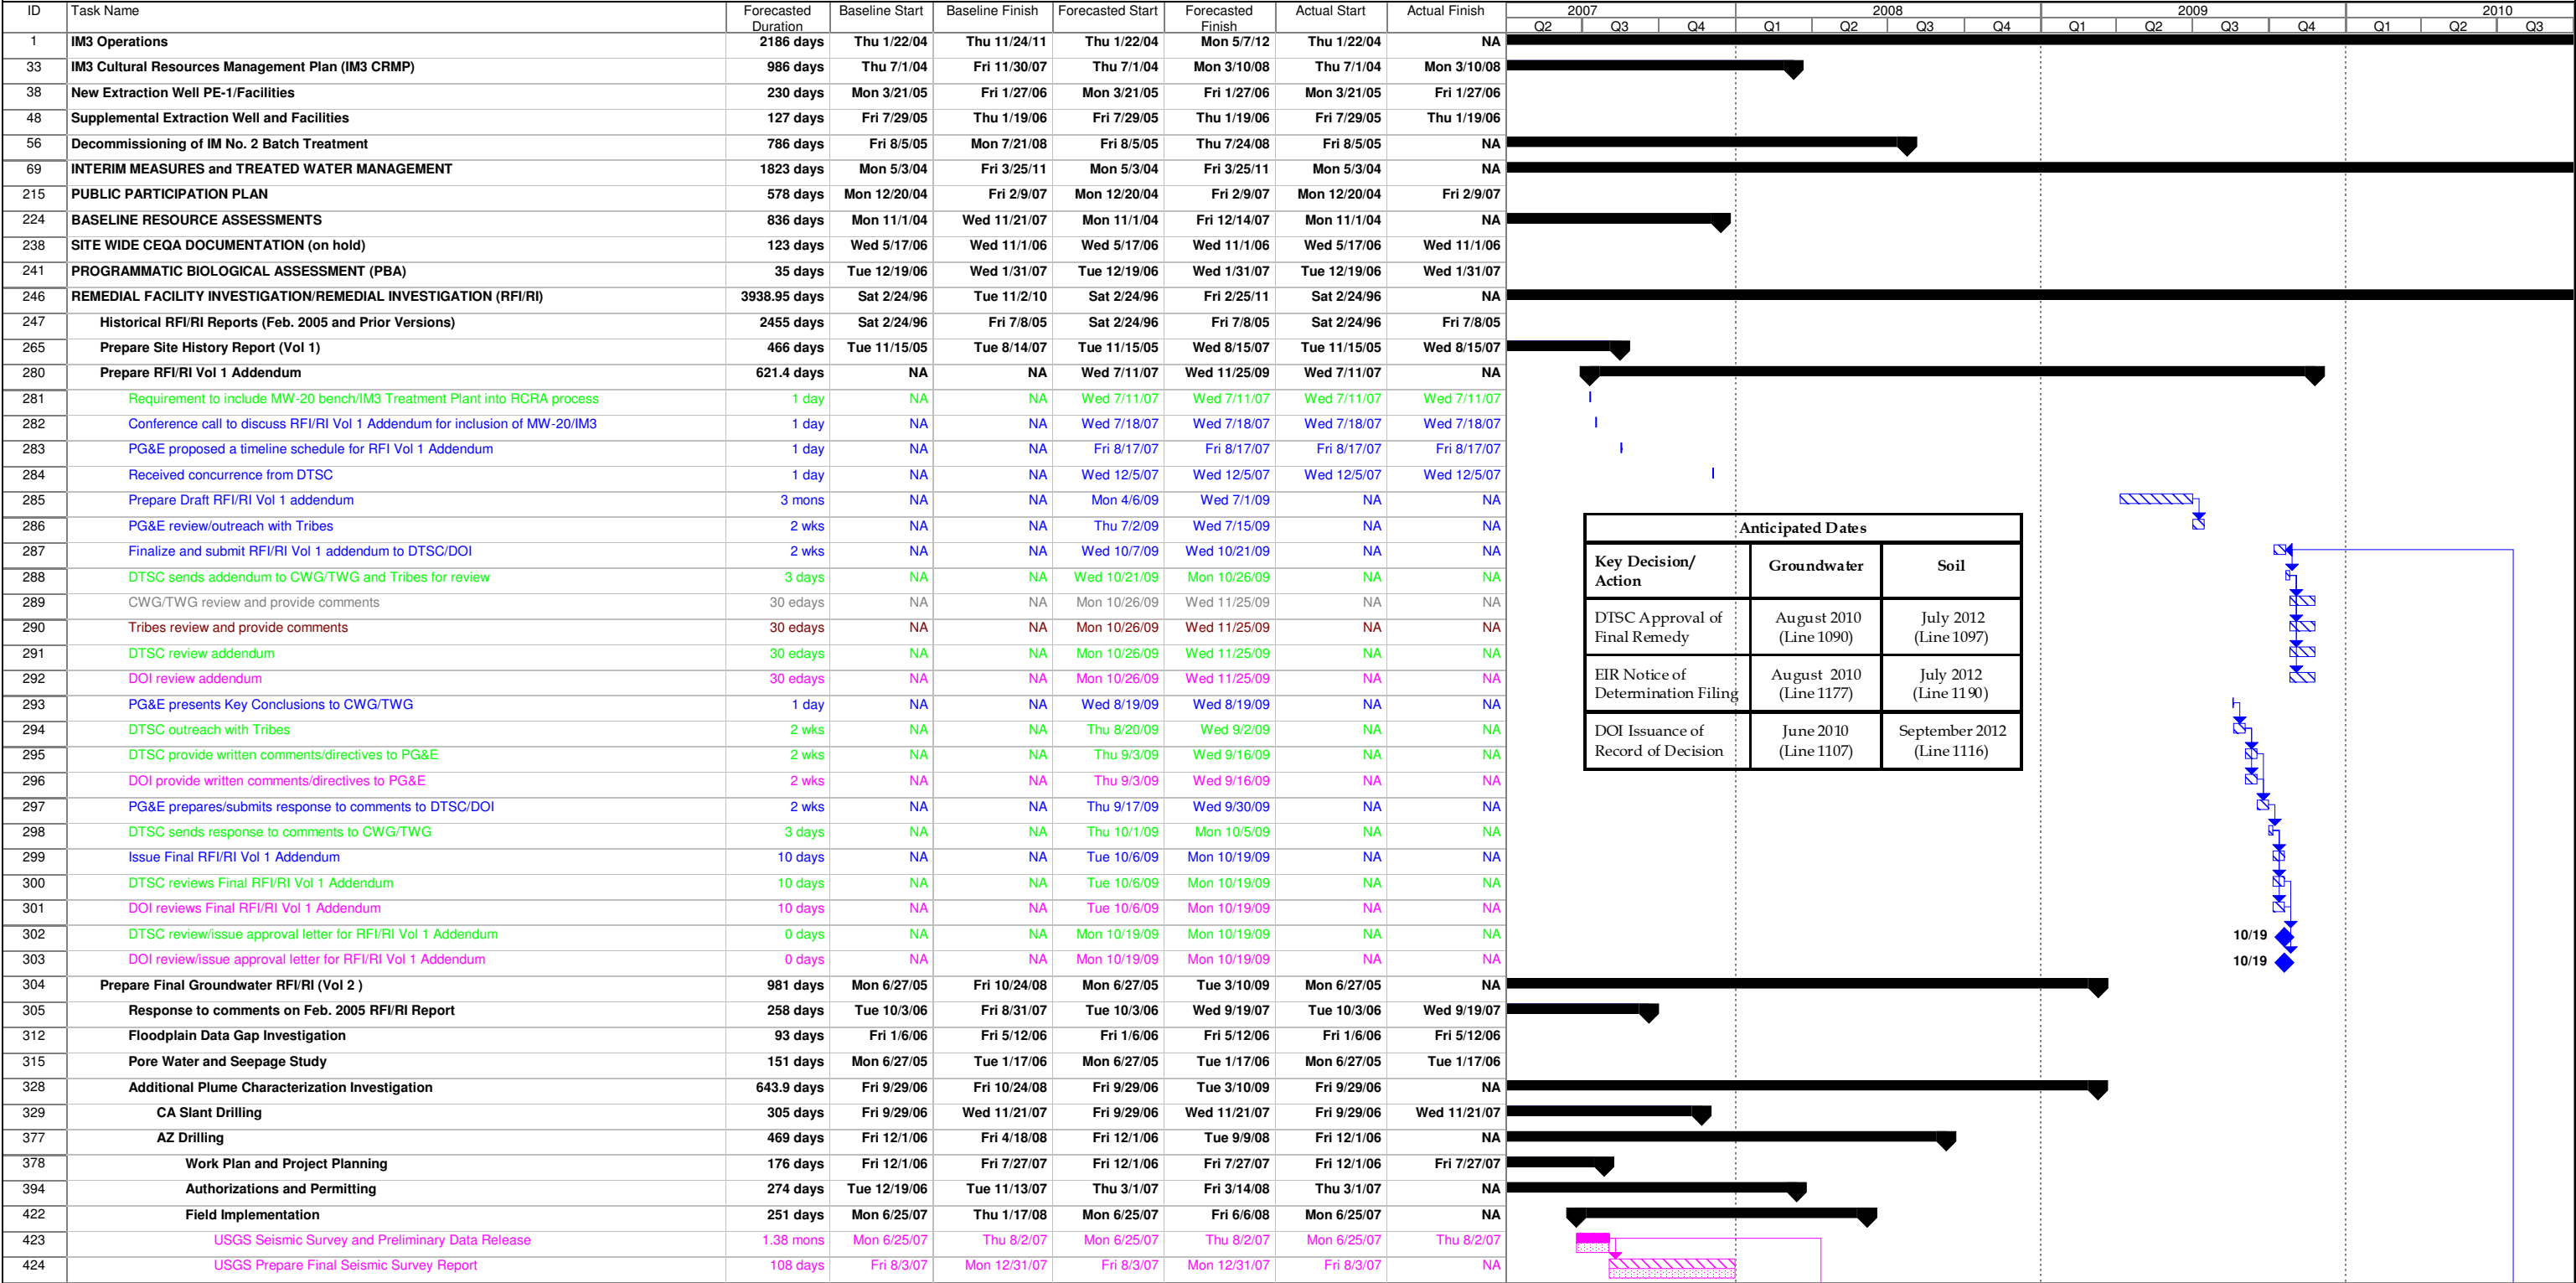

Anticipated Dates		
Key Decision/ Action	Groundwater	Soil
DTSC Approval of Final Remedy	August 2010 (Line 1090)	July 2012 (Line 1097)
EIR Notice of Determination Filing	August 2010 (Line 1177)	July 2012 (Line 1190)
DOI Issuance of Record of Decision	June 2010 (Line 1107)	September 2012 (Line 1116)

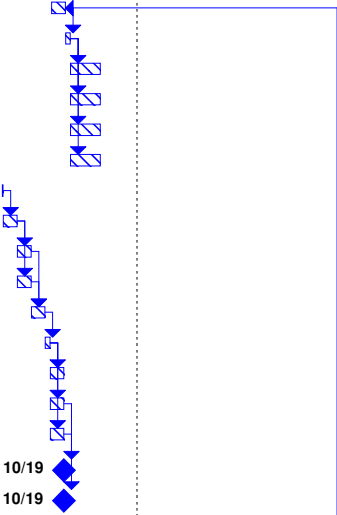

Handout 6A
Topock Remediation Project Schedule
April 2, 2008 (Revision 2)

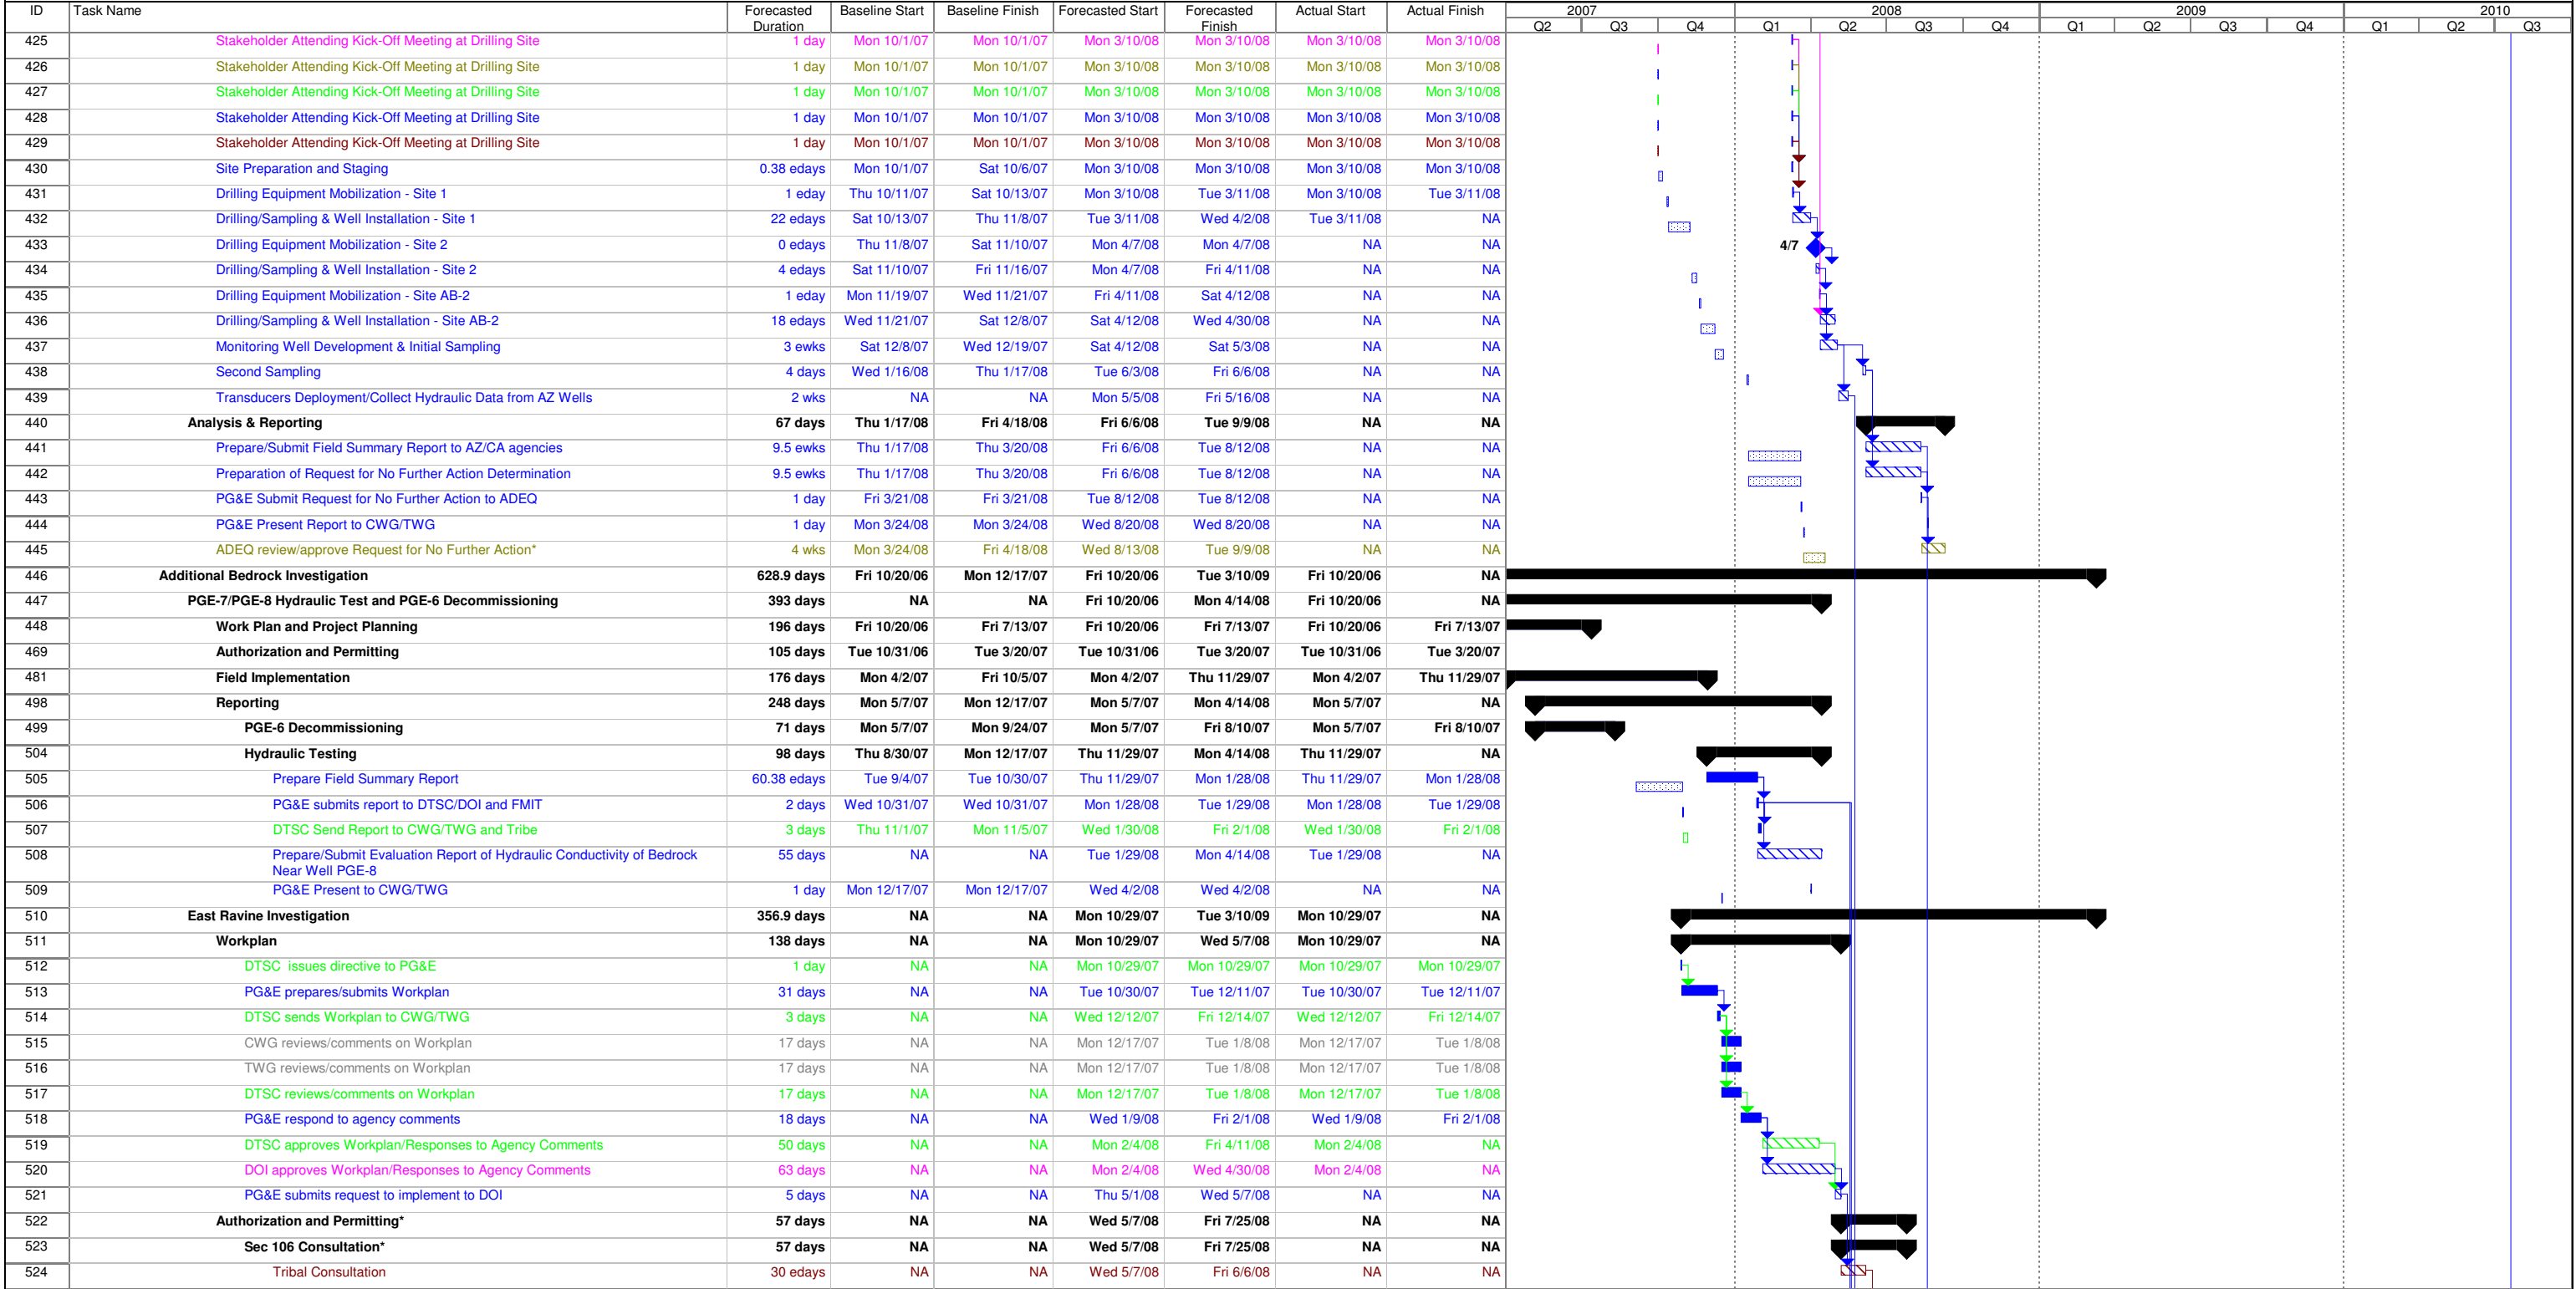


Handout 6A

Topock Remediation Project Schedule

April 2, 2008 (Revision 2)

ID	Task Name	Forecasted Duration	Baseline Start	Baseline Finish	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2007			2008				2009				2010		
									Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
525	BLM Letter to SHPO	3 days	NA	NA	Mon 6/9/08	Wed 6/11/08	NA	NA														
526	SHPO Consultation	30 edays	NA	NA	Wed 6/11/08	Fri 7/11/08	NA	NA														
527	BLM sign off of SHPO concurrence	5 days	NA	NA	Mon 7/14/08	Fri 7/18/08	NA	NA														
528	HNWR Approval Letter	5 days	NA	NA	Mon 7/21/08	Fri 7/25/08	NA	NA														
529	Field Implementation (2 well locations, 2 sampling events)*	82.9 days	NA	NA	Mon 7/28/08	Wed 11/19/08	NA	NA														
530	Stakeholder Attending Kick-Off Meeting at Site	1 day	NA	NA	Mon 7/28/08	Mon 7/28/08	NA	NA														
531	Stakeholder Attending Kick-Off Meeting at Site	1 day	NA	NA	Mon 7/28/08	Mon 7/28/08	NA	NA														
532	Stakeholder Attending Kick-Off Meeting at Site	1 day	NA	NA	Mon 7/28/08	Mon 7/28/08	NA	NA														
533	Stakeholder Attending Kick-Off Meeting at Site	1 day	NA	NA	Mon 7/28/08	Mon 7/28/08	NA	NA														
534	Stakeholder Attending Kick-Off Meeting at Site	1 day	NA	NA	Mon 7/28/08	Mon 7/28/08	NA	NA														
535	Field Implementation (2 wells, 2 sampling events)	3.9 mons	NA	NA	Tue 7/29/08	Wed 11/19/08	NA	NA														
536	Reporting*	79 days	NA	NA	Wed 11/19/08	Tue 3/10/09	NA	NA														
537	PG&E prepare/submit Tech Memo	1 mon	NA	NA	Wed 11/19/08	Thu 12/18/08	NA	NA														
538	DTSC forward TM to CWG/TWG	3 days	NA	NA	Thu 12/18/08	Tue 12/23/08	NA	NA														
539	PG&E presents Key Conclusions to CWG/TWG	1 day	NA	NA	Wed 12/10/08	Wed 12/10/08	NA	NA														
540	DTSC reviews/comments on TM	1 mon	NA	NA	Tue 12/23/08	Wed 1/21/09	NA	NA														
541	DOI reviews/comments on TM	1 mon	NA	NA	Tue 12/23/08	Wed 1/21/09	NA	NA														
542	CWG reviews/comments on TM	1 mon	NA	NA	Tue 12/23/08	Wed 1/21/09	NA	NA														
543	TWG reviews/comments on TM	1 mon	NA	NA	Tue 12/23/08	Wed 1/21/09	NA	NA														
544	PG&E respond to comments/finalizes TM	1 mon	NA	NA	Wed 1/21/09	Thu 2/19/09	NA	NA														
545	DTSC reviews/approves final TM	10 days	NA	NA	Thu 2/19/09	Thu 3/5/09	NA	NA														
546	DOI reviews/approves final TM	10 days	NA	NA	Thu 2/19/09	Thu 3/5/09	NA	NA														
547	PG&E issues final TM	3 days	NA	NA	Thu 3/5/09	Tue 3/10/09	NA	NA														
548	Prepare and Submit Final GW RFI/RI	345.45 days	Wed 8/1/07	Mon 9/1/08	Mon 8/20/07	Fri 12/12/08	Mon 8/20/07	NA														
549	Prepare Draft RFI/RI Vol 2 report	8.9 mons	Wed 8/1/07	Tue 1/29/08	Mon 8/20/07	Mon 5/5/08	Mon 8/20/07	NA														
550	PG&E review/outreach with Tribes	1.5 mons	Tue 1/22/08	Thu 3/6/08	Mon 5/5/08	Wed 6/18/08	NA	NA														
551	Finalize and submit RFI/RI Vol 2 report to DTSC/DOI	2 wks	Thu 3/6/08	Thu 3/20/08	Wed 6/18/08	Wed 7/2/08	NA	NA														
552	DTSC sends report to CWG/TWG and Tribes for review	3 days	Thu 3/20/08	Tue 3/25/08	Wed 7/2/08	Mon 7/7/08	NA	NA														
553	CWG/TWG Review and Provide Comments	2.05 mons	Tue 3/25/08	Fri 5/23/08	Mon 7/7/08	Thu 9/4/08	NA	NA														
554	Tribes Review and Provide Comments	2.05 mons	Tue 3/25/08	Fri 5/23/08	Mon 7/7/08	Thu 9/4/08	NA	NA														
555	PG&E presents Key Report Conclusions to CWG/TWG	1 day	Fri 4/11/08	Tue 4/15/08	Wed 8/20/08	Wed 8/20/08	NA	NA														
556	DTSC outreach with Tribes	2 wks	Fri 4/11/08	Fri 4/25/08	Wed 8/20/08	Tue 9/2/08	NA	NA														
557	DTSC convene to discuss stakeholders' comments	3 wks	Fri 5/23/08	Fri 6/13/08	Thu 9/4/08	Thu 9/25/08	NA	NA														
558	DOI convene to discuss stakeholders' comments	1 wk	Fri 5/23/08	Fri 5/30/08	Thu 9/4/08	Thu 9/11/08	NA	NA														
559	DTSC provide written comments/directives to PG&E	1 mon	Fri 5/23/08	Mon 6/23/08	Thu 9/4/08	Fri 10/3/08	NA	NA														
560	DOI provide written comments/directives to PG&E	2 wks	Fri 5/30/08	Fri 6/13/08	Thu 9/11/08	Thu 9/25/08	NA	NA														
561	PG&E prepares/submits response to comments to DTSC/DOI	3 wks	Mon 6/23/08	Mon 7/14/08	Fri 10/3/08	Fri 10/24/08	NA	NA														
562	DTSC review response to comments	4 wks	Mon 7/14/08	Mon 8/11/08	Fri 10/24/08	Fri 11/21/08	NA	NA														
563	DOI review response to comments	4 wks	Mon 7/14/08	Mon 8/11/08	Fri 10/24/08	Fri 11/21/08	NA	NA														
564	DTSC issues response to comments to CWG	4 wks	Mon 7/14/08	Mon 8/11/08	Fri 10/24/08	Fri 11/21/08	NA	NA														
565	Issue Final RFI/RI Vol 2 Report	10 days	Mon 8/11/08	Mon 8/25/08	Fri 11/21/08	Fri 12/5/08	NA	NA														
566	DTSC reviews Final RFI/RI Vol 2 Report	5 days	Mon 8/25/08	Mon 9/1/08	Fri 12/5/08	Fri 12/12/08	NA	NA														
567	DOI reviews Final RFI/RI Vol 2 Report	5 days	Mon 8/25/08	Mon 9/1/08	Fri 12/5/08	Fri 12/12/08	NA	NA														
568	DTSC issues approval letter for the RFI/RI Vol 2 Report	0 days	Mon 9/1/08	Mon 9/1/08	Fri 12/12/08	Fri 12/12/08	NA	NA														
569	DOI issues approval letter for the RFI/RI Vol 2 Report	0 days	Mon 9/1/08	Mon 9/1/08	Fri 12/12/08	Fri 12/12/08	NA	NA														
570	Prepare and Submit GW RFI/RI Addendum	151 days	Fri 3/21/08	Fri 10/24/08	Tue 8/12/08	Tue 3/10/09	NA	NA														
571	Prepare Draft RFI/RI Vol 2 addendum	3 mons	Fri 3/21/08	Tue 6/17/08	Tue 8/12/08	Thu 11/6/08	NA	NA														
572	PG&E review/outreach with Tribes	2 wks	Wed 6/18/08	Tue 7/1/08	Fri 11/7/08	Thu 11/20/08	NA	NA														
573	Finalize and submit RFI/RI Vol 2 addendum to DTSC/DOI	2 wks	Wed 7/2/08	Tue 7/15/08	Fri 11/21/08	Thu 12/4/08	NA	NA														

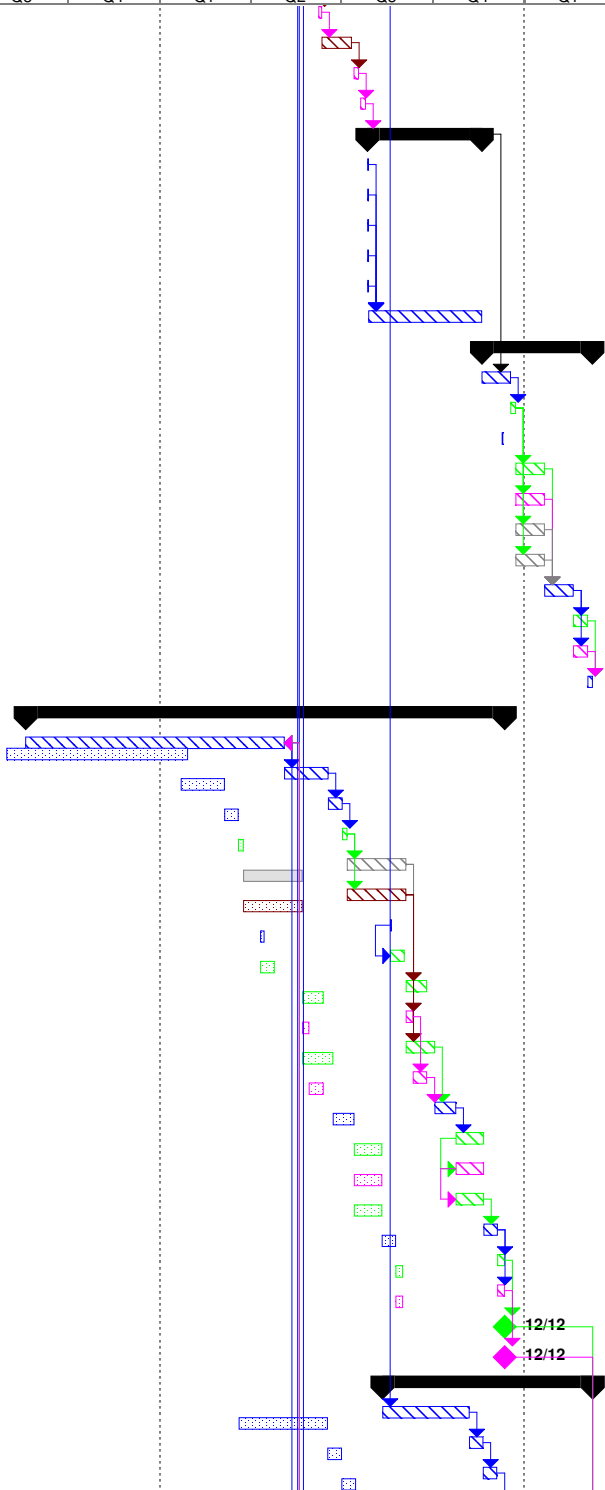

Project: PG&E Topock Remediation Project
Date: Mon 3/31/08

Page 3 of 14

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

Handout 6A

Topock Remediation Project Schedule

April 2, 2008 (Revision 2)

ID	Task Name	Forecasted Duration	Baseline Start	Baseline Finish	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2007			2008				2009				2010		
									Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
574	DTSC sends addendum to CWG/TWG and Tribes for review	3 days	Wed 7/16/08	Fri 7/18/08	Fri 12/5/08	Tue 12/9/08	NA	NA														
575	CWG/TWG review and provide comments	30 edays	Fri 7/18/08	Sun 8/17/08	Tue 12/9/08	Thu 1/8/09	NA	NA														
576	Tribes review and provide comments	30 edays	Fri 7/18/08	Sun 8/17/08	Tue 12/9/08	Thu 1/8/09	NA	NA														
577	DTSC review addendum	30 edays	Fri 7/18/08	Sun 8/17/08	Tue 12/9/08	Thu 1/8/09	NA	NA														
578	DOI review addendum	30 edays	Fri 7/18/08	Sun 8/17/08	Tue 12/9/08	Thu 1/8/09	NA	NA														
579	PG&E presents Key Conclusions to CWG/TWG	1 day	Wed 8/13/08	Thu 8/14/08	Wed 11/19/08	Wed 11/19/08	NA	NA														
580	DTSC outreach with Tribes	2 wks	Wed 8/13/08	Tue 8/26/08	Mon 12/15/08	Fri 12/26/08	NA	NA														
581	DTSC provide written comments/directives to PG&E	2 wks	Wed 8/27/08	Tue 9/9/08	Fri 1/9/09	Thu 1/22/09	NA	NA														
582	DOI provide written comments/directives to PG&E	2 wks	Wed 8/27/08	Tue 9/9/08	Fri 1/9/09	Thu 1/22/09	NA	NA														
583	PG&E prepares/submits response to comments to DTSC/DOI	2 wks	Wed 9/10/08	Tue 9/23/08	Fri 1/23/09	Thu 2/5/09	NA	NA														
584	DTSC sends response to comments to CWG/TWG	3 days	Wed 9/24/08	Fri 9/26/08	Fri 2/6/09	Tue 2/10/09	NA	NA														
585	Issue Final RFI/RI Vol 2 Addendum	10 days	Mon 9/29/08	Fri 10/10/08	Wed 2/11/09	Tue 2/24/09	NA	NA														
586	DTSC reviews Final RFI/RI Vol 2 Addendum	10 days	Mon 10/13/08	Fri 10/24/08	Wed 2/25/09	Tue 3/10/09	NA	NA														
587	DOI reviews Final RFI/RI Vol 2 Addendum	10 days	Mon 10/13/08	Fri 10/24/08	Wed 2/25/09	Tue 3/10/09	NA	NA														
588	DTSC review/issue approval letter for RFI/RI Vol 2 Addendum	0 days	Fri 10/24/08	Fri 10/24/08	Tue 3/10/09	Tue 3/10/09	NA	NA														
589	DOI review/issue approval letter for RFI/RI Vol 2 Addendum	0 days	Fri 10/24/08	Fri 10/24/08	Tue 3/10/09	Tue 3/10/09	NA	NA														
590	Prepare Final Soil RFI/RI (Vol 3)	1211.95 days	Sat 7/15/06	Tue 11/2/10	Sat 7/15/06	Fri 2/25/11	Sat 7/15/06	NA														
591	Implementation of Off-site Soil Sampling (Part A)	988.4 days	Sat 7/15/06	Wed 12/23/09	Sat 7/15/06	Tue 4/20/10	Sat 7/15/06	NA														
592	Part A Phase I	623 days	Sat 7/15/06	Thu 7/31/08	Sat 7/15/06	Mon 11/24/08	Sat 7/15/06	NA														
593	Workplan	311.5 days	NA	NA	Sat 7/15/06	Fri 9/14/07	Sat 7/15/06	Fri 9/14/07														
619	Approval Process for Part A Phase I Investigation	170.5 days	Tue 8/28/07	Mon 12/10/07	Fri 9/14/07	Fri 5/9/08	Fri 9/14/07	NA														
620	Tribal Consultation*	72.38 edays	Tue 8/28/07	Sat 10/27/07	Wed 10/3/07	Fri 12/14/07	Wed 10/3/07	Fri 12/14/07														
621	SHPO Review	77.38 edays	Sat 10/27/07	Mon 11/26/07	Fri 1/11/08	Fri 3/28/08	Fri 1/11/08	NA														
622	PBA Compliance Review	29.5 days	Wed 8/29/07	Mon 9/17/07	Fri 9/14/07	Thu 10/25/07	Fri 9/14/07	Thu 10/25/07														
623	DOI Approval	10 days	Tue 11/27/07	Mon 12/10/07	Mon 3/31/08	Fri 4/11/08	NA	NA														
624	Caltrans Encroachment Permit	159 days	Tue 8/28/07	Sat 12/1/07	Thu 9/27/07	Tue 5/6/08	Thu 9/27/07	NA														
625	Prepare/submit application to Caltrans	38 days	NA	NA	Thu 9/27/07	Mon 11/19/07	Thu 9/27/07	Mon 11/19/07														
626	Caltrans review/issue permit (expires 6/30/08)	58 edays	NA	NA	Tue 11/20/07	Thu 1/17/08	Tue 11/20/07	Thu 1/17/08														
627	Prepare permit renewal application (original permit expires 6/30/08)	6 days	NA	NA	Tue 4/15/08	Tue 4/22/08	NA	NA														
628	Caltrans review/issue new permit	10 days	NA	NA	Wed 4/23/08	Tue 5/6/08	NA	NA														
629	Arizona DOT Encroachment Permit	29 days	NA	NA	Fri 2/15/08	Wed 3/26/08	Fri 2/15/08	Wed 3/26/08														
630	Prepare/submit application to ADOT	20 days	NA	NA	Fri 2/15/08	Thu 3/13/08	Fri 2/15/08	Thu 3/13/08														
631	ADOT review/issue permit	9 days	NA	NA	Fri 3/14/08	Wed 3/26/08	Fri 3/14/08	Wed 3/26/08														
632	BNSF Environmental Access Permit	142 days	NA	NA	Thu 9/27/07	Fri 4/11/08	Thu 9/27/07	NA														
633	Prepare/submit application to BNSF	38 days	NA	NA	Thu 9/27/07	Mon 11/19/07	Thu 9/27/07	NA														
634	BNSF review/issue permit*	143.38 edays	NA	NA	Tue 11/20/07	Fri 4/11/08	Tue 11/20/07	NA														
635	BNSF Culvert Crossing Authorization (AOC-1/AOC-14)	142 days	NA	NA	Thu 9/27/07	Fri 4/11/08	Thu 9/27/07	NA														
636	Prepare/submit application to BNSF	38 days	NA	NA	Thu 9/27/07	Mon 11/19/07	Thu 9/27/07	Mon 11/19/07														
637	BNSF review/issue permit*	143.38 edays	NA	NA	Tue 11/20/07	Fri 4/11/08	Tue 11/20/07	NA														
638	BNSF Grade Crossing Authorization (for equipment)	133 days	NA	NA	Thu 9/27/07	Mon 3/31/08	Thu 9/27/07	NA														
639	Prepare/submit application to BNSF	38 days	NA	NA	Thu 9/27/07	Mon 11/19/07	Thu 9/27/07	Mon 11/19/07														
640	BNSF review the grade crossing application	125.38 edays	NA	NA	Tue 11/20/07	Mon 3/24/08	Tue 11/20/07	NA														
641	PG&E rescinds grade crossing application due to encroachment permit obtained from Caltrans to allow equipment access from I-40	5 days	NA	NA	Tue 3/25/08	Mon 3/31/08	NA	NA														
642	USACE 404 Permit/CERCLA Exemption	30 days	NA	NA	Thu 12/20/07	Wed 1/30/08	Thu 12/20/07	Wed 1/30/08														
644	Colorado River Basin RWQCB Section 401 permit	30 days	NA	NA	Thu 12/20/07	Wed 1/30/08	Thu 12/20/07	Wed 1/30/08														
646	San Bernardino County Grading Permit - not required due to CERCLA exemption	48 days	NA	NA	Wed 12/12/07	Fri 2/15/08	Wed 12/12/07	Fri 2/15/08														
649	San Bernardino County Well/Boring Permit - not required due to CERCLA exemption	12 days	NA	NA	Fri 2/15/08	Mon 3/3/08	Fri 2/15/08	Mon 3/3/08														
650	CDFG Notification/Process	10 days	NA	NA	Mon 4/28/08	Fri 5/9/08	NA	NA														
651	Part A Phase I Field Implementation/Data Reporting	377 days	Thu 1/10/08	Thu 7/31/08	Mon 6/18/07	Mon 11/24/08	Mon 6/18/07	NA														

Project: PG&E Topock Remediation Project
Date: Mon 3/31/08

Page 4 of 14


Tasks Not Started/In Progress



Tasks Finished



Baseline Schedule



Milestone



Overall Task Duration



edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

April 2, 2008 (Revision 2)

ID	Task Name		Forecasted Duration	Baseline Start	Baseline Finish	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2007				2008				2009				2010		
										Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
652	Implement Phase I off-site soil investigation*		61 days	Thu 1/10/08	Wed 3/19/08	Mon 5/12/08	Mon 8/4/08	NA	NA															
653	Stakeholder Attending Kick-Off Meeting at Site		1 day	NA	NA	Mon 5/12/08	Mon 5/12/08	NA	NA															
654	Stakeholder Attending Kick-Off Meeting at Site		1 day	NA	NA	Mon 5/12/08	Mon 5/12/08	NA	NA															
655	Stakeholder Attending Kick-Off Meeting at Site		1 day	NA	NA	Mon 5/12/08	Mon 5/12/08	NA	NA															
656	Stakeholder Attending Kick-Off Meeting at Site		1 day	NA	NA	Mon 5/12/08	Mon 5/12/08	NA	NA															
657	Stakeholder Attending Kick-Off Meeting at Site		1 day	NA	NA	Mon 5/12/08	Mon 5/12/08	NA	NA															
658	Field Implementation		9.8 wks	NA	NA	Tue 5/13/08	Fri 7/18/08	NA	NA															
659	Data Validation/Data Management		45 days	NA	NA	Tue 6/3/08	Mon 8/4/08	NA	NA															
660	Supplemental Soil Analysis		36 days	NA	NA	Mon 6/16/08	Mon 8/4/08	NA	NA															
661	2006 Soil and Sediment Data Usability Assessment Tech Memo		253 days	NA	NA	Mon 6/18/07	Tue 6/3/08	Mon 6/18/07	NA															
662	Resubmit 2006 Soil and Sediment Data Usability Assessment TM		1 day	Mon 6/18/07	Mon 6/18/07	Mon 6/18/07	Mon 6/18/07	Mon 6/18/07	Mon 6/18/07															
663	DTSC review/comment on Data Usability Assessment Tech Memo		54 days	Tue 6/19/07	Fri 8/31/07	Tue 6/19/07	Fri 8/31/07	Tue 6/19/07	Fri 8/31/07															
664	DOI review/comment on Data Usability Assessment Tech Memo		54 days	Tue 6/19/07	Fri 8/31/07	Tue 6/19/07	Fri 8/31/07	Tue 6/19/07	Fri 8/31/07															
665	PG&E submits response to comments		50 days	NA	NA	Fri 8/31/07	Wed 11/7/07	Fri 8/31/07	Wed 11/7/07															
666	DTSC reviews/provides joint agency direction to finalize TM		108 days	NA	NA	Wed 11/7/07	Fri 4/4/08	Wed 11/7/07	NA															
667	DOI reviews/provides joint agency direction to finalize TM		108 days	NA	NA	Wed 11/7/07	Fri 4/4/08	Wed 11/7/07	NA															
668	PG&E finalizes/submits Final TM		1 mon	NA	NA	Mon 4/7/08	Mon 5/5/08	NA	NA															
669	DTSC reviews/approves Final TM		1 mon	NA	NA	Tue 5/6/08	Tue 6/3/08	NA	NA															
670	DOI reviews/approves Final TM		1 mon	NA	NA	Tue 5/6/08	Tue 6/3/08	NA	NA															
671	PG&E issues Final TM		0 days	NA	NA	Tue 6/3/08	Tue 6/3/08	NA	NA															
672	Groundwater Screening Level Approach Tech Memo		42 days	NA	NA	Tue 4/1/08	Wed 5/28/08	NA	NA															
673	Prepare/Submit GSL Tech Memo		42 days	NA	NA	Tue 4/1/08	Wed 5/28/08	NA	NA															
674	Ecological Comparison Values Tech Memos		208 days	NA	NA	Thu 2/7/08	Mon 11/24/08	Thu 2/7/08	NA															
675	TM No. 3 - Ecological Comparison Values for Inorganics/PAHs		80 days	NA	NA	Thu 2/7/08	Wed 5/28/08	Thu 2/7/08	NA															
676	Prepare/Submit Tech Memo		80 days	NA	NA	Thu 2/7/08	Wed 5/28/08	Thu 2/7/08	NA															
677	TM No. 4 - Additional Ecological Comparison Values		71 days	NA	NA	Mon 8/18/08	Mon 11/24/08	NA	NA															
678	Prepare/Submit Tech Memo		71 days	NA	NA	Mon 8/18/08	Mon 11/24/08	NA	NA															
679	Soil Background Data Tech Memo		24 days	NA	NA	Wed 6/4/08	Mon 7/7/08	NA	NA															
680	Calculation of Soil Background Data/Prep Tech Memo		24 days	NA	NA	Wed 6/4/08	Mon 7/7/08	NA	NA															
681	Part A Phase 1 Results Tech Memo		79.5 days	NA	NA	Mon 8/4/08	Mon 11/24/08	NA	NA															
682	Prepare/submit Part A Phase 1 TM		60 edays	Thu 3/20/08	Wed 6/11/08	Mon 8/4/08	Fri 10/3/08	NA	NA															
683	DTSC forward to CWG/TWG/Tribes		3 days	Thu 6/12/08	Mon 6/16/08	Mon 10/6/08	Wed 10/8/08	NA	NA															
684	PG&E presents to TWG/CWG		2 days	Wed 6/18/08	Thu 6/19/08	Wed 8/20/08	Thu 8/21/08	NA	NA															
685	DTSC review and comment on TM		1.5 mons	Tue 6/17/08	Wed 7/30/08	Thu 10/9/08	Fri 11/21/08	NA	NA															
686	DOI review and comments on TM		1.5 mons	Tue 6/17/08	Wed 7/30/08	Thu 10/9/08	Fri 11/21/08	NA	NA															
687	FMIT/CRIT/Hualapai/Chemuevi/Tribes review and comment on TM		1.5 mons	Tue 6/17/08	Wed 7/30/08	Thu 10/9/08	Fri 11/21/08	NA	NA															
688	Agency/Tribes/PG&E meet to discuss comments		1 day	Wed 7/30/08	Thu 7/31/08	Fri 11/21/08	Mon 11/24/08	NA	NA															
689	Part A Phase II		365.4 days	Thu 7/31/08	Wed 12/23/09	Tue 11/25/08	Tue 4/20/10	NA	NA															
690	Prepare Part A Phase II Work Plan (incl. staking of locations)		3 mons	Thu 7/31/08	Tue 10/28/08	Tue 11/25/08	Thu 2/19/09	NA	NA															
691	DTSC send Part A Phase II Workplan to CWG/TWG		3 days	Tue 10/28/08	Fri 10/31/08	Fri 2/20/09	Tue 2/24/09	NA	NA															
692	CWG/TWG review and comment		30 edays	Fri 10/31/08	Sun 11/30/08	Tue 2/24/09	Thu 3/26/09	NA	NA															
693	DTSC review and comment		30 edays	Fri 10/31/08	Sun 11/30/08	Tue 2/24/09	Thu 3/26/09	NA	NA															
694	DOI review and comment		30 edays	Fri 10/31/08	Sun 11/30/08	Tue 2/24/09	Thu 3/26/09	NA	NA															
695	PG&E respond to comments		10 days	Mon 12/1/08	Fri 12/12/08	Fri 3/27/09	Thu 4/9/09	NA	NA															
696	DTSC review response to comments		30 edays	Fri 12/12/08	Sun 1/11/09	Thu 4/9/09	Sat 5/9/09	NA	NA															
697	DOI review response to comments		30 edays	Fri 12/12/08	Sun 1/11/09	Thu 4/9/09	Sat 5/9/09	NA	NA															
698	DTSC send Part A Phase II approval letter to PG&E		0 days	Mon 1/12/09	Mon 1/12/09	Mon 5/11/09	Mon 5/11/09	NA	NA															
699	Prepare/submit a Request for Approval to Implement Phase II Investigation		10 days	Tue 1/13/09	Mon 1/26/09	Tue 5/12/09	Mon 5/25/09	NA	NA															
700	Approval Process for Phase II Investigation		81 days	Mon 1/26/09	Tue 5/19/09	Mon 5/25/09	Tue 9/15/09	NA	NA															


Major Assumptions

- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

Handout 6A

Topock Remediation Project Schedule

April 2, 2008 (Revision 2)

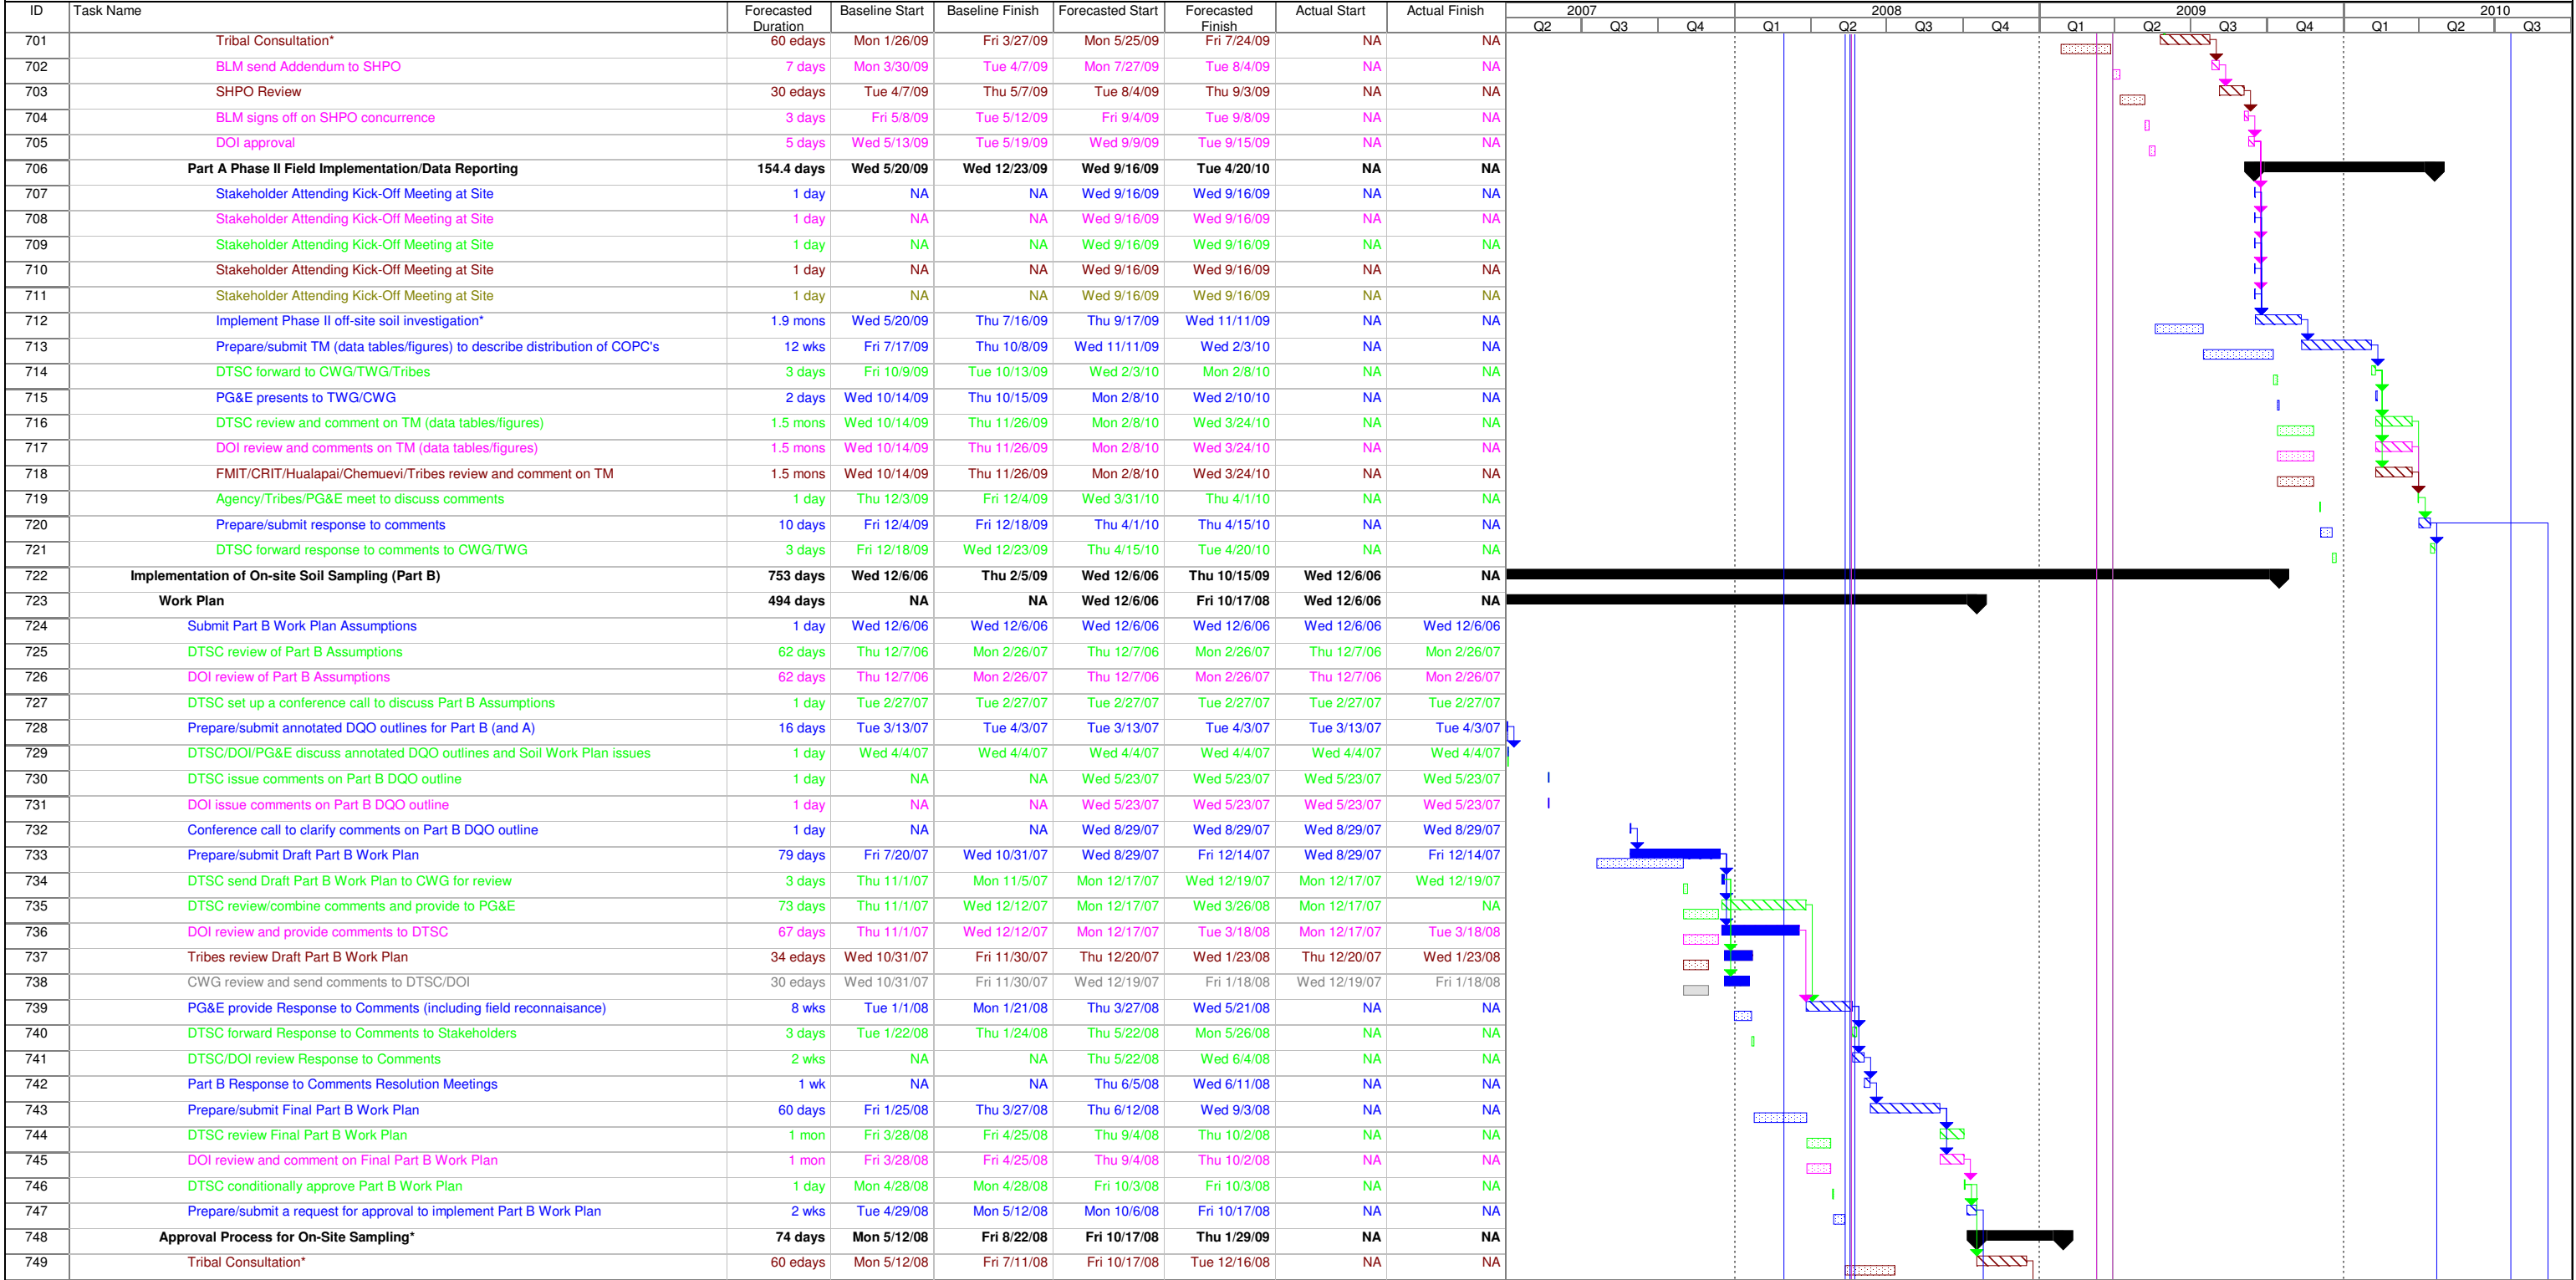

Project: PG&E Topock Remediation Project
Date: Mon 3/31/08

Page 6 of 14

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.


Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.


Handout 6A

Topock Remediation Project Schedule

April 2, 2008 (Revision 2)

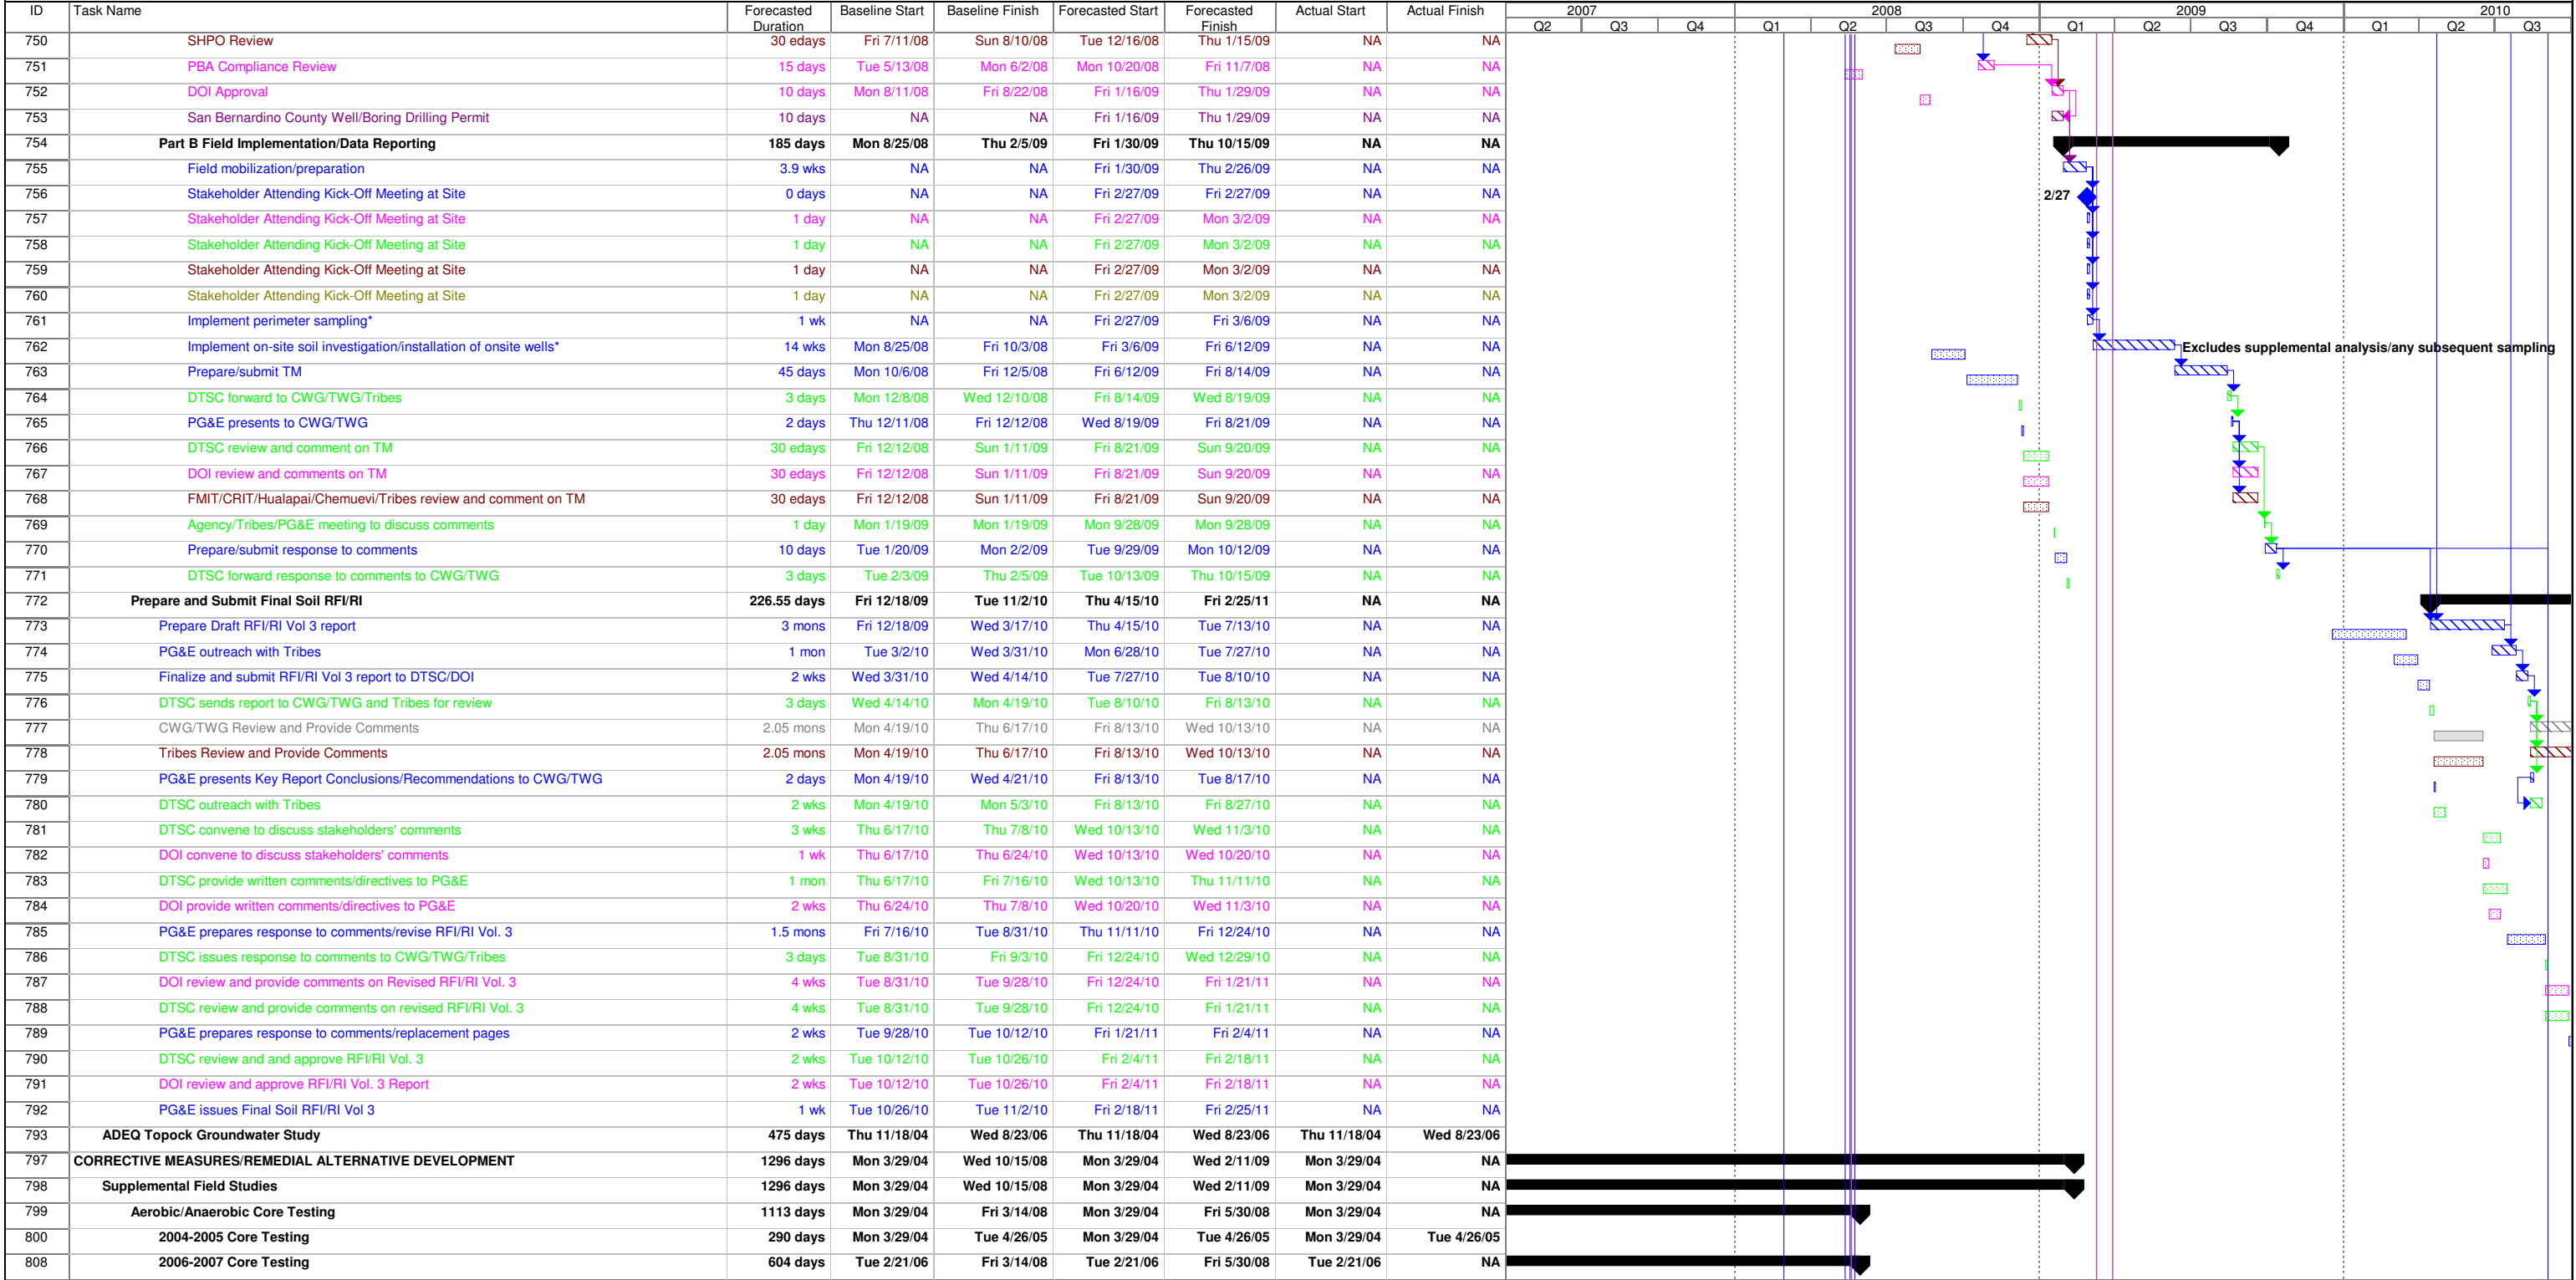

Handout 6A
Topock Remediation Project Schedule
April 2, 2008 (Revision 2)

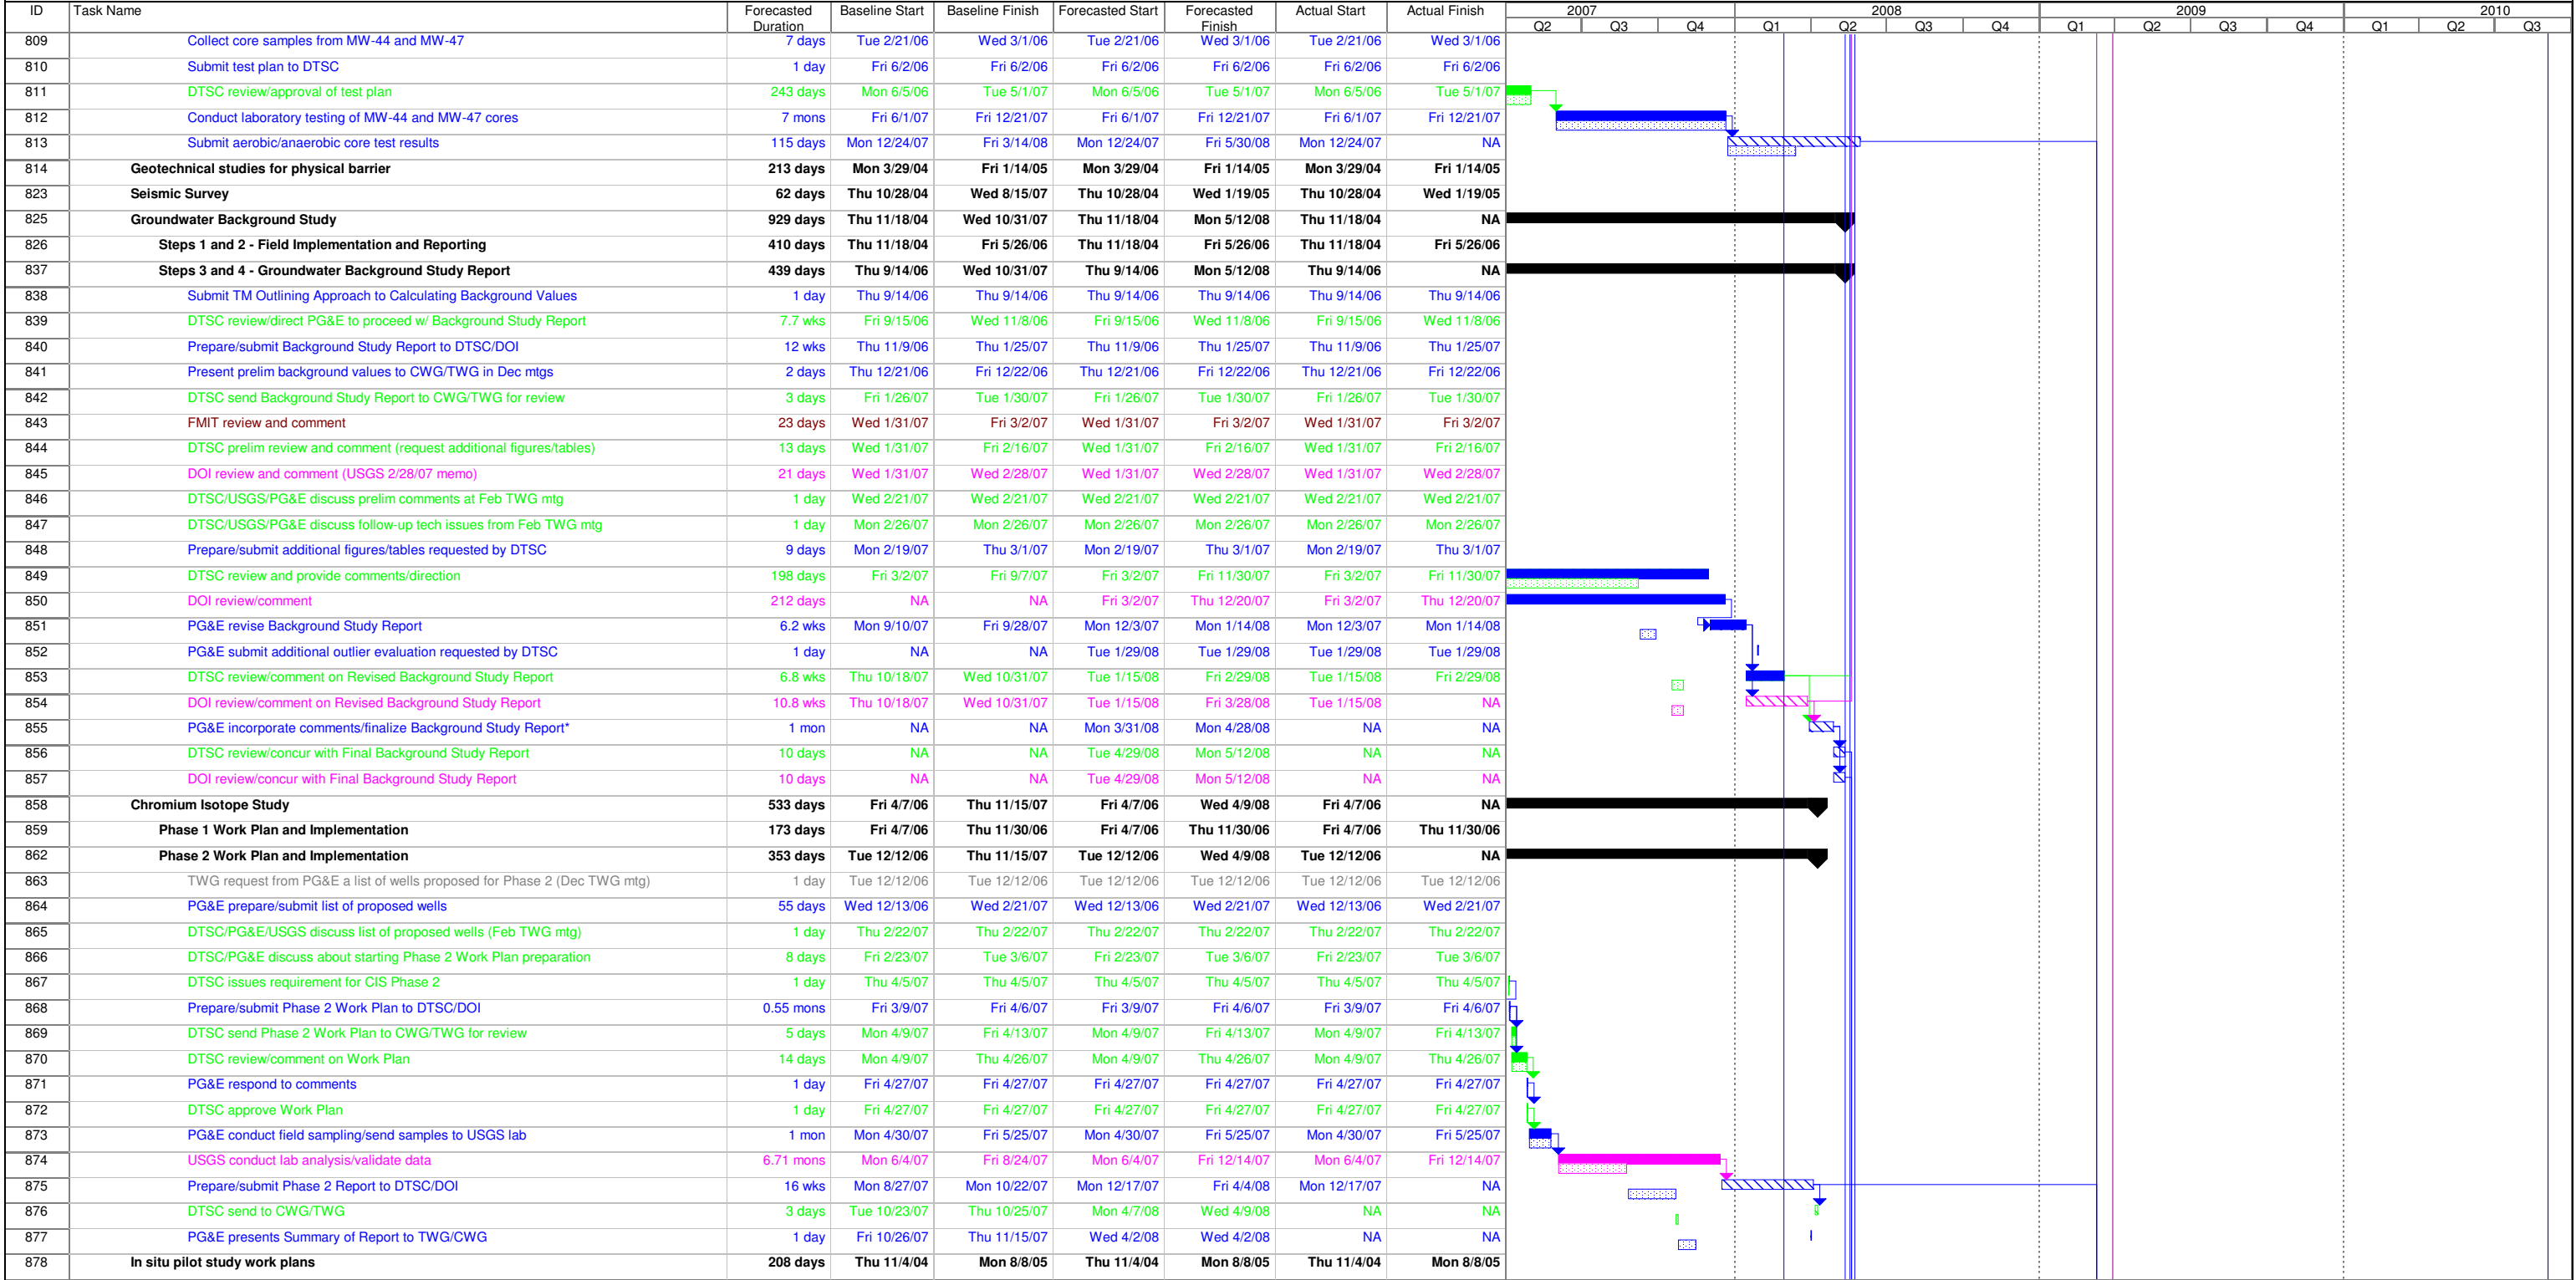

Project: PG&E Topock Remediation Project
Date: Mon 3/31/08

Page 8 of 14

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone


Overall Task Duration

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

Handout 6A
Topock Remediation Project Schedule
April 2, 2008 (Revision 2)

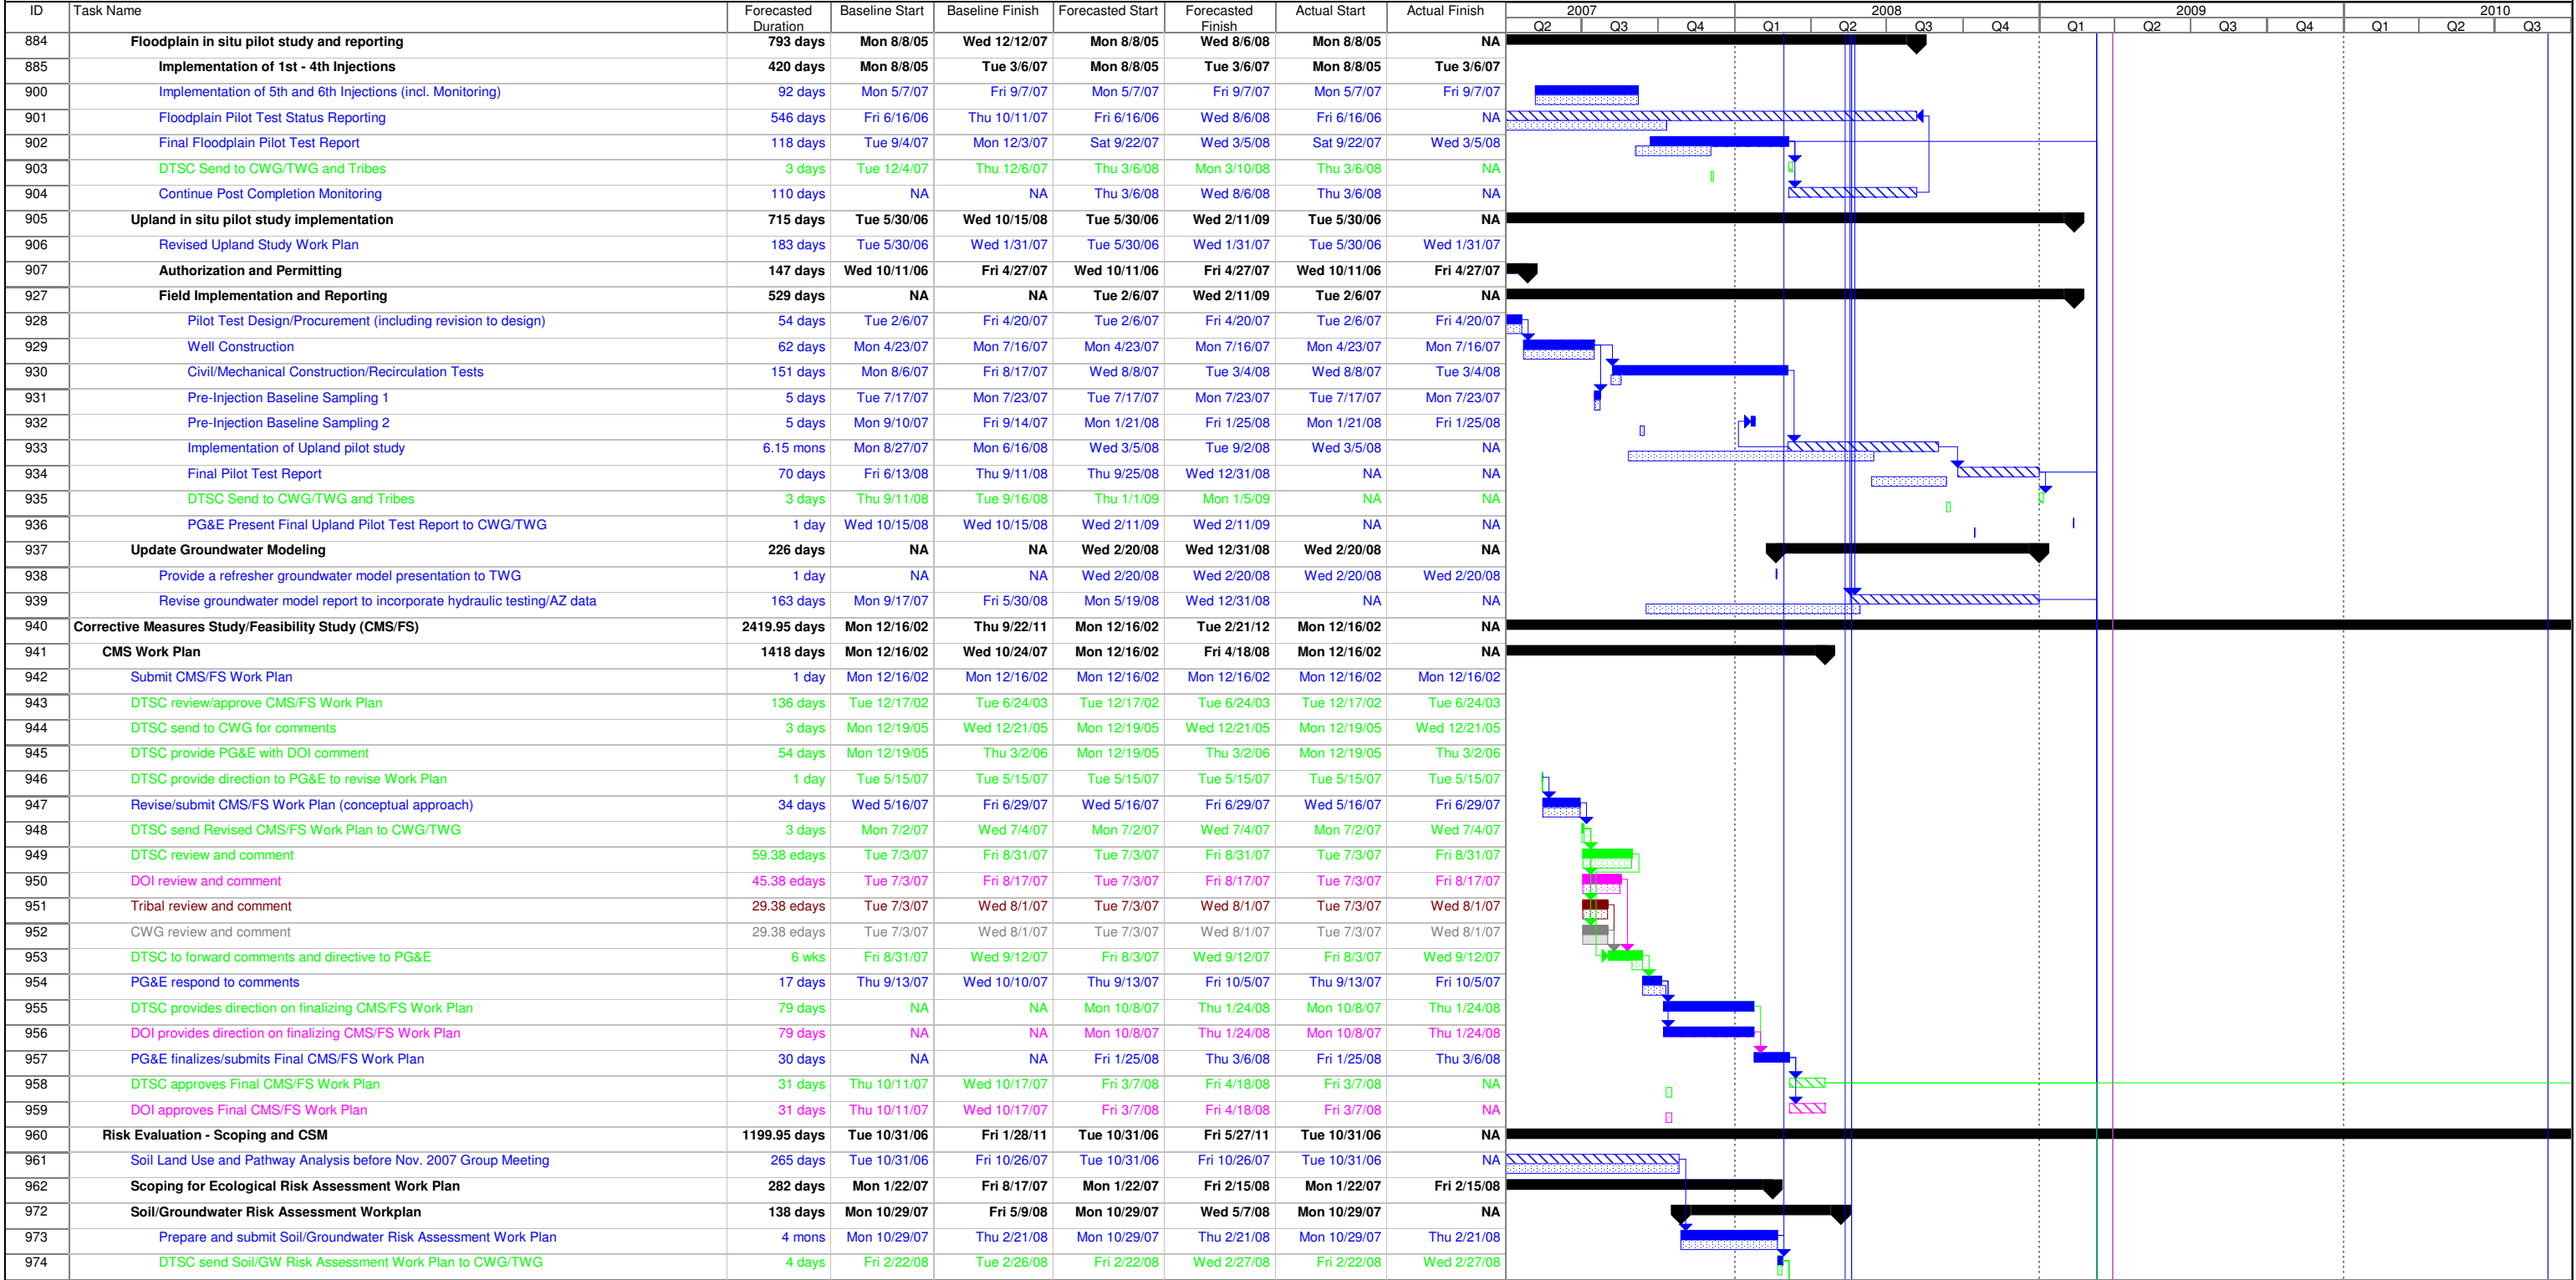

Project: PG&E Topock Remediation Project
Date: Mon 3/31/08

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone


Overall Task Duration

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.


Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

Handout 6A
Topock Remediation Project Schedule
April 2, 2008 (Revision 2)

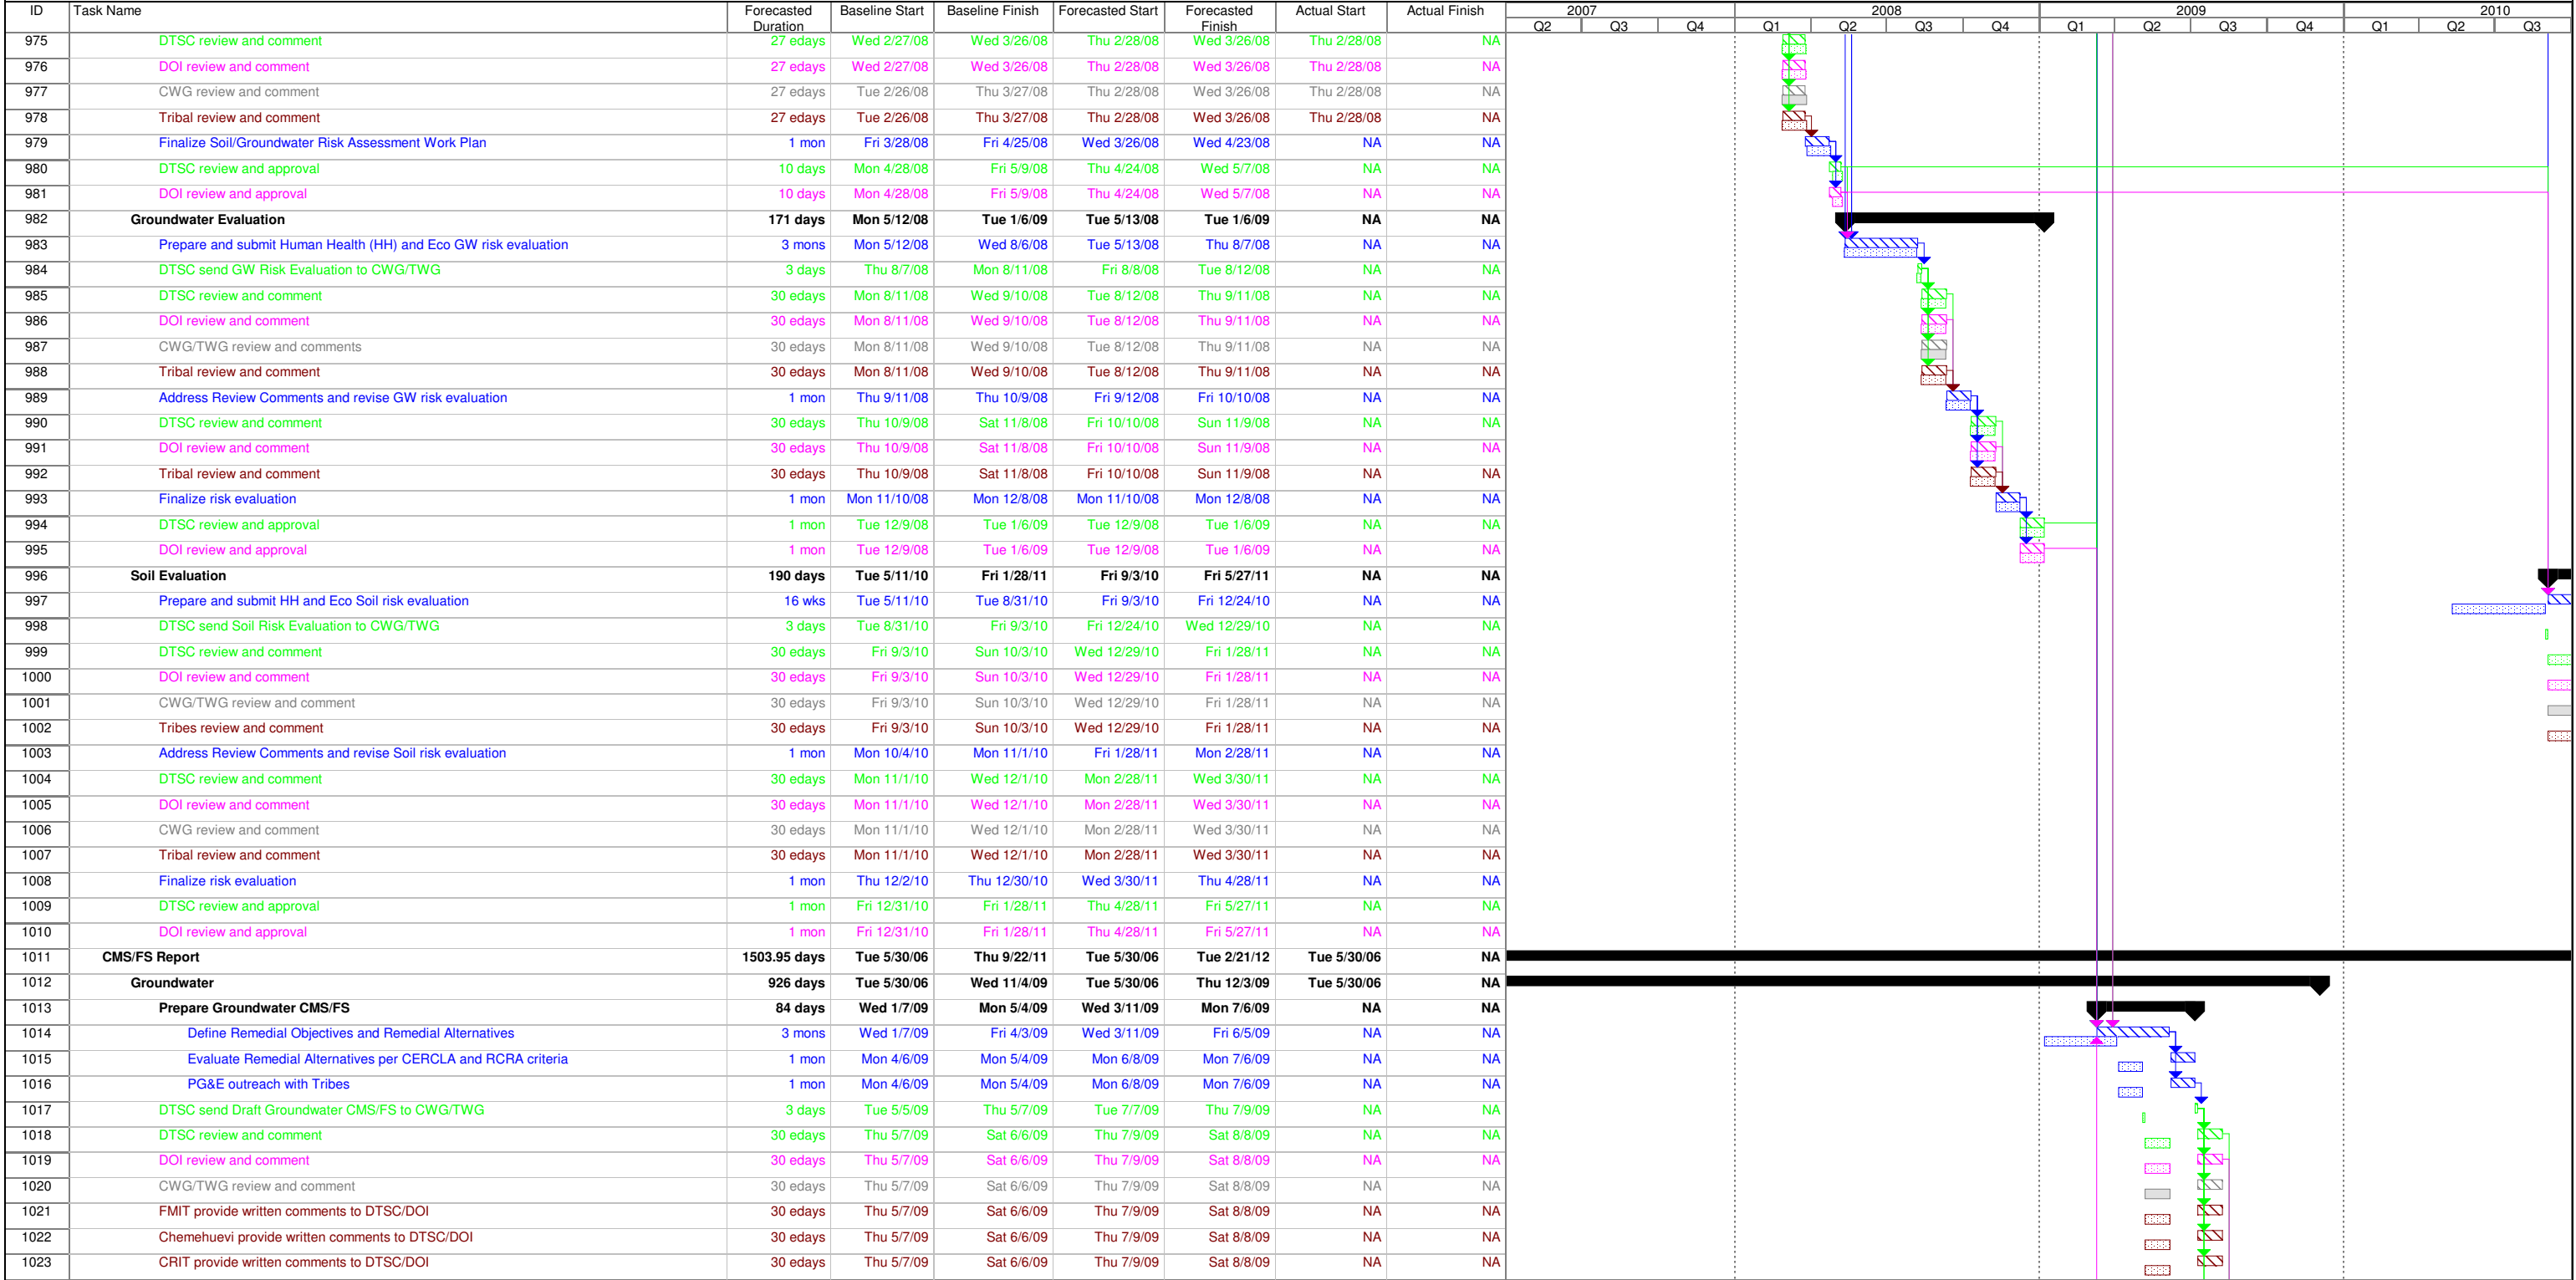

Handout 6A
Topock Remediation Project Schedule
April 2, 2008 (Revision 2)

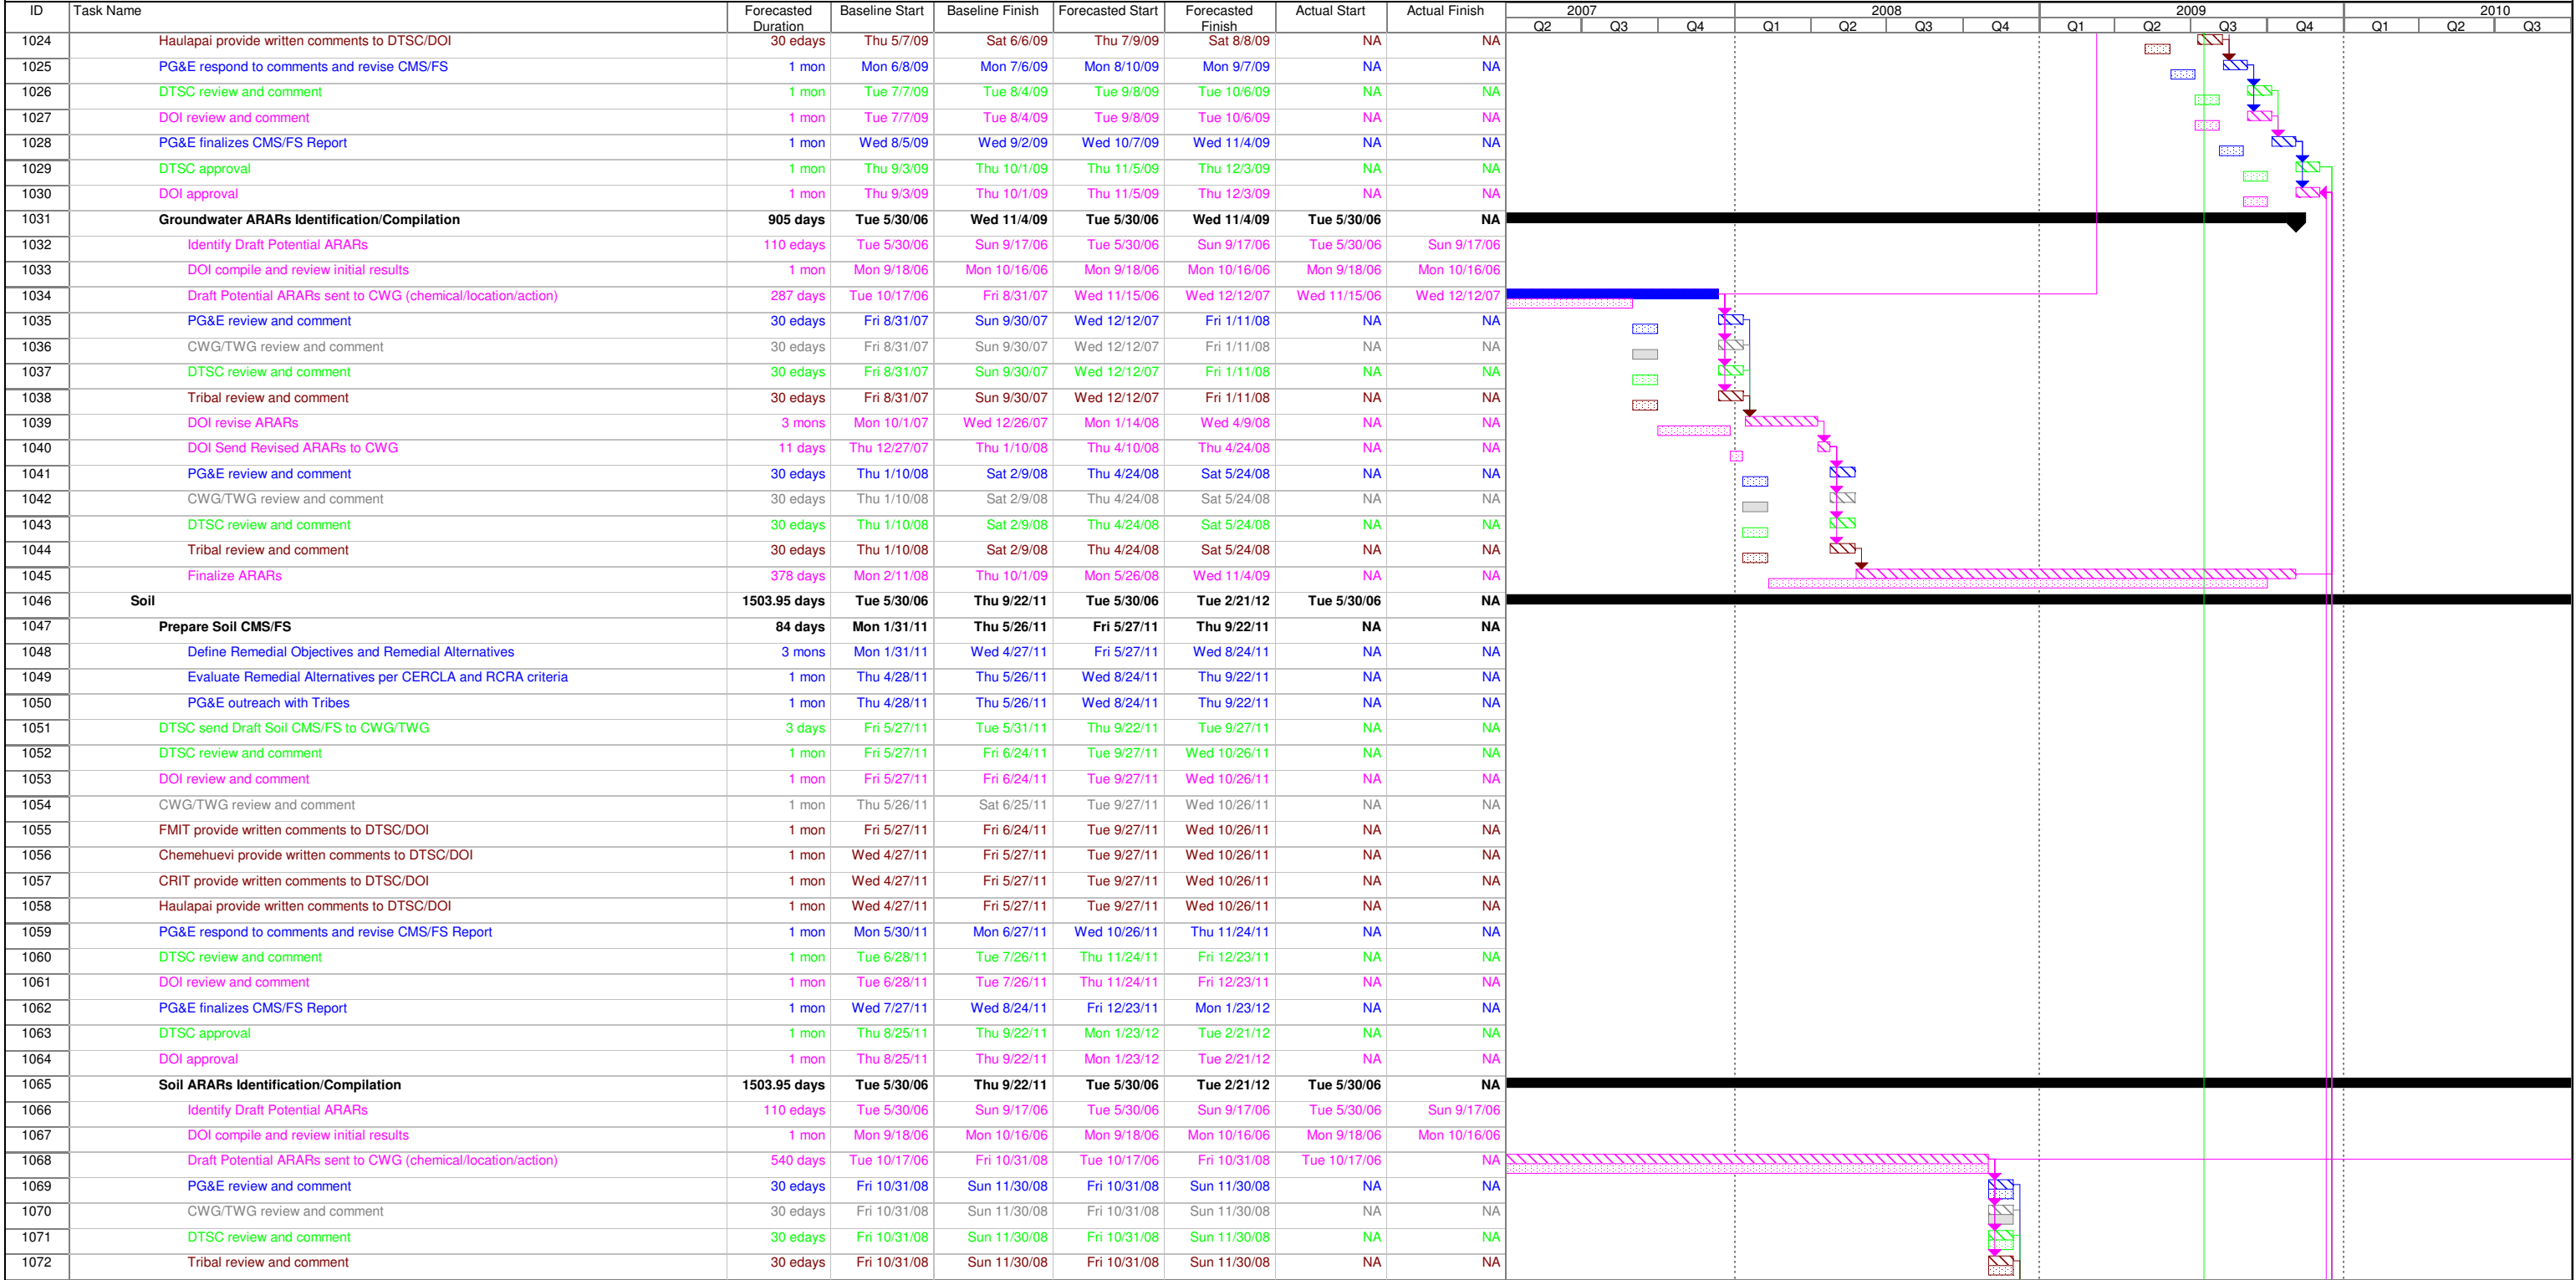

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.


Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

Handout 6A

Topock Remediation Project Schedule

April 2, 2008 (Revision 2)

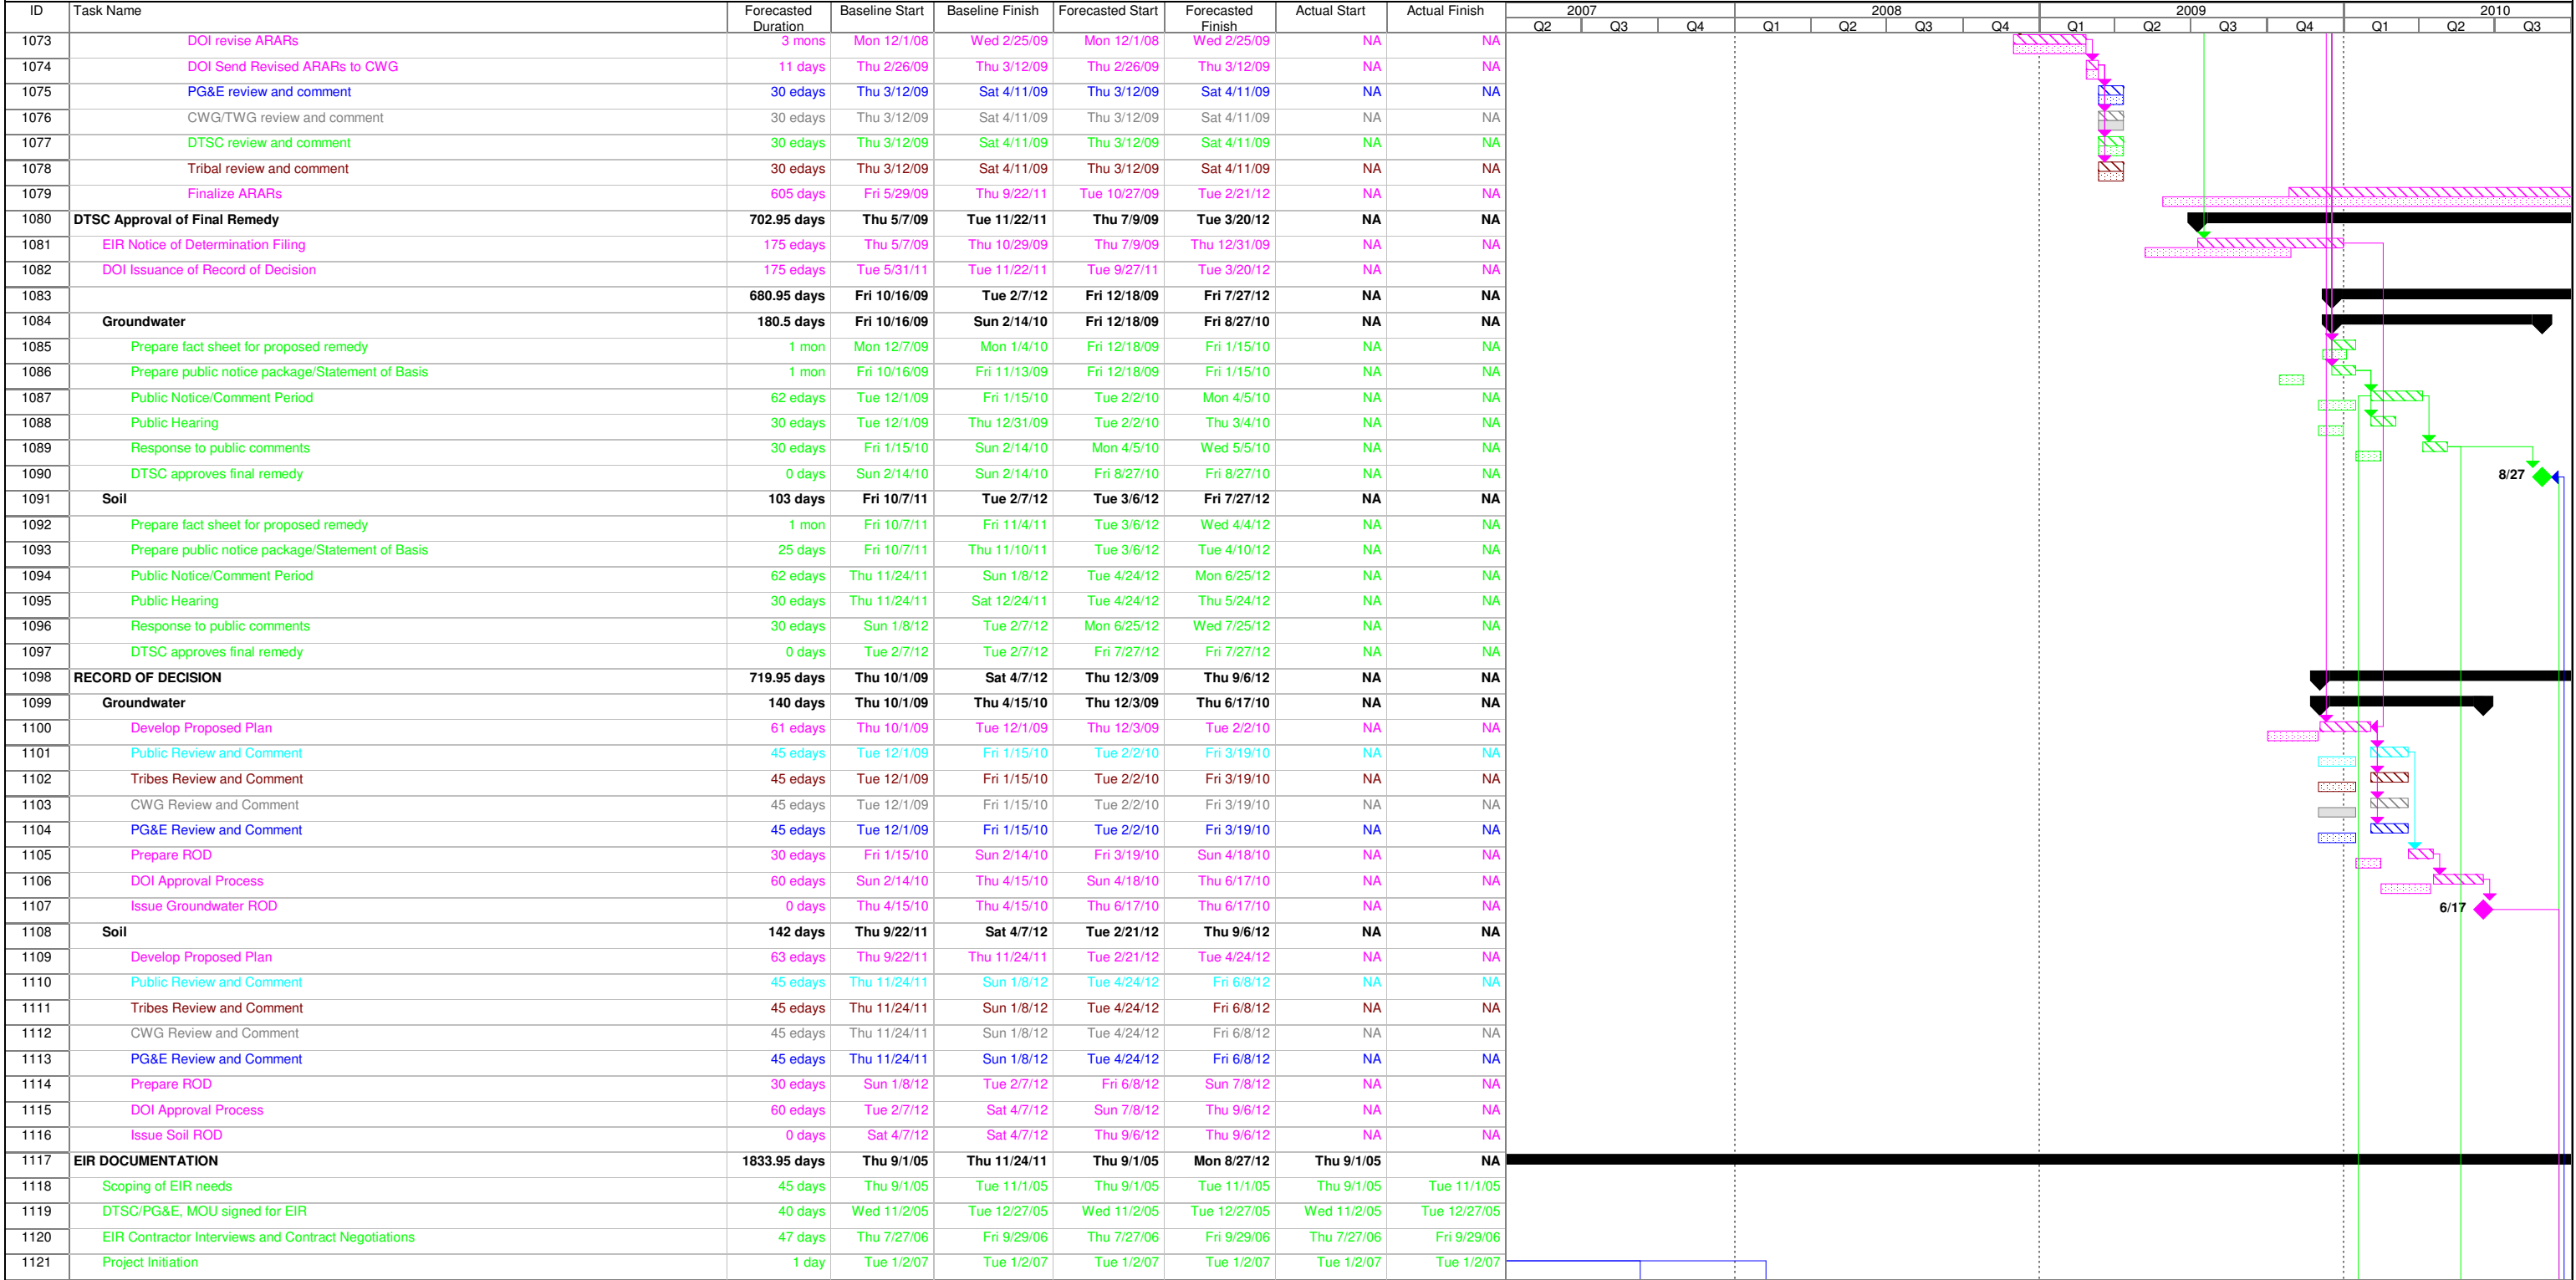

Project: PG&E Topock Remediation Project
Date: Mon 3/31/08

Page 12 of 14

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

Handout 6A

Topock Remediation Project Schedule

April 2, 2008 (Revision 2)



Project: PG&E Topock Remediation Project
Date: Mon 3/31/08

Page 13 of 14

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

Handout 6A

Topock Remediation Project Schedule

April 2, 2008 (Revision 2)

ID	Task Name	Forecasted Duration	Baseline Start	Baseline Finish	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2007			2008				2009				2010		
									Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4			
1169	EDAW prepares first administrative draft of final EIR for DTSC review	44 edays	Fri 1/2/09	Sun 2/15/09	Tue 5/11/10	Thu 6/24/10	NA	NA														
1170	DTSC reviews first administrative draft final EIR; provides comments to EDAW	30 edays	Sun 2/15/09	Tue 3/17/09	Thu 6/24/10	Sat 7/24/10	NA	NA														
1171	EDAW prepares screencheck final EIR	7.5 days	Wed 3/18/09	Fri 3/27/09	Mon 7/26/10	Wed 8/4/10	NA	NA														
1172	DTSC reviews screencheck final EIR and provides comments to EDAW	15 days	Fri 3/27/09	Fri 4/17/09	Wed 8/4/10	Wed 8/25/10	NA	NA														
1173	EDAW prepares draft Mitigation Monitoring Plan (MMP) for review by DTSC	7.5 days	Fri 3/27/09	Tue 4/7/09	Wed 8/4/10	Fri 8/13/10	NA	NA														
1174	DTSC distributes final EIR to public/commenting agencies/tribal representatives	1 day	Fri 4/17/09	Mon 4/20/09	Wed 8/25/10	Thu 8/26/10	NA	NA														
1175	Final EIR hearing conducted by DTSC; EIR certified	1 day	Mon 4/20/09	Mon 4/20/09	Thu 8/26/10	Fri 8/27/10	NA	NA														
1176	Notice of Determination filing	20.5 days	Mon 4/20/09	Wed 5/20/09	Fri 8/27/10	Sun 9/26/10	NA	NA														
1177	Notice of Determination (NOD) is filed with County Clerk; posts for 30 calendar days	30 edays	Mon 4/20/09	Wed 5/20/09	Fri 8/27/10	Sun 9/26/10	NA	NA														
1178	Supplemental EIR - Soil	239 days	Wed 6/1/11	Thu 11/24/11	Tue 9/27/11	Mon 8/27/12	NA	NA														
1179	Prepare Supplemental EIR	4 mons	Wed 6/1/11	Thu 7/28/11	Tue 9/27/11	Mon 1/23/12	NA	NA														
1180	Review/Comment/Approve	3.08 mons	Fri 7/29/11	Tue 10/25/11	Mon 1/23/12	Mon 4/23/12	NA	NA														
1181	Supplemental EIR circulates for 60 calendar days	62 edays	NA	NA	Tue 4/24/12	Mon 6/25/12	NA	NA														
1182	DTSC and EDAW conduct public hearing with public, tribes, and agencies	30 edays	NA	NA	Wed 4/25/12	Fri 5/25/12	NA	NA														
1183	PG&E review and comment	62 edays	NA	NA	Tue 4/24/12	Mon 6/25/12	NA	NA														
1184	CWG review and comment	62 edays	NA	NA	Tue 4/24/12	Mon 6/25/12	NA	NA														
1185	Tribal review and comment	62 edays	NA	NA	Tue 4/24/12	Mon 6/25/12	NA	NA														
1186	Supplemental EIR public comment period closes	1 day	NA	NA	Mon 6/25/12	Tue 6/26/12	NA	NA														
1187	EDAW assimilates comments and prepares responses for inclusion in Supplemental EIR	30 edays	NA	NA	Tue 6/26/12	Thu 7/26/12	NA	NA														
1188	Final Supplemental EIR hearing conducted; Supplemental EIR certified	1 day	NA	NA	Thu 7/26/12	Fri 7/27/12	NA	NA														
1189	Notice of Determination filing	21 days	Tue 10/25/11	Thu 11/24/11	Fri 7/27/12	Mon 8/27/12	NA	NA														
1190	Notice of Determination (NOD) is filed with County Clerk; posts for 30 calendar days	31 edays	Tue 10/25/11	Thu 11/24/11	Fri 7/27/12	Mon 8/27/12	NA	NA														
1191	DESIGN AND PERMITTING	420 days	Thu 4/15/10	Thu 11/24/11	Mon 9/27/10	Mon 5/7/12	NA	NA														
1192	Groundwater	420 days	Thu 4/15/10	Thu 11/24/11	Mon 9/27/10	Mon 5/7/12	NA	NA														
1193	Start Design and Permitting	0 days	Thu 4/15/10	Thu 4/15/10	Mon 9/27/10	Mon 9/27/10	NA	NA														
1194	CMI Workplan/Design	4 mons	Fri 4/16/10	Wed 8/11/10	Tue 9/28/10	Fri 1/21/11	NA	NA														
1195	DTSC Review and Approval	2 mons	Thu 8/12/10	Fri 10/8/10	Mon 1/24/11	Tue 3/22/11	NA	NA														
1196	WDRs	4 mons	Mon 10/11/10	Thu 2/3/11	Wed 3/23/11	Mon 7/18/11	NA	NA														
1197	CUPA	4 mons	Mon 10/11/10	Thu 2/3/11	Wed 3/23/11	Mon 7/18/11	NA	NA														
1198	USFWS Section 7 Consultation	4 mons	Mon 10/11/10	Thu 2/3/11	Wed 3/23/11	Mon 7/18/11	NA	NA														
1199	Other Permits	4 mons	Mon 10/11/10	Thu 2/3/11	Wed 3/23/11	Mon 7/18/11	NA	NA														
1200	Prepare Mitigation Monitoring Program	2 mons	Mon 10/11/10	Tue 12/7/10	Wed 3/23/11	Thu 5/19/11	NA	NA														
1201	Implementation/Construction/O&M Work Plans	3 mons	Mon 10/11/10	Wed 1/5/11	Wed 3/23/11	Fri 6/17/11	NA	NA														
1202	DTSC Review and Approval	2 mons	Thu 1/6/11	Fri 3/4/11	Mon 6/20/11	Tue 8/16/11	NA	NA														
1203	Procurement / Construction	9 mons	Mon 3/7/11	Thu 11/24/11	Wed 8/17/11	Mon 5/7/12	NA	NA														
1204	Corrective Measure Construction Complete	0 days	Thu 11/24/11	Thu 11/24/11	Mon 5/7/12	Mon 5/7/12	NA	NA														
1205	Start Operation of Final Remedy	0 days	Thu 11/24/11	Thu 11/24/11	Mon 5/7/12	Mon 5/7/12	NA	NA														
