

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 61)
SEPTEMBER 16, 2026 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2025				2026				2027				2028				Q
							Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	
1	IM Installation (Note that IM3 is currently in operation and will remain in operation until directed otherwise by agencies)	512 days	Thu 1/22/04	Tue 12/20/05	Thu 1/22/04	Tue 12/20/05																	
32	IM3 Cultural Resources Management Plan (IM3 CRMP)	986 days	Thu 7/1/04	Mon 3/10/08	Thu 7/1/04	Mon 3/10/08																	
37	Extraction Well PE-1/Facilities	230 days	Mon 3/21/05	Fri 1/27/06	Mon 3/21/05	Fri 1/27/06																	
47	Supplemental Extraction Well and Facilities	127 days	Fri 7/29/05	Thu 1/19/06	Fri 7/29/05	Thu 1/19/06																	
55	Decommissioning of IM2 Batch Treatment	1182 days	Fri 8/5/05	Fri 1/29/10	Fri 8/5/05	Fri 1/29/10																	
66	Interim Measures and Treated Water Management	751 days	Mon 5/3/04	Fri 2/16/07	Mon 5/3/04	Fri 2/16/07																	
210	Public Participation Plan	578 days	Mon 12/20/04	Fri 2/9/07	Mon 12/20/04	Fri 2/9/07																	
219	Baseline Resources Assessments	897 days	Mon 11/1/04	Mon 3/10/08	Mon 11/1/04	Mon 3/10/08																	
233	Sitewide CEQA Documentation	586 days	Wed 5/17/06	Fri 8/1/08	Wed 5/17/06	Fri 8/1/08																	
237	Programmatic Biological Assessment (PBA)	1920 days	Tue 12/19/06	Tue 4/15/14	Tue 12/19/06	Tue 4/15/14																	
250	REMEDIAL FACILITY INVESTIGATION/REMEDIAL INVESTIGATION (RFI/RI)	8156 days	Sat 2/24/96	Tue 4/13/27	Sat 2/24/96	NA																	
251	Historical RFI/RI Reports (Feb. 2005 and Prior Versions)	2455 days	Sat 2/24/96	Fri 7/8/05	Sat 2/24/96	Fri 7/8/05																	
269	Site History Report (Vol 1)	466 days	Tue 11/15/05	Wed 8/15/07	Tue 11/15/05	Wed 8/15/07																	
284	RFI/RI Vol 1 Addendum	1829 days	Wed 7/11/07	Tue 7/8/14	Wed 7/11/07	Tue 7/8/14																	
306	Final Groundwater RFI/RI (Vol 2)	1948 days	Mon 6/27/05	Fri 11/16/12	Mon 6/27/05	Fri 11/16/12																	
616	ADEQ Topock Groundwater Study	475 days	Thu 11/18/04	Wed 8/23/06	Thu 11/18/04	Wed 8/23/06																	
620	Final Soil RFI/RI (Vol 3)	5346 days	Sat 7/15/06	Thu 12/17/26	Sat 7/15/06	NA																	
621	Implementation of Off-site Soil Sampling (Part A Phase 1) and Data Gaps Evaluation	1215 days	Sat 7/15/06	Fri 2/25/11	Sat 7/15/06	Fri 2/25/11																	
770	Draft On-site Soil Sampling (Part B) DQOs	1122 days	Wed 12/6/06	Fri 3/11/11	Wed 12/6/06	Fri 3/11/11																	
825	Soil RFI/RI Work Plan	1211 days	Tue 1/4/11	Mon 8/24/15	Tue 1/4/11	Mon 8/24/15																	
922	Work Plan Implementation/Data Gaps Analysis	594 days	Tue 8/25/15	Thu 11/30/17	Tue 8/25/15	Thu 11/30/17																	
978	Reporting	2483 days	Tue 6/20/17	Thu 12/17/26	Tue 6/20/17	NA																	
979	Soil Risk Assessment	770 days	Tue 6/20/17	Fri 5/29/20	Tue 6/20/17	Fri 5/29/20																	
1002	Soil Post-NTCRA Risk Assessment	693 days	Wed 4/24/24	Thu 12/17/26	Wed 4/24/24	NA																	
1003	Validated NTCRA Data Available for Risk Assessment	80 days	Wed 4/24/24	Tue 8/13/24	Wed 4/24/24	Tue 8/13/24																	
1004	PG&E prepares/submits Soil Post-NTCRA Risk Assessment Report	5 mons	Thu 6/6/24	Fri 12/13/24	Thu 6/6/24	Fri 12/13/24																	
1005	DTSC review/comment	142.38 edays	Mon 12/16/24	Wed 5/7/25	Mon 12/16/24	Wed 5/7/25																	
1006	DOI review/comment	147.38 edays	Mon 12/16/24	Mon 5/12/25	Mon 12/16/24	Mon 5/12/25																	
1007	CWG/TWG review/comment	71.38 edays	Mon 12/16/24	Tue 2/25/25	Mon 12/16/24	Tue 2/25/25																	
1008	Tribes review/comment	74.38 edays	Mon 12/16/24	Fri 2/28/25	Mon 12/16/24	Fri 2/28/25																	
1009	Review/compile Comment Table	24.38 edays	Tue 5/13/25	Fri 6/6/25	Tue 5/13/25	Fri 6/6/25																	
1010	Prepare/send RTC Table	60.38 edays	Fri 6/6/25	Tue 8/5/25	Fri 6/6/25	Tue 8/5/25																	
1011	Hold RTC Meeting	0 days	Thu 10/9/25	Thu 10/9/25	Thu 10/9/25	Thu 10/9/25																	
1012	Finalize/Submit Draft Soil Post-NTCRA Risk Assessment with RTC Table	4.1 mons	Fri 10/10/25	Fri 2/6/26	Fri 10/10/25	Fri 2/6/26																	
1013	CWG/TWG review	18.38 edays	Mon 2/9/26	Fri 2/27/26	Mon 2/9/26	Fri 2/27/26																	
1014	Tribes review	16.38 edays	Mon 2/9/26	Wed 2/25/26	Mon 2/9/26	Wed 2/25/26																	
1015	DTSC review	8.2 wks	Mon 2/9/26	Mon 4/6/26	Mon 2/9/26	Mon 4/6/26																	
1016	DOI review	4 wks	Mon 2/9/26	Fri 3/6/26	Mon 2/9/26	Fri 3/6/26																	
1017	Meeting to discuss review comments	0 days	Wed 3/4/26	Wed 3/4/26	Wed 3/4/26	Wed 3/4/26																	
1018	Finalize/Submit Final Soil Post-NTCRA Risk Assessment Report with RTC Table	239.38 edays	Thu 3/5/26	Fri 10/30/26	Thu 3/5/26	NA																	
1019	DTSC review/accept report	45 edays	Mon 11/2/26	Thu 12/17/26	NA	NA																	
1020	DOI review/accept report	45 edays	Mon 11/2/26	Thu 12/17/26	NA	NA																	

Project: PG&E Topock Remediation Project
Date: Tue 8/25/26

Page 1 of 5

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:

PG&E
DTSC
Federal Agencies
Tribes/SHPO
CWG/TWG
Other CA Agencies
Public
AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 61)
SEPTEMBER 16, 2026 CWG MEETING

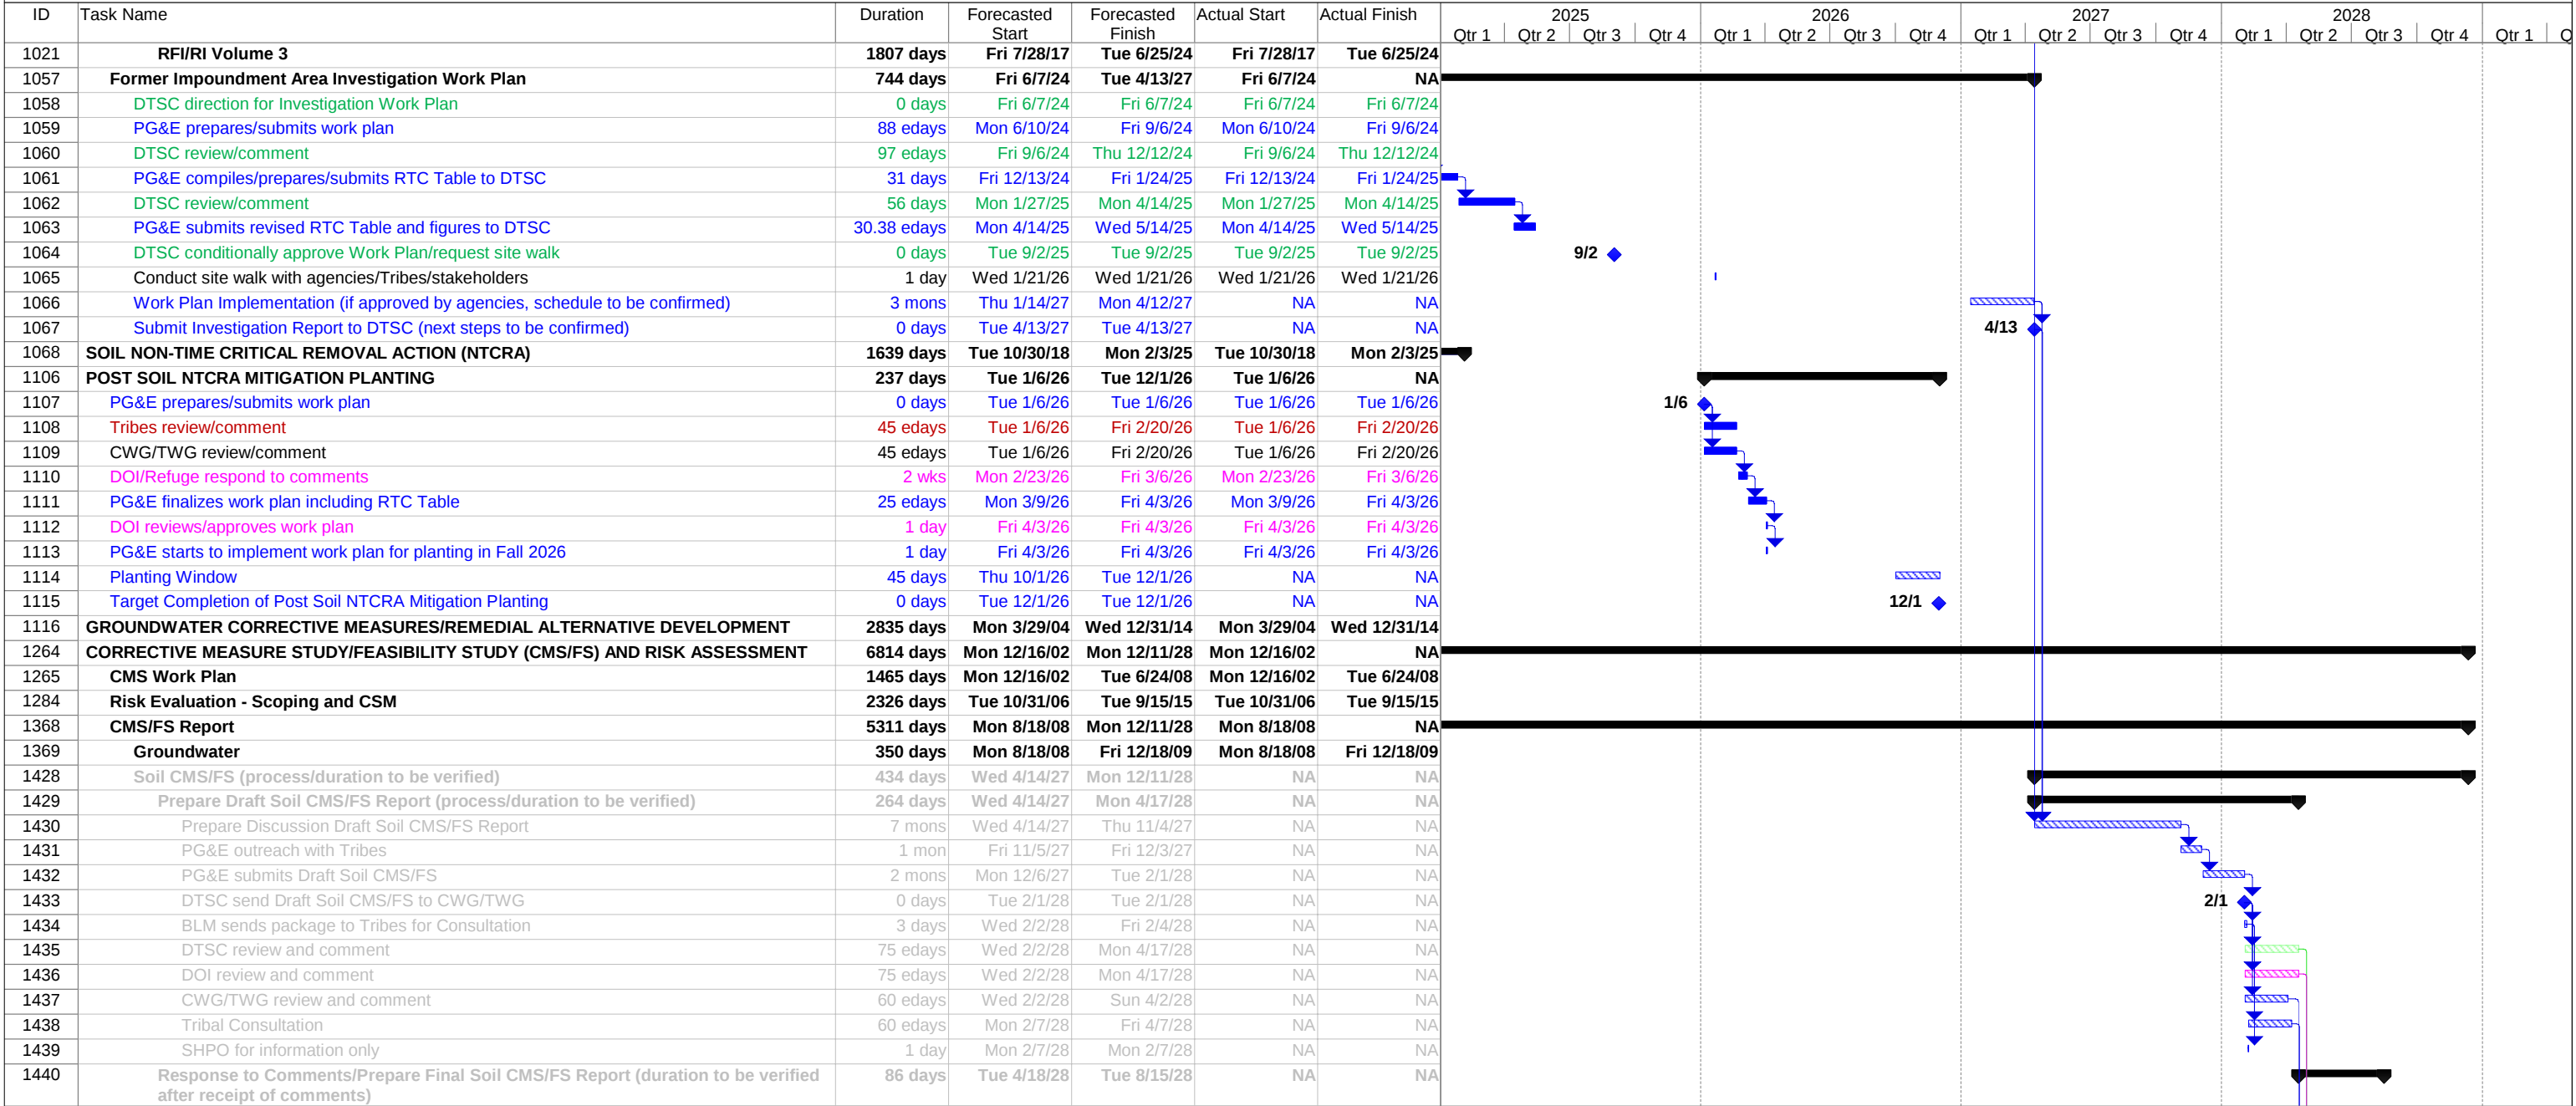

Project: PG&E Topock Remediation Project
Date: Tue 8/25/26

Page 2 of 5

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:


PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions

- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 61)
SEPTEMBER 16, 2026 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2025				2026				2027				2028				Qtr 1	Qtr 2	Qtr 3	Qtr 4
							Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4				
1441	Review/compile Comment Table	1 mon	Tue 4/18/28	Tue 5/16/28	NA	NA																				
1442	Comment clarification meeting	0 days	Mon 4/24/28	Mon 4/24/28	NA	NA																				
1443	Prepare/send RTC Table	2 mons	Wed 5/17/28	Thu 7/13/28	NA	NA																				
1444	RTC Meeting	23 days	Thu 7/13/28	Tue 8/15/28	NA	NA																				
1445	Send agenda (2 wks prior to meeting)	0 days	Thu 7/13/28	Thu 7/13/28	NA	NA																				
1446	Hold Multiple Meetings	13 days	Fri 7/28/28	Tue 8/15/28	NA	NA																				
1447	Prepare Final Soil CMS/FS Report	3 mons	Wed 8/16/28	Fri 11/10/28	NA	NA																				
1448	DTSC review and concur	1 mon	Mon 11/13/28	Mon 12/11/28	NA	NA																				
1449	DOI review and concur	1 mon	Mon 11/13/28	Mon 12/11/28	NA	NA																				
1450	CEQA Evaluation (Place Holder Item only. Details including duration will be provided after the prior steps are better defined))	3 mons	Tue 12/12/28	Thu 3/8/29	NA	NA																				
1451	STATEMENT OF BASIS	5073 days	Mon 1/4/10	Wed 5/30/29	Mon 1/4/10	NA																				
1452	Groundwater	284 days	Mon 1/4/10	Mon 1/31/11	Mon 1/4/10	Mon 1/31/11																				
1459	Soil (process/duration to be verified)	121 days	Wed 12/13/28	Wed 5/30/29	NA	NA																				
1460	Prepare fact sheet for proposed remedy	1 mon	Wed 12/13/28	Wed 1/10/29	NA	NA																				
1461	Prepare public notice package/Statement of Basis	2 mons	Tue 12/19/28	Wed 2/14/29	NA	NA																				
1462	Public Notice/Comment Period	46 edays	Thu 2/15/29	Mon 4/2/29	NA	NA																				
1463	Public Hearing	15 edays	Wed 2/28/29	Thu 3/15/29	NA	NA																				
1464	Prepare Responsiveness Summary	2 mons	Tue 4/3/29	Wed 5/30/29	NA	NA																				
1465	DTSC adopts final remedy	0 days	Wed 5/30/29	Wed 5/30/29	NA	NA																				
1466	RECORD OF DECISION	5179 days	Fri 12/18/09	Wed 10/10/29	Fri 12/18/09	NA																				
1467	Groundwater	288 days	Fri 12/18/09	Thu 1/20/11	Fri 12/18/09	Thu 1/20/11																				
1478	Soil (process/duration to be verified)	217 days	Mon 12/11/28	Wed 10/10/29	NA	NA																				
1479	Develop Proposed Plan	60 edays	Mon 12/11/28	Fri 2/9/29	NA	NA																				
1480	Prepare factsheet	60 edays	Mon 12/11/28	Fri 2/9/29	NA	NA																				
1481	Tribal Consultation	60 edays	Mon 2/12/29	Fri 4/13/29	NA	NA																				
1482	Public Review and Comment	45 edays	Mon 2/12/29	Thu 3/29/29	NA	NA																				
1483	CWG Review and Comment	45 edays	Mon 2/12/29	Thu 3/29/29	NA	NA																				
1484	PG&E Review and Comment	45 edays	Mon 2/12/29	Thu 3/29/29	NA	NA																				
1485	Prepare ROD and Responsiveness Summary	119 edays	Fri 4/13/29	Fri 8/10/29	NA	NA																				
1486	DOI Approval Process	60 edays	Fri 8/10/29	Tue 10/9/29	NA	NA																				
1487	Issue Soil ROD	1 day	Wed 10/10/29	Wed 10/10/29	NA	NA																				
1488	Section 106 Programmatic Agreement (PA)	1858 days	Fri 10/10/08	Wed 11/18/15	Fri 10/10/08	NA																				
1521	EIR DOCUMENTATION	1449 days	Thu 9/1/05	Wed 3/2/11	Thu 9/1/05	Wed 3/2/11																				
1594	DESIGN, PERMITTING, AND CONSTRUCTION OF GROUNDWATER REMEDY	3669 days	Mon 1/31/11	Thu 2/13/25	Mon 1/31/11	Thu 2/13/25																				
1595	Corrective Measure Implementation/Remedial Design (CMI/RD) Workplan	199 days	Mon 1/31/11	Thu 11/3/11	Mon 1/31/11	Thu 11/3/11																				
1609	Remedial Design (Preliminary, Intermediate, and Pre-Final/Final)	1723 days	Tue 9/20/11	Tue 4/24/18	Tue 9/20/11	Tue 4/24/18																				
1782	Proposed Phase 2B Design Modification	575 days	Fri 12/2/22	Thu 2/13/25	Fri 12/2/22	Thu 2/13/25																				
1790	Community Outreach	1710 days	Fri 10/7/11	Tue 4/24/18	Fri 10/7/11	Tue 4/24/18																				
1800	Project Contracting	2.9 mons	Wed 4/4/18	Wed 6/27/18	Wed 4/4/18	Wed 6/27/18																				
1801	Construction	2015 days?	Wed 6/27/18	Wed 3/11/26	Wed 6/27/18	NA																				
1802	Phase 1 Construction	1046 days	Wed 6/27/18	Fri 6/24/22	Wed 6/27/18	Fri 6/24/22																				
1834	Phase 2A Planning/Contracting	30 days	Mon 2/14/22	Fri 3/25/22	Mon 2/14/22	Fri 3/25/22																				

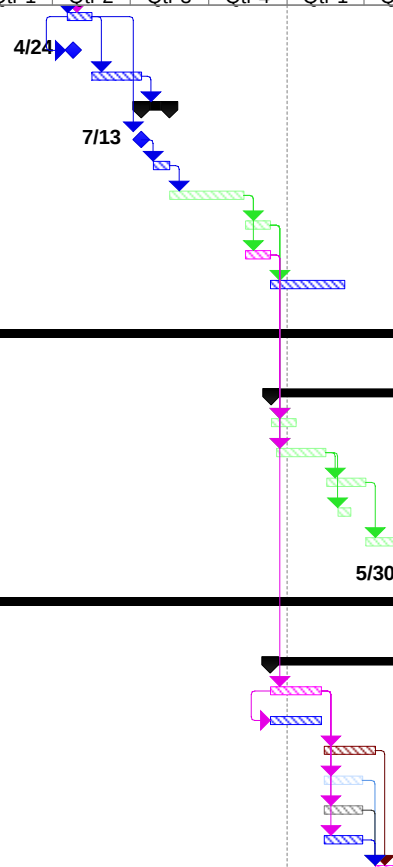

Project: PG&E Topock Remediation Project
Date: Tue 8/25/26

Page 3 of 5

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

[

]

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:

PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions

- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 61)
SEPTEMBER 16, 2026 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2025				2026				2027				2028				Q
							Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	
1835	Phase 2A Construction Mobilization	16 days	Mon 2/14/22	Mon 3/7/22	Mon 2/14/22	Mon 3/7/22																	
1839	Major Phase 2A Construction Activities	1262 days	Tue 3/8/22	Mon 1/4/27	Tue 3/8/22	NA																	
1840	Well Installation	1262 days	Tue 3/8/22	Mon 1/4/27	Tue 3/8/22	NA																	
1841	Decision on FW-2	1 day	Tue 3/17/26	Tue 3/17/26	Tue 3/17/26	Tue 3/17/26																	
1842	Install and Develop Arsenic Monitoring Wells (MW-HH, MW-II)	65 days	Tue 10/6/26	Mon 1/4/27	NA	NA																	
1843	Well Installation and Buildout (TCS-1/2, TWB-1/3, ER-1/2/3/4, RB-5, TCS-1, 2, ER-6, TWB-1/3 full build-out; RB-2, 3, 4 civil/ mechanical only, ER-1/2 full build-out, ER-3/4 civil	389 days	Tue 3/8/22	Thu 8/31/23	Tue 3/8/22	Thu 8/31/23																	
1844	Pipeline Installation	975 days	Mon 4/4/22	Thu 12/25/25	Mon 4/4/22	Thu 12/25/25																	
1845	Inside TCS	160 days	Mon 4/4/22	Fri 11/11/22	Mon 4/4/22	Fri 11/11/22																	
1846	Outside TCS	250 days	Tue 7/19/22	Fri 6/30/23	Tue 7/19/22	Fri 6/30/23																	
1847	East Ravine Pipeline (C18)	104 days	Mon 8/4/25	Thu 12/25/25	Mon 8/4/25	Thu 12/25/25																	
1848	Phase 2B Planning/Contracting	9.3 mons	Mon 1/6/25	Mon 10/6/25	Mon 1/6/25	NA																	
1849	Phase 2B Well Drilling (For Planning Only, Schedule May Change)	25.86 mons	Tue 3/4/25	Wed 3/31/27	Tue 3/4/25	NA																	
1921	Phase 2B Pipeline and Supporting Infrastructure Construction	935 days	Mon 1/6/25	Thu 8/3/28	Mon 1/6/25	NA																	
1922	Planning/Preparation	365 days	Mon 1/6/25	Fri 5/29/26	Mon 1/6/25	Fri 5/29/26																	
1923	Pipeline B (incl final connection and testing)	413 days	Mon 10/6/25	Tue 5/4/27	Mon 10/6/25	NA																	
1924	I-40 Jack and Bore	52 days	Wed 2/18/26	Thu 4/30/26	Wed 2/18/26	Thu 4/30/26																	
1925	Arch Bridge	163 days	Wed 9/30/26	Thu 5/13/27	NA	NA																	
1926	Pipeline I2 (Initial)	63 edays	Wed 12/17/25	Wed 2/18/26	Wed 12/17/25	Wed 2/18/26																	
1927	Pipeline I2 (Final)	50 days	Wed 9/9/26	Mon 11/16/26	NA	NA																	
1928	Pipeline C11 (Connect ER-3 and ER-4)	41 days	Mon 10/5/26	Mon 11/30/26	NA	NA																	
1929	Pipeline A	176 days	Tue 6/23/26	Mon 2/22/27	Tue 6/23/26	NA																	
1930	Remaining Supporting Facilities (Including TCS Tank Farm Retrofit and RPWCP)	589 days	Tue 5/5/26	Thu 8/3/28	Tue 5/5/26	NA																	
1931	Phase 2 Well Vaults and Electrical	133 days	Mon 1/4/27	Wed 7/7/27	NA	NA																	
1932	System Integration and Functional Testing	201 days	Thu 10/28/27	Thu 8/3/28	NA	NA																	
1933	Site Cleanup and Demob	45 days	Fri 8/4/28	Thu 10/5/28	NA	NA																	
1934	Start-up Complete Groundwater Remedy	0 days	Thu 10/5/28	Thu 10/5/28	NA	NA																	
1935	Start-up Complete/Start Full Remedy Operation	0 days	Thu 10/5/28	Thu 10/5/28	NA	NA																	
1936	Reporting	2688 days	Mon 11/12/18	Wed 2/21/29	NA	NA																	
1937	Prepare/submit monthly construction progress reports	128 mons	Mon 11/12/18	Wed 2/21/29	NA	NA																	
1938	Complete Remedy Startup/Start Remedy Operation and Maintenance	0 days	Thu 10/5/28	Thu 10/5/28	NA	NA																	
1939	First Five Year Review of Groundwater Remedy	160 days	Mon 5/1/23	Thu 12/7/23	Mon 5/1/23	Thu 12/7/23																	
1940	Public Notice/Factsheet	0 days	Mon 5/1/23	Mon 5/1/23	Mon 5/1/23	Mon 5/1/23																	
1941	Request For Interview	30.38 edays	Mon 5/1/23	Wed 5/31/23	Mon 5/1/23	Wed 5/31/23																	
1942	Interview Period	60.38 edays	Thu 6/1/23	Mon 7/31/23	Thu 6/1/23	Mon 7/31/23																	
1943	Five-Year Review Report Preparation	220.38 edays	Mon 5/1/23	Thu 12/7/23	Mon 5/1/23	Thu 12/7/23																	
1944	Notice of Report Availability	0 days	Thu 12/7/23	Thu 12/7/23	Thu 12/7/23	Thu 12/7/23																	
1945	Other Topock Investigative Activities	240 days	Mon 12/9/24	Mon 11/10/25	Mon 12/9/24	Mon 11/10/25																	
1946	PFAS Soil and Groundwater Investigation (RWQCB Order R7-2024-040)	240 days	Mon 12/9/24	Mon 11/10/25	Mon 12/9/24	Mon 11/10/25																	
1947	RWQCB Issued Investigative Order R7-2024-040	0 days	Mon 12/9/24	Mon 12/9/24	Mon 12/9/24	Mon 12/9/24																	
1948	PG&E prepares/submits Review of PFAS Evaluation of Historical Chemical Use Report	81 days	Mon 12/9/24	Mon 3/31/25	Mon 12/9/24	Mon 3/31/25																	
1949	RWQCB review of submittal	72 days	Tue 4/1/25	Wed 7/9/25	Tue 4/1/25	Wed 7/9/25																	
1950	PG&E requested an extension of the report and work plan due date	0 days	Thu 9/11/25	Thu 9/11/25	Thu 9/11/25	Thu 9/11/25																	

Project: PG&E Topock Remediation Project
Date: Tue 8/25/26

Page 4 of 5

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:

PG&E
DTSC
Federal Agencies
Tribes/SHPO
CWG/TWG
Other CA Agencies
Public
AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 61)
SEPTEMBER 16, 2026 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2025				2026				2027				2028				Q
							Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	
1951	RWQCB approved the extension request	0 days	Mon 9/22/25	Mon 9/22/25	Mon 9/22/25	Mon 9/22/25			9/22														
1952	PG&E prepares/submits updated PFAS Evaluation of Historical Chemical Use and PFAS Investigation Work Plan	70 days	Thu 7/10/25	Wed 10/15/25	Thu 7/10/25	Wed 10/15/25																	
1953	PG&E resubmits the redacted PFAS Evaluation of Historical Chemical Use	0 days	Mon 11/10/25	Mon 11/10/25	Mon 11/10/25	Mon 11/10/25			11/10														

Project: PG&E Topock Remediation Project
Date: Tue 8/25/26

Page 5 of 5

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only
