

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 58)
DECEMBER 3, 2025 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2025				2026				2027				2028				Q
							Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	
1	IM Installation (Note that IM3 is currently in operation and will remain in operation until directed otherwise by agencies)	512 days	Thu 1/22/04	Tue 12/20/05	Thu 1/22/04	Tue 12/20/05																	
32	IM3 Cultural Resources Management Plan (IM3 CRMP)	986 days	Thu 7/1/04	Mon 3/10/08	Thu 7/1/04	Mon 3/10/08																	
37	Extraction Well PE-1/Facilities	230 days	Mon 3/21/05	Fri 1/27/06	Mon 3/21/05	Fri 1/27/06																	
47	Supplemental Extraction Well and Facilities	127 days	Fri 7/29/05	Thu 1/19/06	Fri 7/29/05	Thu 1/19/06																	
55	Decommissioning of IM2 Batch Treatment	1182 days	Fri 8/5/05	Fri 1/29/10	Fri 8/5/05	Fri 1/29/10																	
66	Interim Measures and Treated Water Management	751 days	Mon 5/3/04	Fri 2/16/07	Mon 5/3/04	Fri 2/16/07																	
210	Public Participation Plan	578 days	Mon 12/20/04	Fri 2/9/07	Mon 12/20/04	Fri 2/9/07																	
219	Baseline Resources Assessments	897 days	Mon 11/1/04	Mon 3/10/08	Mon 11/1/04	Mon 3/10/08																	
233	Sitewide CEQA Documentation	586 days	Wed 5/17/06	Fri 8/1/08	Wed 5/17/06	Fri 8/1/08																	
237	Programmatic Biological Assessment (PBA)	1920 days	Tue 12/19/06	Tue 4/15/14	Tue 12/19/06	Tue 4/15/14																	
250	REMEDIAL FACILITY INVESTIGATION/REMEDIAL INVESTIGATION (RFI/RI)	7916.35 days	Sat 2/24/96	Thu 5/14/26	Sat 2/24/96	NA																	
251	Historical RFI/RI Reports (Feb. 2005 and Prior Versions)	2455 days	Sat 2/24/96	Fri 7/8/05	Sat 2/24/96	Fri 7/8/05																	
269	Site History Report (Vol 1)	466 days	Tue 11/15/05	Wed 8/15/07	Tue 11/15/05	Wed 8/15/07																	
284	RFI/RI Vol 1 Addendum	1829 days	Wed 7/11/07	Tue 7/8/14	Wed 7/11/07	Tue 7/8/14																	
306	Final Groundwater RFI/RI (Vol 2)	1948 days	Mon 6/27/05	Fri 11/16/12	Mon 6/27/05	Fri 11/16/12																	
616	ADEQ Topock Groundwater Study	475 days	Thu 11/18/04	Wed 8/23/06	Thu 11/18/04	Wed 8/23/06																	
620	Final Soil RFI/RI (Vol 3)	5189.35 days	Sat 7/15/06	Thu 5/14/26	Sat 7/15/06	NA																	
621	Implementation of Off-site Soil Sampling (Part A Phase 1) and Data Gaps Evaluation	1215 days	Sat 7/15/06	Fri 2/25/11	Sat 7/15/06	Fri 2/25/11																	
770	Draft On-site Soil Sampling (Part B) DQOs	1122 days	Wed 12/6/06	Fri 3/11/11	Wed 12/6/06	Fri 3/11/11																	
825	Soil RFI/RI Work Plan	1211 days	Tue 1/4/11	Mon 8/24/15	Tue 1/4/11	Mon 8/24/15																	
922	Work Plan Implementation/Data Gaps Analysis	594 days	Tue 8/25/15	Thu 11/30/17	Tue 8/25/15	Thu 11/30/17																	
978	Reporting	2326.35 days	Tue 6/20/17	Thu 5/14/26	Tue 6/20/17	NA																	
979	Soil Risk Assessment	770 days	Tue 6/20/17	Fri 5/29/20	Tue 6/20/17	Fri 5/29/20																	
1002	Soil Post-NTCRA Risk Assessment	536.35 days	Wed 4/24/24	Thu 5/14/26	Wed 4/24/24	NA																	
1003	Validated NTCRA Data Available for Risk Assessment	80 days	Wed 4/24/24	Tue 8/13/24	Wed 4/24/24	Tue 8/13/24																	
1004	PG&E prepares/submits Soil Post-NTCRA Risk Assessment Report	5 mons	Thu 6/6/24	Fri 12/13/24	Thu 6/6/24	Fri 12/13/24																	
1005	DTSC review/comment	142.38 edays	Mon 12/16/24	Wed 5/7/25	Mon 12/16/24	Wed 5/7/25																	
1006	DOI review/comment	147.38 edays	Mon 12/16/24	Mon 5/12/25	Mon 12/16/24	Mon 5/12/25																	
1007	CWG/TWG review/comment	71.38 edays	Mon 12/16/24	Tue 2/25/25	Mon 12/16/24	Tue 2/25/25																	
1008	Tribes review/comment	74.38 edays	Mon 12/16/24	Fri 2/28/25	Mon 12/16/24	Fri 2/28/25																	
1009	Review/compile Comment Table	24.38 edays	Tue 5/13/25	Fri 6/6/25	Tue 5/13/25	Fri 6/6/25																	
1010	Prepare/send RTC Table	60.38 edays	Fri 6/6/25	Tue 8/5/25	Fri 6/6/25	Tue 8/5/25																	
1011	Hold RTC Meeting	0 days	Thu 10/9/25	Thu 10/9/25	Thu 10/9/25	Thu 10/9/25																	
1012	Finalize/Submit Draft Final Soil Post-NTCRA Risk Assessment with RTC Table	3.35 mons	Fri 10/10/25	Fri 1/16/26	Fri 10/10/25	NA																	
1013	CWG/TWG review	3 wks	Mon 1/19/26	Mon 2/9/26	NA	NA																	
1014	Tribes review	3 wks	Mon 1/19/26	Mon 2/9/26	NA	NA																	
1015	DTSC review	3 wks	Mon 1/19/26	Mon 2/9/26	NA	NA																	
1016	DOI review	3 wks	Mon 1/19/26	Mon 2/9/26	NA	NA																	
1017	Meeting to discuss review comments (if needed, date to be confirmed)	0 days	Wed 2/11/26	Wed 2/11/26	NA	NA																	
1018	Finalize/Submit Final Soil Post-NTCRA Risk Assessment Report with RTC Table	46 edays	Thu 2/12/26	Mon 3/30/26	NA	NA																	
1019	DTSC review/accept report	45 edays	Mon 3/30/26	Thu 5/14/26	NA	NA																	
1020	DOI review/accept report	45 edays	Mon 3/30/26	Thu 5/14/26	NA	NA																	

Project: PG&E Topock Remediation Project

Date: Sat 11/15/25

Page 1 of 4

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

[


]

edays = calendar days; days = work days

Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).

*Timeframes shown are for planning purpose. Actual timeframes may vary.

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 58)
DECEMBER 3, 2025 CWG MEETING

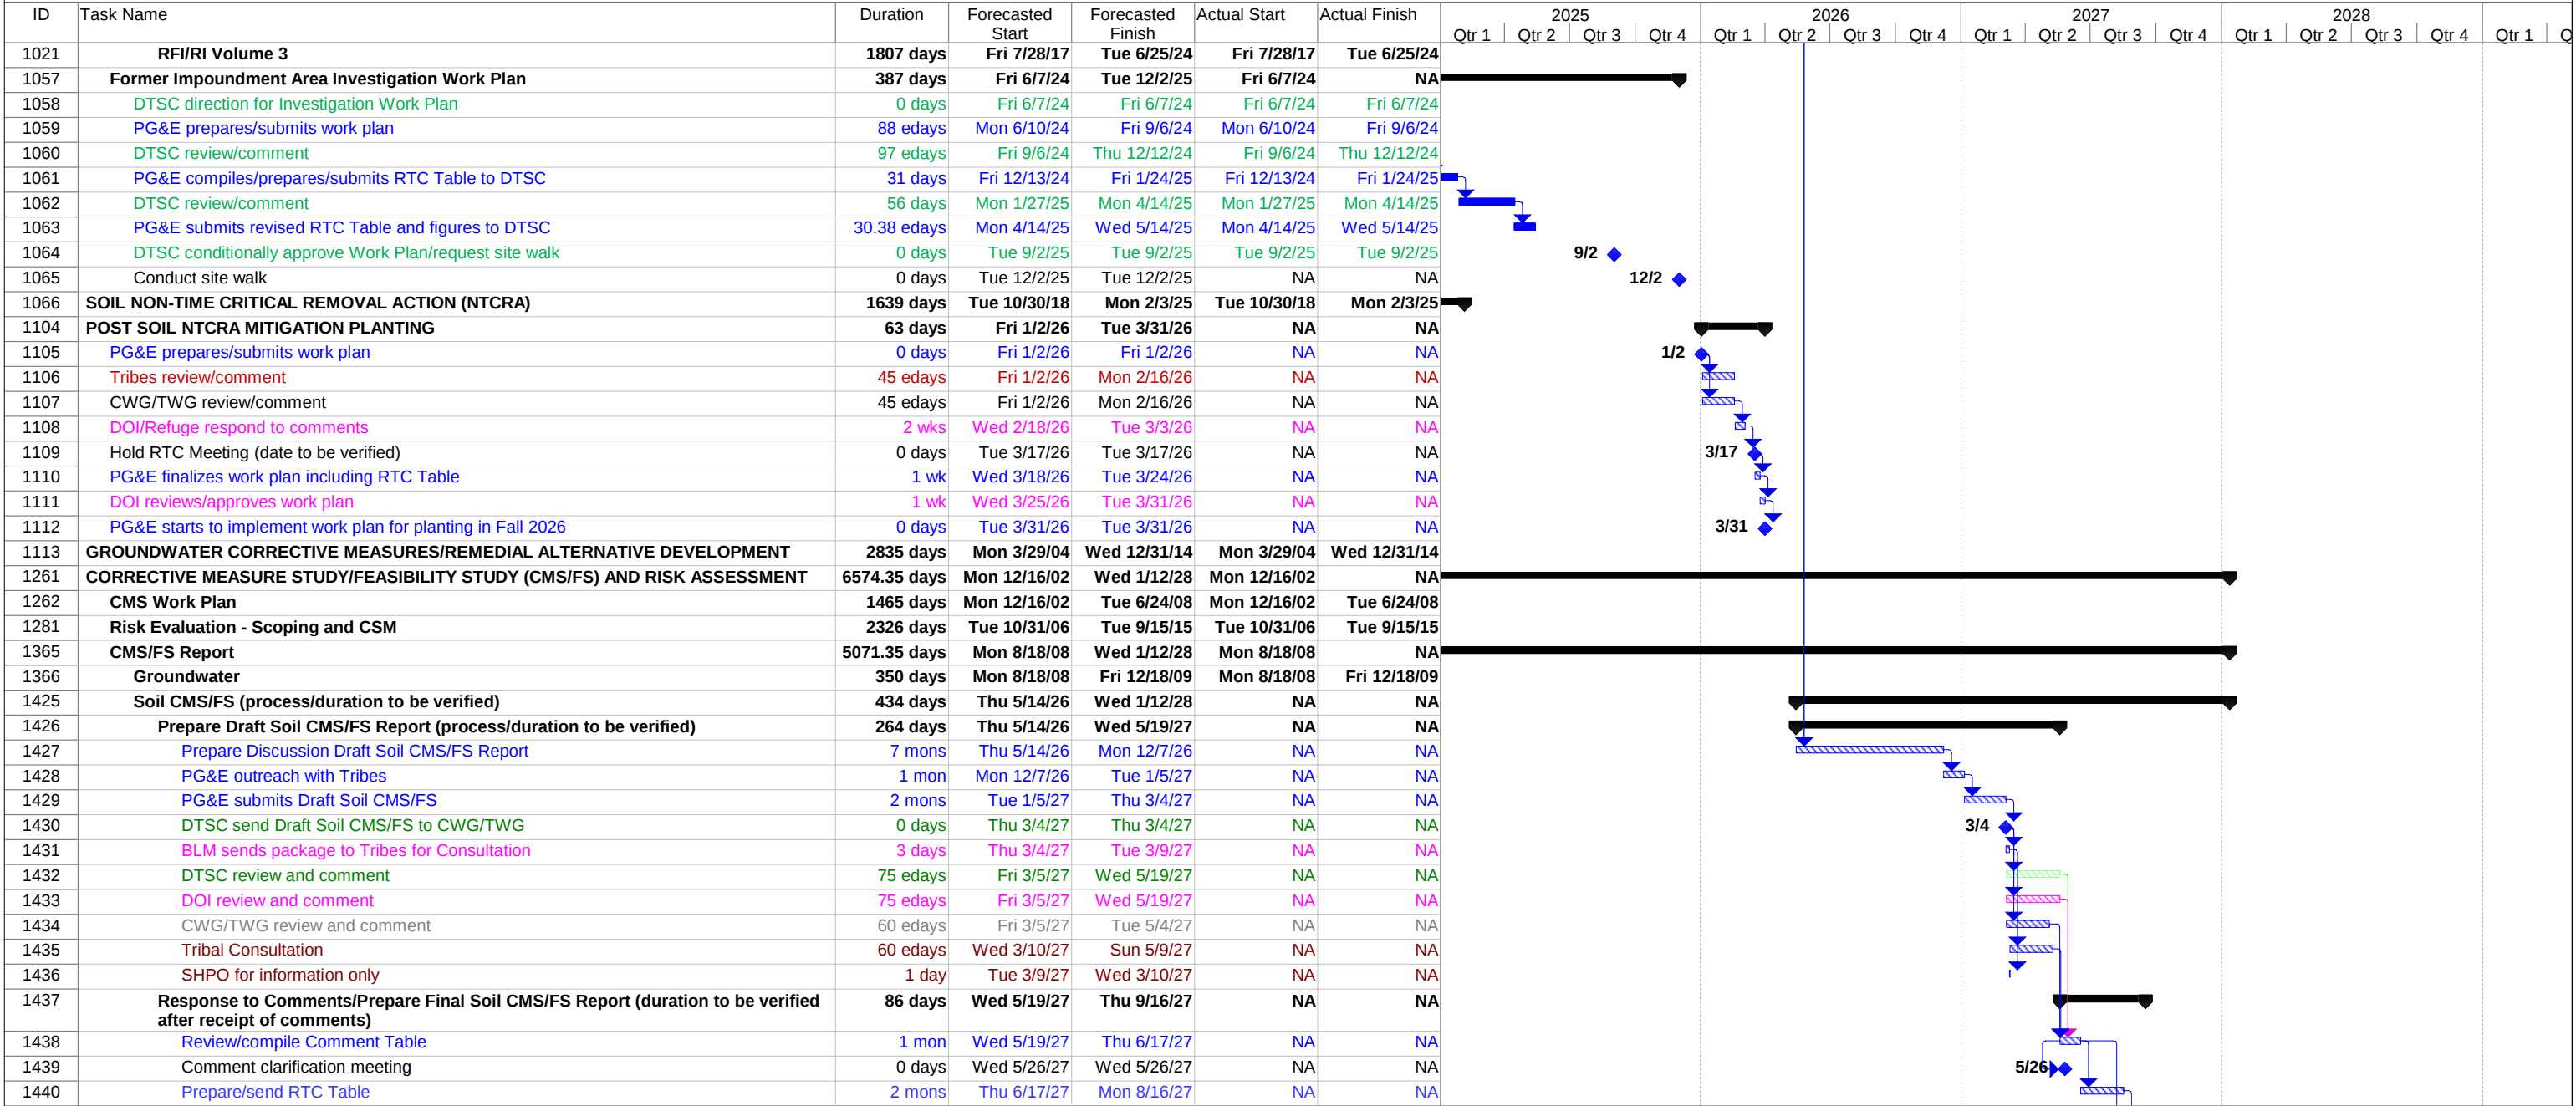

Project: PG&E Topock Remediation Project
Date: Sat 11/15/25

Page 2 of 4

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:

PG&E
DTSC
Federal Agencies
Tribes/SHPO
CWG/TWG
Other CA Agencies
Public
AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 58)
DECEMBER 3, 2025 CWG MEETING

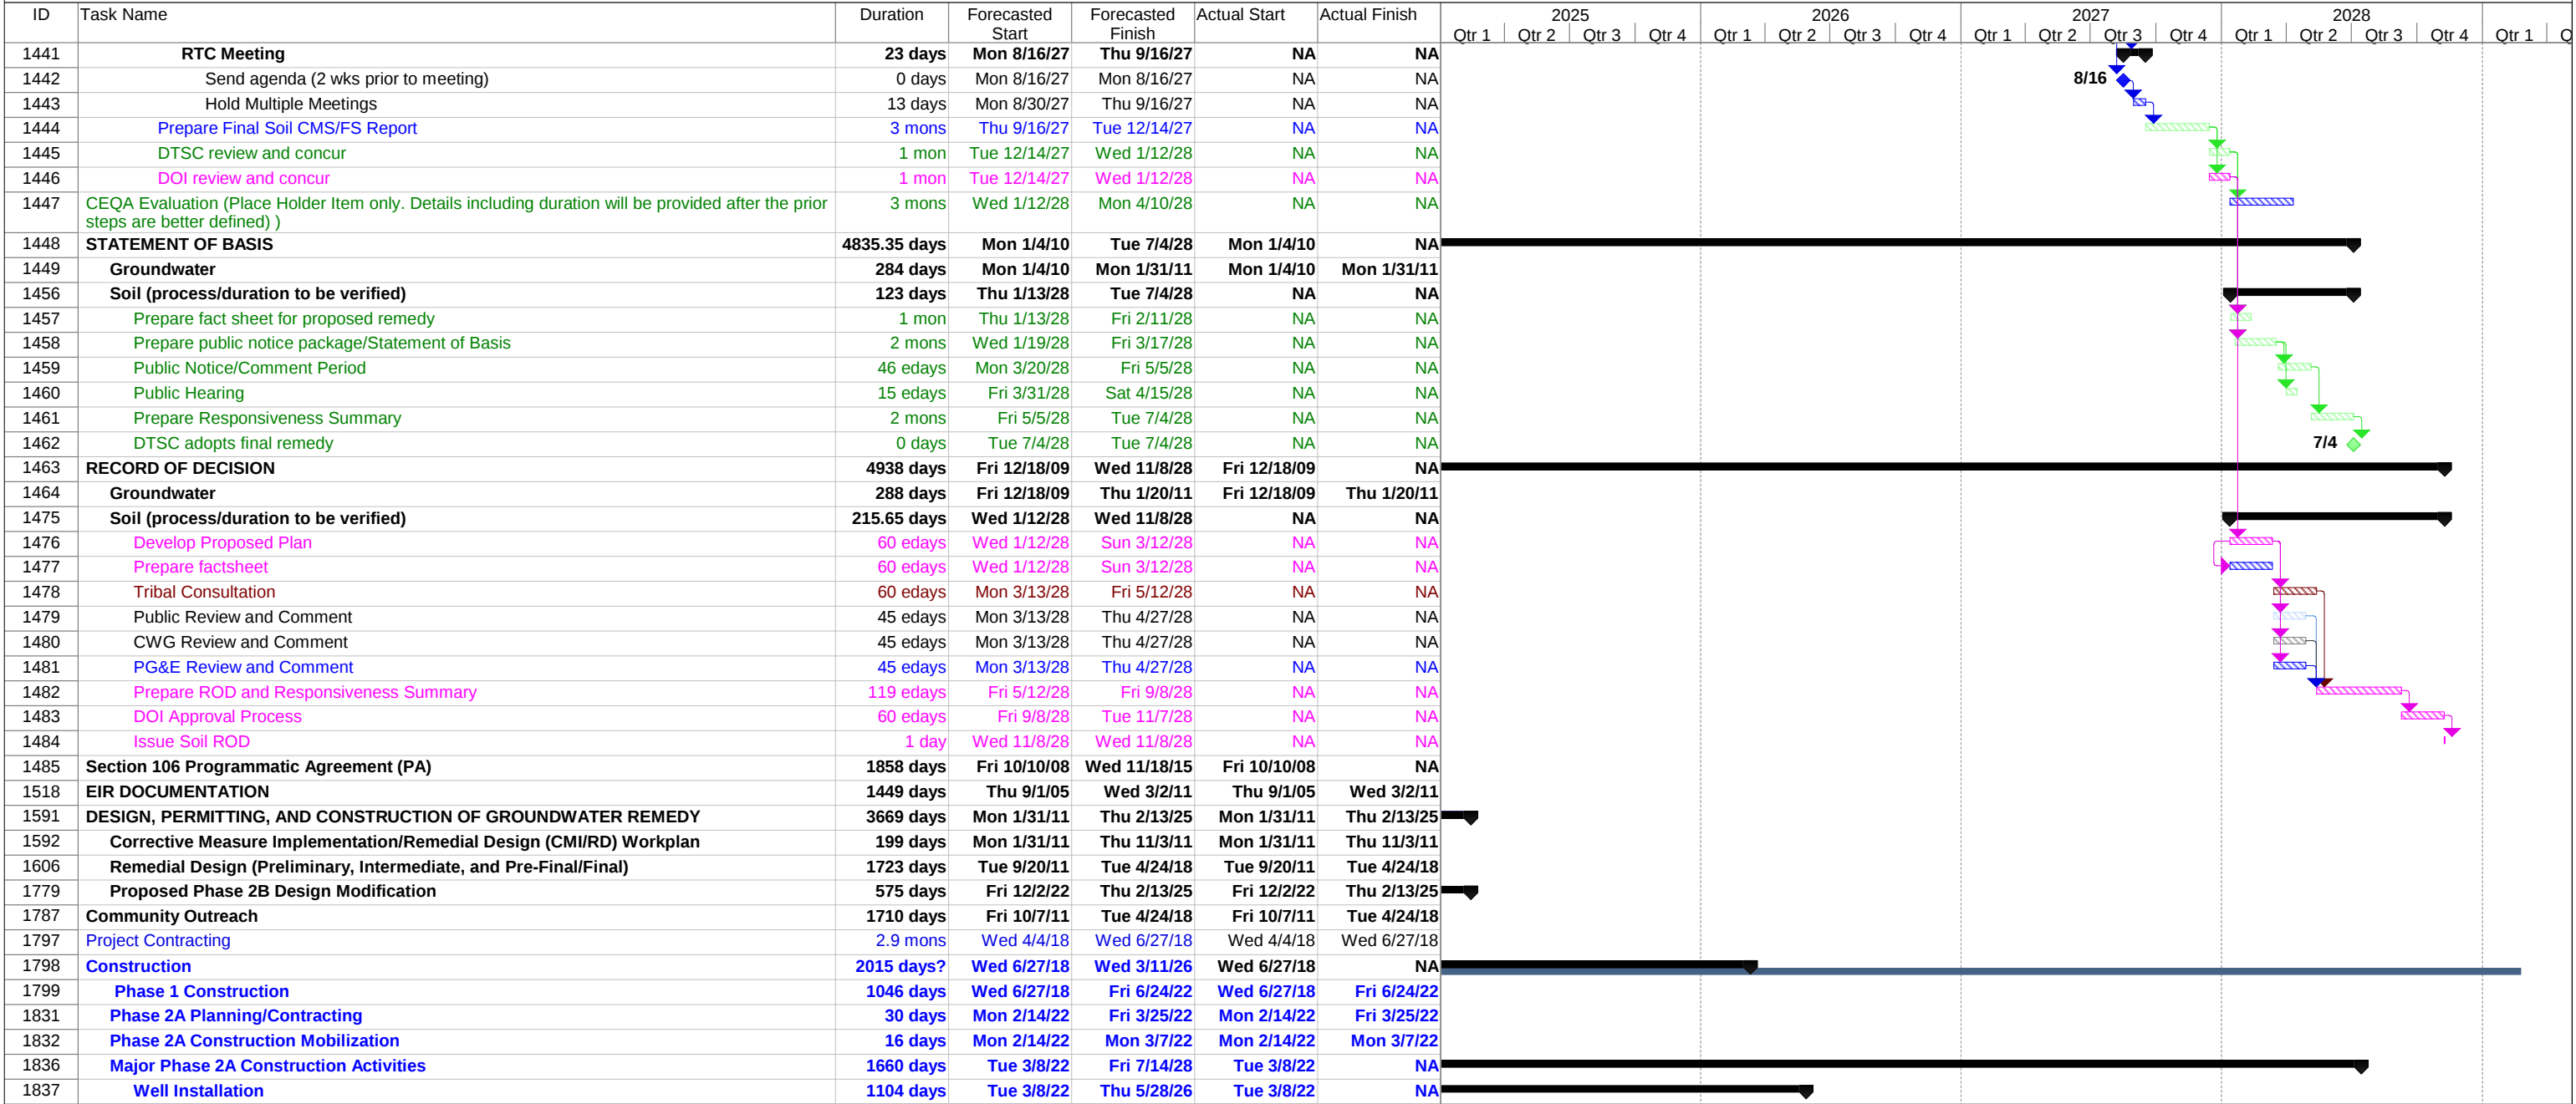

Project: PG&E Topock Remediation Project
Date: Sat 11/15/25

Page 3 of 4

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.


Color Coding:

PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions

- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 58)
DECEMBER 3, 2025 CWG MEETING

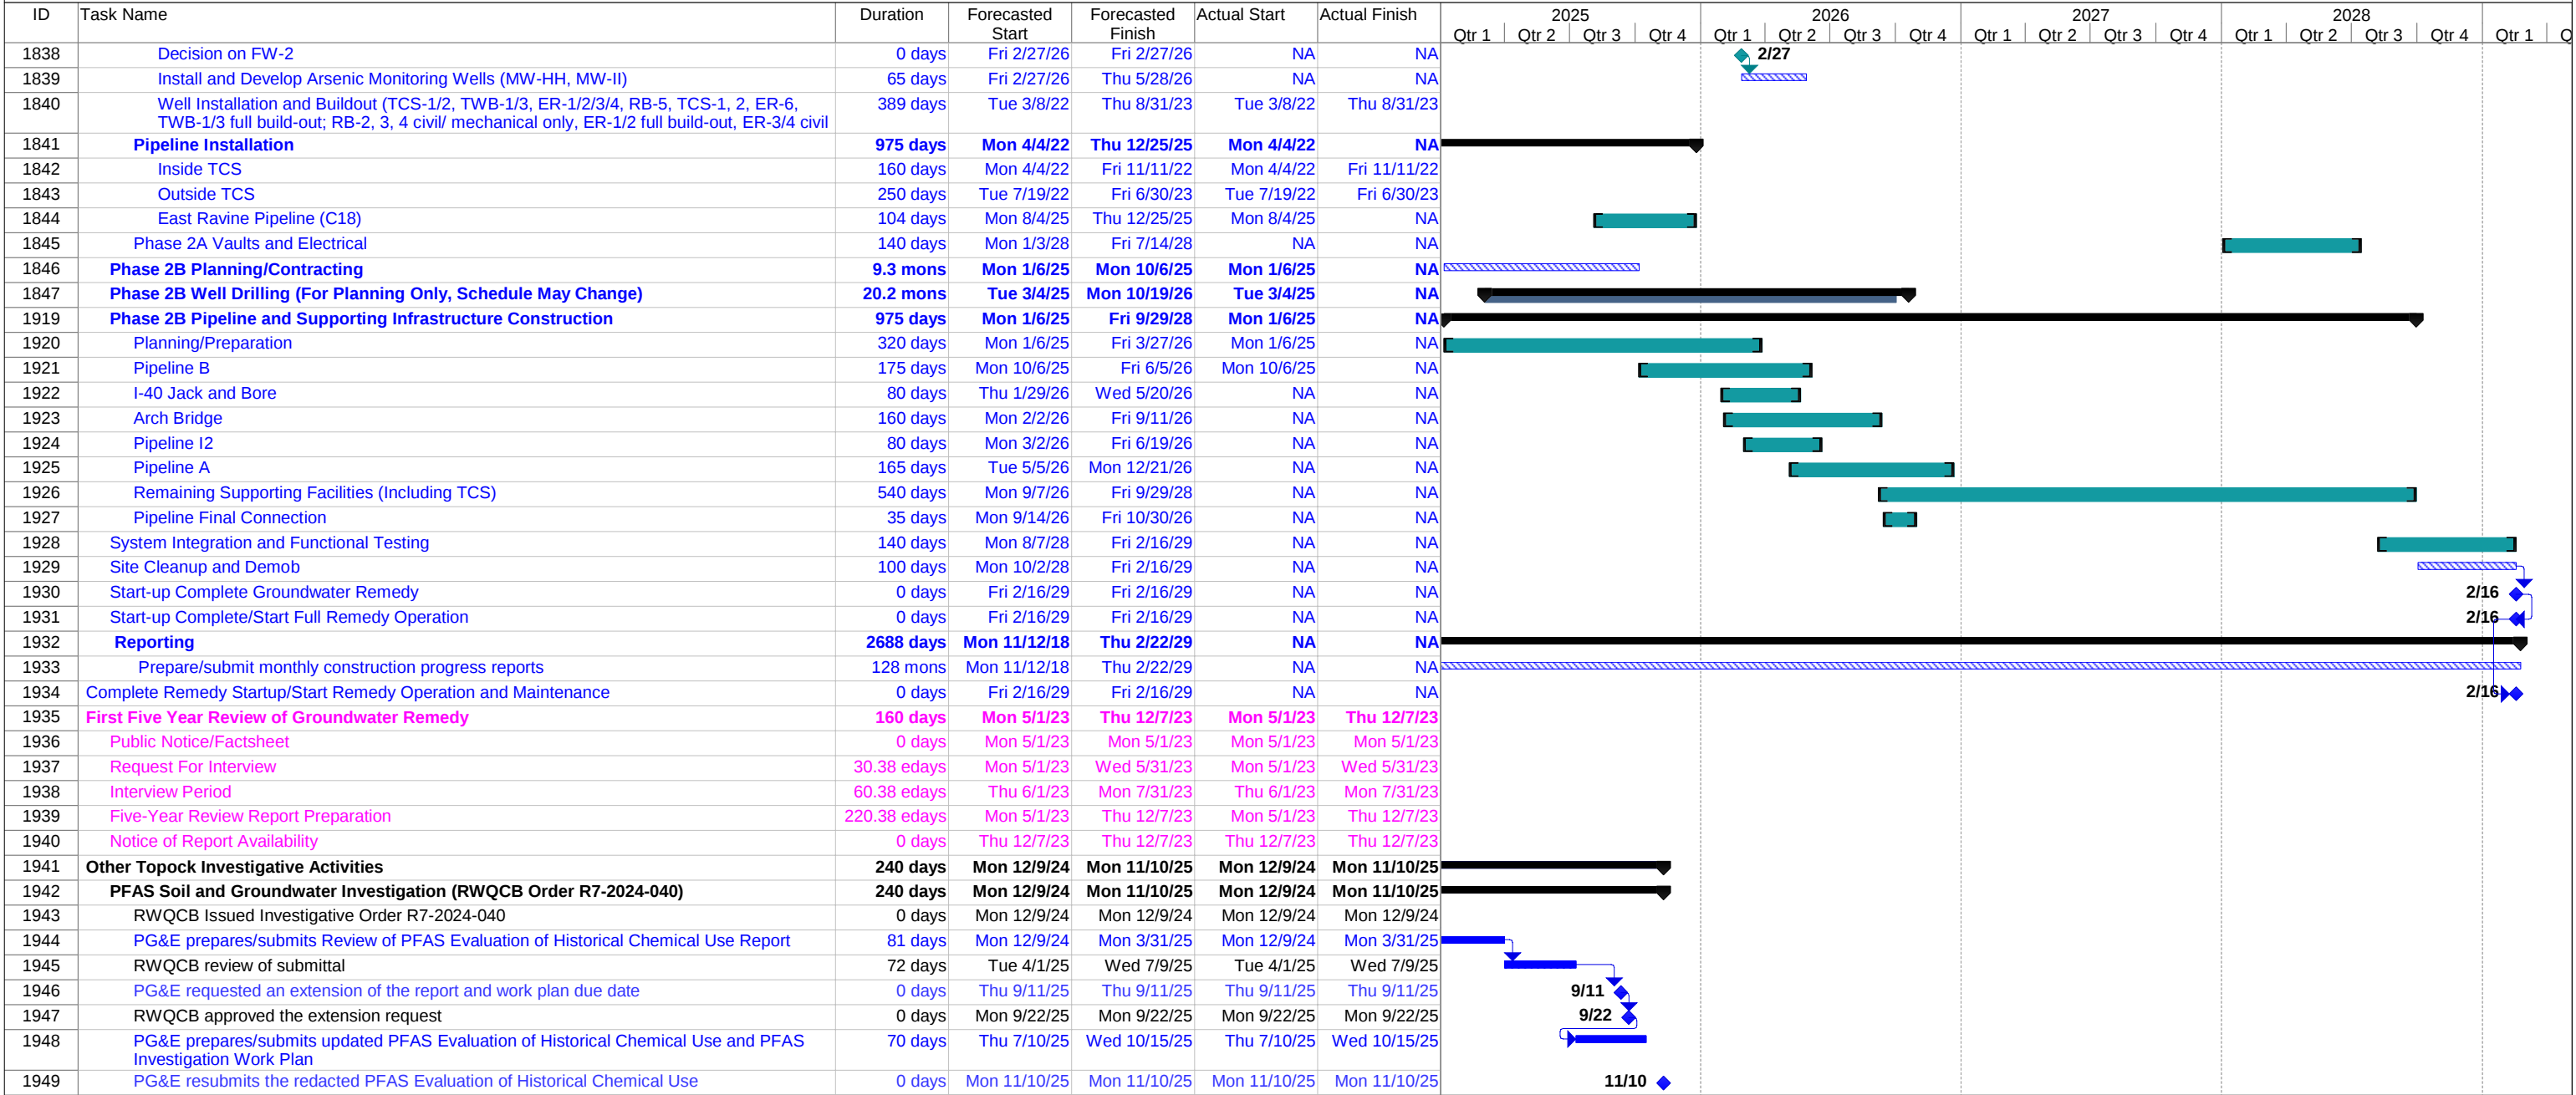

Project: PG&E Topock Remediation Project
Date: Sat 11/15/25

Page 4 of 4

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:

PG&E
Federal Agencies
DTSC
Tribes/SHPO
Other CA Agencies
AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.
