

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 59)  
MARCH 4, 2026 CWG MEETING

| ID   | Task Name                                                                                                                   | Duration     | Forecasted Start | Forecasted Finish | Actual Start | Actual Finish | 2025  |       |       |       | 2026  |       |       |       | 2027  |       |       |       | 2028  |       |       |       | 2029  |       |
|------|-----------------------------------------------------------------------------------------------------------------------------|--------------|------------------|-------------------|--------------|---------------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|
|      |                                                                                                                             |              |                  |                   |              |               | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 |
| 1    | IM Installation (Note that IM3 is currently in operation and will remain in operation until directed otherwise by agencies) | 512 days     | Thu 1/22/04      | Tue 12/20/05      | Thu 1/22/04  | Tue 12/20/05  |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 32   | IM3 Cultural Resources Management Plan (IM3 CRMP)                                                                           | 986 days     | Thu 7/1/04       | Mon 3/10/08       | Thu 7/1/04   | Mon 3/10/08   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 37   | Extraction Well PE-1/Facilities                                                                                             | 230 days     | Mon 3/21/05      | Fri 1/27/06       | Mon 3/21/05  | Fri 1/27/06   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 47   | Supplemental Extraction Well and Facilities                                                                                 | 127 days     | Fri 7/29/05      | Thu 1/19/06       | Fri 7/29/05  | Thu 1/19/06   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 55   | Decommissioning of IM2 Batch Treatment                                                                                      | 1182 days    | Fri 8/5/05       | Fri 1/29/10       | Fri 8/5/05   | Fri 1/29/10   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 66   | Interim Measures and Treated Water Management                                                                               | 751 days     | Mon 5/3/04       | Fri 2/16/07       | Mon 5/3/04   | Fri 2/16/07   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 210  | Public Participation Plan                                                                                                   | 578 days     | Mon 12/20/04     | Fri 2/9/07        | Mon 12/20/04 | Fri 2/9/07    |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 219  | Baseline Resources Assessments                                                                                              | 897 days     | Mon 11/1/04      | Mon 3/10/08       | Mon 11/1/04  | Mon 3/10/08   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 233  | Sitewide CEQA Documentation                                                                                                 | 586 days     | Wed 5/17/06      | Fri 8/1/08        | Wed 5/17/06  | Fri 8/1/08    |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 237  | Programmatic Biological Assessment (PBA)                                                                                    | 1920 days    | Tue 12/19/06     | Tue 4/15/14       | Tue 12/19/06 | Tue 4/15/14   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 250  | REMEDIAL FACILITY INVESTIGATION/REMEDIAL INVESTIGATION (RFI/RI)                                                             | 8080 days    | Sat 2/24/96      | Tue 12/29/26      | Sat 2/24/96  | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 251  | Historical RFI/RI Reports (Feb. 2005 and Prior Versions)                                                                    | 2455 days    | Sat 2/24/96      | Fri 7/8/05        | Sat 2/24/96  | Fri 7/8/05    |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 269  | Site History Report (Vol 1)                                                                                                 | 466 days     | Tue 11/15/05     | Wed 8/15/07       | Tue 11/15/05 | Wed 8/15/07   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 284  | RFI/RI Vol 1 Addendum                                                                                                       | 1829 days    | Wed 7/11/07      | Tue 7/8/14        | Wed 7/11/07  | Tue 7/8/14    |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 306  | Final Groundwater RFI/RI (Vol 2 )                                                                                           | 1948 days    | Mon 6/27/05      | Fri 11/16/12      | Mon 6/27/05  | Fri 11/16/12  |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 616  | ADEQ Topock Groundwater Study                                                                                               | 475 days     | Thu 11/18/04     | Wed 8/23/06       | Thu 11/18/04 | Wed 8/23/06   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 620  | Final Soil RFI/RI (Vol 3)                                                                                                   | 5211 days    | Sat 7/15/06      | Fri 6/12/26       | Sat 7/15/06  | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 621  | Implementation of Off-site Soil Sampling (Part A Phase 1) and Data Gaps Evaluation                                          | 1215 days    | Sat 7/15/06      | Fri 2/25/11       | Sat 7/15/06  | Fri 2/25/11   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 770  | Draft On-site Soil Sampling (Part B) DQOs                                                                                   | 1122 days    | Wed 12/6/06      | Fri 3/11/11       | Wed 12/6/06  | Fri 3/11/11   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 825  | Soil RFI/RI Work Plan                                                                                                       | 1211 days    | Tue 1/4/11       | Mon 8/24/15       | Tue 1/4/11   | Mon 8/24/15   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 922  | Work Plan Implementation/Data Gaps Analysis                                                                                 | 594 days     | Tue 8/25/15      | Thu 11/30/17      | Tue 8/25/15  | Thu 11/30/17  |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 978  | Reporting                                                                                                                   | 2348 days    | Tue 6/20/17      | Fri 6/12/26       | Tue 6/20/17  | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 979  | Soil Risk Assessment                                                                                                        | 770 days     | Tue 6/20/17      | Fri 5/29/20       | Tue 6/20/17  | Fri 5/29/20   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1002 | Soil Post-NTCRA Risk Assessment                                                                                             | 558 days     | Wed 4/24/24      | Fri 6/12/26       | Wed 4/24/24  | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1003 | Validated NTCRA Data Available for Risk Assessment                                                                          | 80 days      | Wed 4/24/24      | Tue 8/13/24       | Wed 4/24/24  | Tue 8/13/24   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1004 | PG&E prepares/submits Soil Post-NTCRA Risk Assessment Report                                                                | 5 mons       | Thu 6/6/24       | Fri 12/13/24      | Thu 6/6/24   | Fri 12/13/24  |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1005 | DTSC review/comment                                                                                                         | 142.38 edays | Mon 12/16/24     | Wed 5/7/25        | Mon 12/16/24 | Wed 5/7/25    |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1006 | DOI review/comment                                                                                                          | 147.38 edays | Mon 12/16/24     | Mon 5/12/25       | Mon 12/16/24 | Mon 5/12/25   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1007 | CWG/TWG review/comment                                                                                                      | 71.38 edays  | Mon 12/16/24     | Tue 2/25/25       | Mon 12/16/24 | Tue 2/25/25   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1008 | Tribes review/comment                                                                                                       | 74.38 edays  | Mon 12/16/24     | Fri 2/28/25       | Mon 12/16/24 | Fri 2/28/25   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1009 | Review/compile Comment Table                                                                                                | 24.38 edays  | Tue 5/13/25      | Fri 6/6/25        | Tue 5/13/25  | Fri 6/6/25    |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1010 | Prepare/send RTC Table                                                                                                      | 60.38 edays  | Fri 6/6/25       | Tue 8/5/25        | Fri 6/6/25   | Tue 8/5/25    |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1011 | Hold RTC Meeting                                                                                                            | 0 days       | Thu 10/9/25      | Thu 10/9/25       | Thu 10/9/25  | Thu 10/9/25   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1012 | Finalize/Submit Draft Soil Post-NTCRA Risk Assessment with RTC Table                                                        | 4.1 mons     | Fri 10/10/25     | Fri 2/6/26        | Fri 10/10/25 | Fri 2/6/26    |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1013 | CWG/TWG review                                                                                                              | 18.38 edays  | Mon 2/9/26       | Fri 2/27/26       | Mon 2/9/26   | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1014 | Tribes review                                                                                                               | 18.38 edays  | Mon 2/9/26       | Fri 2/27/26       | Mon 2/9/26   | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1015 | DTSC review                                                                                                                 | 4 wks        | Mon 2/9/26       | Fri 3/6/26        | Mon 2/9/26   | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1016 | DOI review                                                                                                                  | 4 wks        | Mon 2/9/26       | Fri 3/6/26        | Mon 2/9/26   | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1017 | Meeting to discuss review comments (if needed, date to be confirmed)                                                        | 0 days       | Tue 3/10/26      | Tue 3/10/26       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1018 | Finalize/Submit Final Soil Post-NTCRA Risk Assessment Report with RTC Table                                                 | 47 edays     | Wed 3/11/26      | Mon 4/27/26       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1019 | DTSC review/accept report                                                                                                   | 45 edays     | Tue 4/28/26      | Fri 6/12/26       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1020 | DOI review/accept report                                                                                                    | 45 edays     | Tue 4/28/26      | Fri 6/12/26       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |

Project: PG&E Topock Remediation Project  
Date: Sun 2/22/26

Page 1 of 5

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

edays = calendar days; days = work days  
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).  
\*Timeframes shown are for planning purpose. Actual timeframes may vary.


Color Coding:

PG&E Federal Agencies CWG/TWG Public  
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions

- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.  
- Actual dates may vary depending on field conditions.

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 59)  
MARCH 4, 2026 CWG MEETING

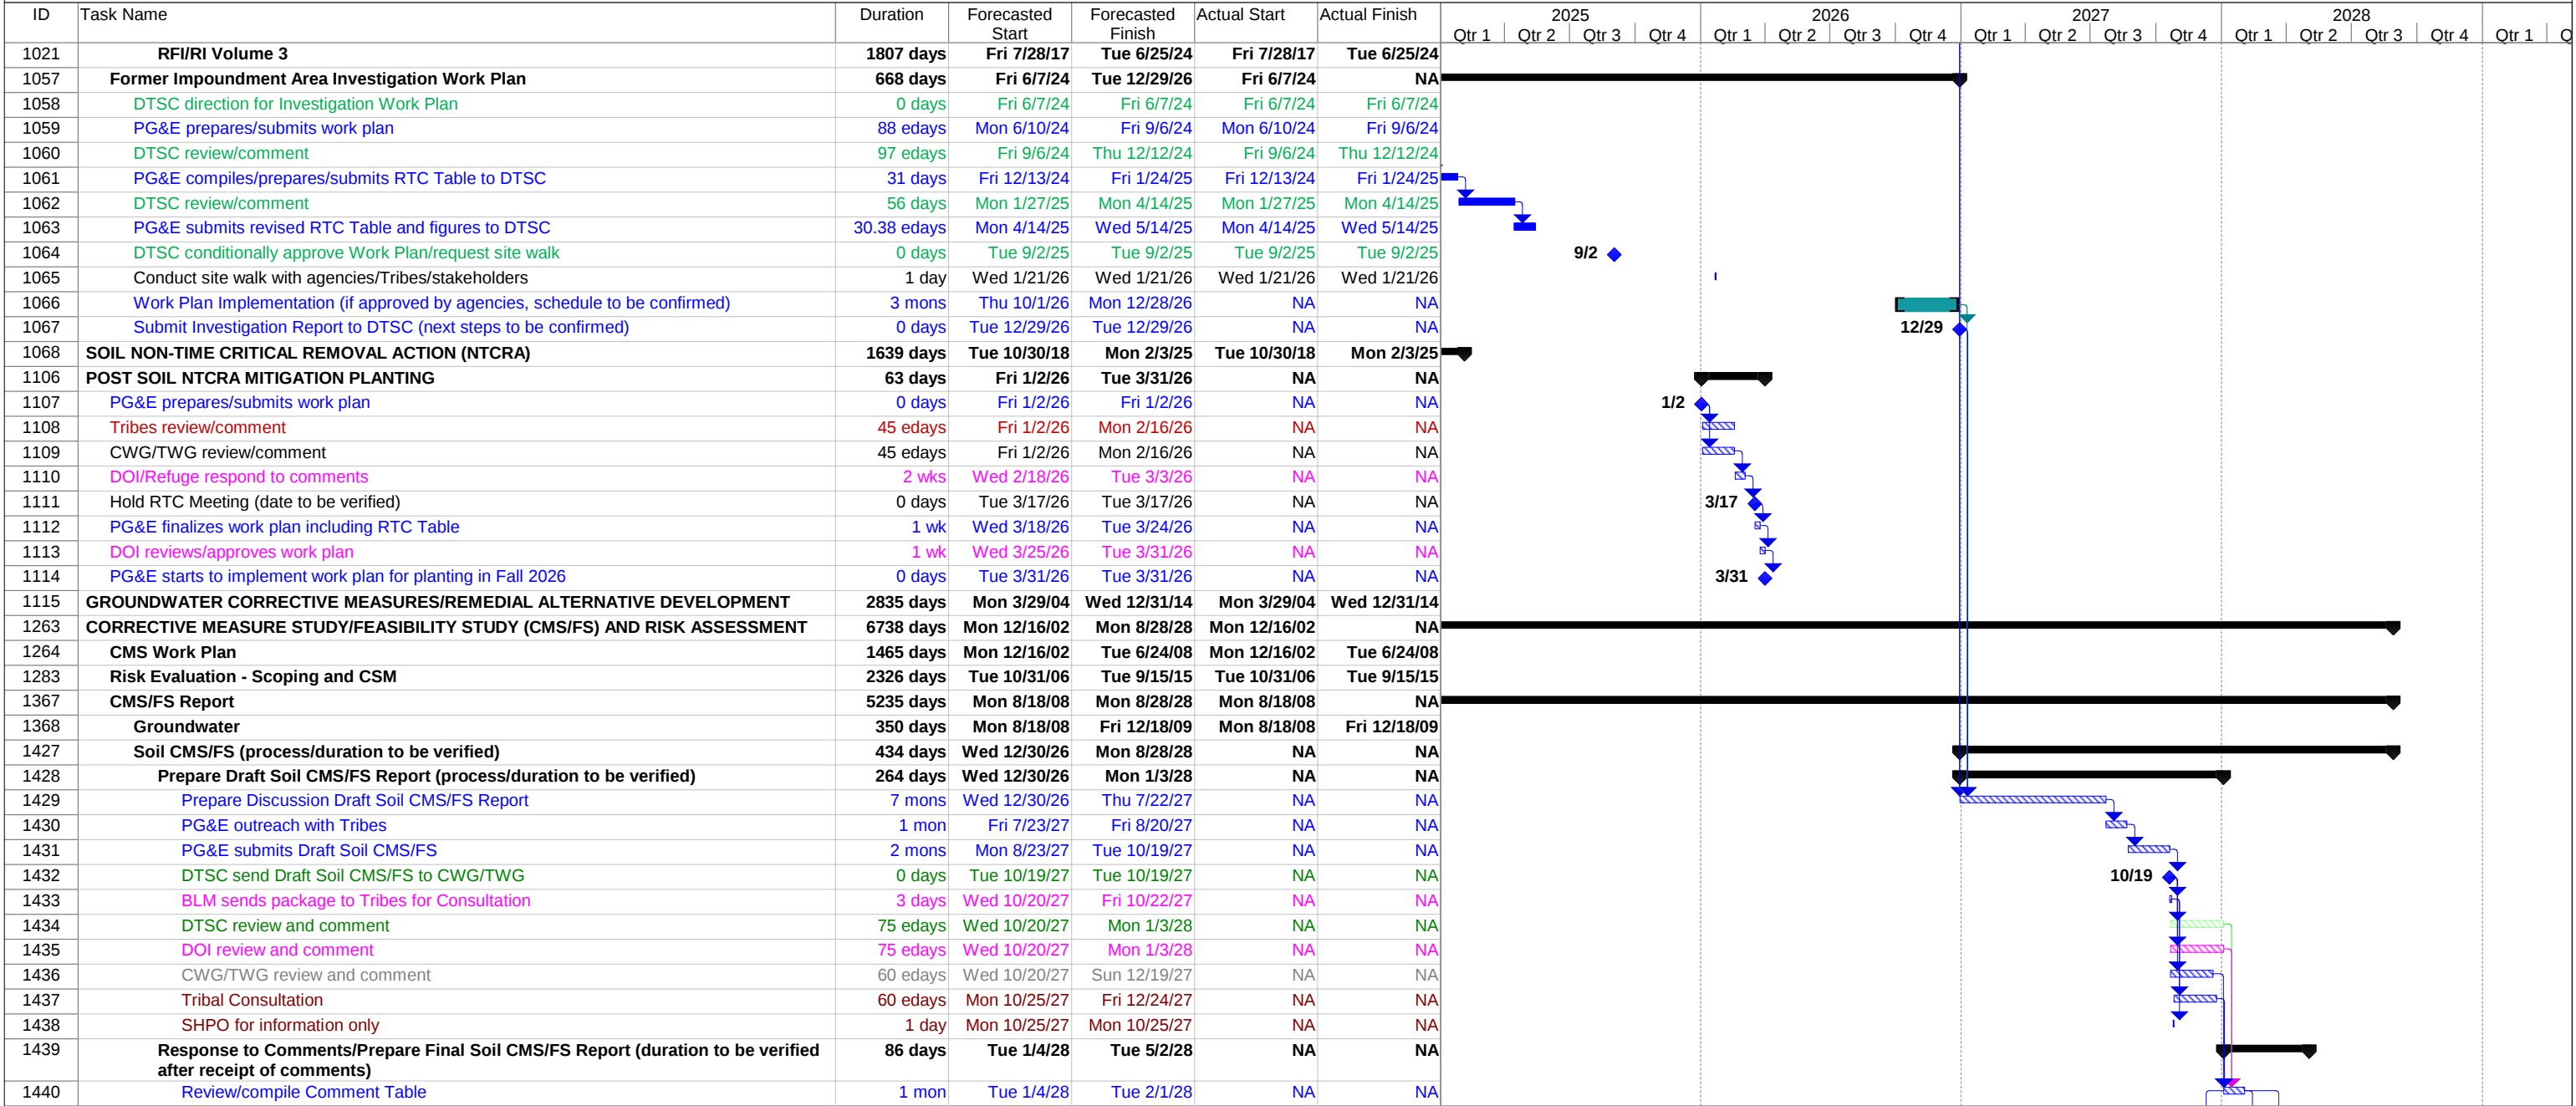

Project: PG&E Topock Remediation Project  
Date: Sun 2/22/26

Page 2 of 5

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

edays = calendar days; days = work days  
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).  
\*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:

PG&E Federal Agencies CWG/TWG Public  
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions

- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.  
- Actual dates may vary depending on field conditions.

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 59)  
MARCH 4, 2026 CWG MEETING

| ID   | Task Name                                                                                                                        | Duration   | Forecasted Start | Forecasted Finish | Actual Start | Actual Finish | 2025  |       |       |       | 2026  |       |       |       | 2027  |       |       |       | 2028  |       |       |       | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 |
|------|----------------------------------------------------------------------------------------------------------------------------------|------------|------------------|-------------------|--------------|---------------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|
|      |                                                                                                                                  |            |                  |                   |              |               | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 |       |       |       |       |
| 1441 | Comment clarification meeting                                                                                                    | 0 days     | Mon 1/10/28      | Mon 1/10/28       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1442 | Prepare/send RTC Table                                                                                                           | 2 mons     | Wed 2/2/28       | Thu 3/30/28       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1443 | RTC Meeting                                                                                                                      | 23 days    | Thu 3/30/28      | Tue 5/2/28        | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1444 | Send agenda (2 wks prior to meeting)                                                                                             | 0 days     | Thu 3/30/28      | Thu 3/30/28       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1445 | Hold Multiple Meetings                                                                                                           | 13 days    | Fri 4/14/28      | Tue 5/2/28        | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1446 | Prepare Final Soil CMS/FS Report                                                                                                 | 3 mons     | Wed 5/3/28       | Fri 7/28/28       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1447 | DTSC review and concur                                                                                                           | 1 mon      | Mon 7/31/28      | Mon 8/28/28       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1448 | DOI review and concur                                                                                                            | 1 mon      | Mon 7/31/28      | Mon 8/28/28       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1449 | CEQA Evaluation (Place Holder Item only. Details including duration will be provided after the prior steps are better defined) ) | 3 mons     | Tue 8/29/28      | Thu 11/23/28      | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1450 | STATEMENT OF BASIS                                                                                                               | 4997 days  | Mon 1/4/10       | Wed 2/14/29       | Mon 1/4/10   | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1451 | Groundwater                                                                                                                      | 284 days   | Mon 1/4/10       | Mon 1/31/11       | Mon 1/4/10   | Mon 1/31/11   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1458 | Soil (process/duration to be verified)                                                                                           | 121 days   | Wed 8/30/28      | Wed 2/14/29       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1459 | Prepare fact sheet for proposed remedy                                                                                           | 1 mon      | Wed 8/30/28      | Wed 9/27/28       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1460 | Prepare public notice package/Statement of Basis                                                                                 | 2 mons     | Tue 9/5/28       | Wed 11/1/28       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1461 | Public Notice/Comment Period                                                                                                     | 46 edays   | Thu 11/2/28      | Mon 12/18/28      | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1462 | Public Hearing                                                                                                                   | 15 edays   | Wed 11/15/28     | Thu 11/30/28      | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1463 | Prepare Responsiveness Summary                                                                                                   | 2 mons     | Tue 12/19/28     | Wed 2/14/29       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1464 | DTSC adopts final remedy                                                                                                         | 0 days     | Wed 2/14/29      | Wed 2/14/29       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1465 | RECORD OF DECISION                                                                                                               | 5103 days  | Fri 12/18/09     | Wed 6/27/29       | Fri 12/18/09 | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1466 | Groundwater                                                                                                                      | 288 days   | Fri 12/18/09     | Thu 1/20/11       | Fri 12/18/09 | Thu 1/20/11   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1477 | Soil (process/duration to be verified)                                                                                           | 217 days   | Mon 8/28/28      | Wed 6/27/29       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1478 | Develop Proposed Plan                                                                                                            | 60 edays   | Mon 8/28/28      | Fri 10/27/28      | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1479 | Prepare factsheet                                                                                                                | 60 edays   | Mon 8/28/28      | Fri 10/27/28      | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1480 | Tribal Consultation                                                                                                              | 60 edays   | Mon 10/30/28     | Fri 12/29/28      | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1481 | Public Review and Comment                                                                                                        | 45 edays   | Mon 10/30/28     | Thu 12/14/28      | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1482 | CWG Review and Comment                                                                                                           | 45 edays   | Mon 10/30/28     | Thu 12/14/28      | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1483 | PG&E Review and Comment                                                                                                          | 45 edays   | Mon 10/30/28     | Thu 12/14/28      | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1484 | Prepare ROD and Responsiveness Summary                                                                                           | 119 edays  | Fri 12/29/28     | Fri 4/27/29       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1485 | DOI Approval Process                                                                                                             | 60 edays   | Fri 4/27/29      | Tue 6/26/29       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1486 | Issue Soil ROD                                                                                                                   | 1 day      | Wed 6/27/29      | Wed 6/27/29       | NA           | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1487 | Section 106 Programmatic Agreement (PA)                                                                                          | 1858 days  | Fri 10/10/08     | Wed 11/18/15      | Fri 10/10/08 | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1520 | EIR DOCUMENTATION                                                                                                                | 1449 days  | Thu 9/1/05       | Wed 3/2/11        | Thu 9/1/05   | Wed 3/2/11    |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1593 | DESIGN, PERMITTING, AND CONSTRUCTION OF GROUNDWATER REMEDY                                                                       | 3669 days  | Mon 1/31/11      | Thu 2/13/25       | Mon 1/31/11  | Thu 2/13/25   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1594 | Corrective Measure Implementation/Remedial Design (CMI/RD) Workplan                                                              | 199 days   | Mon 1/31/11      | Thu 11/3/11       | Mon 1/31/11  | Thu 11/3/11   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1608 | Remedial Design (Preliminary, Intermediate, and Pre-Final/Final)                                                                 | 1723 days  | Tue 9/20/11      | Tue 4/24/18       | Tue 9/20/11  | Tue 4/24/18   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1781 | Proposed Phase 2B Design Modification                                                                                            | 575 days   | Fri 12/2/22      | Thu 2/13/25       | Fri 12/2/22  | Thu 2/13/25   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1789 | Community Outreach                                                                                                               | 1710 days  | Fri 10/7/11      | Tue 4/24/18       | Fri 10/7/11  | Tue 4/24/18   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1799 | Project Contracting                                                                                                              | 2.9 mons   | Wed 4/4/18       | Wed 6/27/18       | Wed 4/4/18   | Wed 6/27/18   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1800 | Construction                                                                                                                     | 2015 days? | Wed 6/27/18      | Wed 3/11/26       | Wed 6/27/18  | NA            |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1801 | Phase 1 Construction                                                                                                             | 1046 days  | Wed 6/27/18      | Fri 6/24/22       | Wed 6/27/18  | Fri 6/24/22   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1833 | Phase 2A Planning/Contracting                                                                                                    | 30 days    | Mon 2/14/22      | Fri 3/25/22       | Mon 2/14/22  | Fri 3/25/22   |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |
| 1834 | Phase 2A Construction Mobilization                                                                                               | 16 days    | Mon 2/14/22      | Mon 3/7/22        | Mon 2/14/22  | Mon 3/7/22    |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |

Project: PG&E Topock Remediation Project  
Date: Sun 2/22/26

Page 3 of 5

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

edays = calendar days; days = work days  
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).  
\*Timeframes shown are for planning purpose. Actual timeframes may vary.


Color Coding:

PG&E  
DTSC  
Federal Agencies  
Tribes/SHPO  
CWG/TWG  
Other CA Agencies  
Public  
AZ Agencies

Major Assumptions

- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.  
- Actual dates may vary depending on field conditions.

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 59)  
MARCH 4, 2026 CWG MEETING

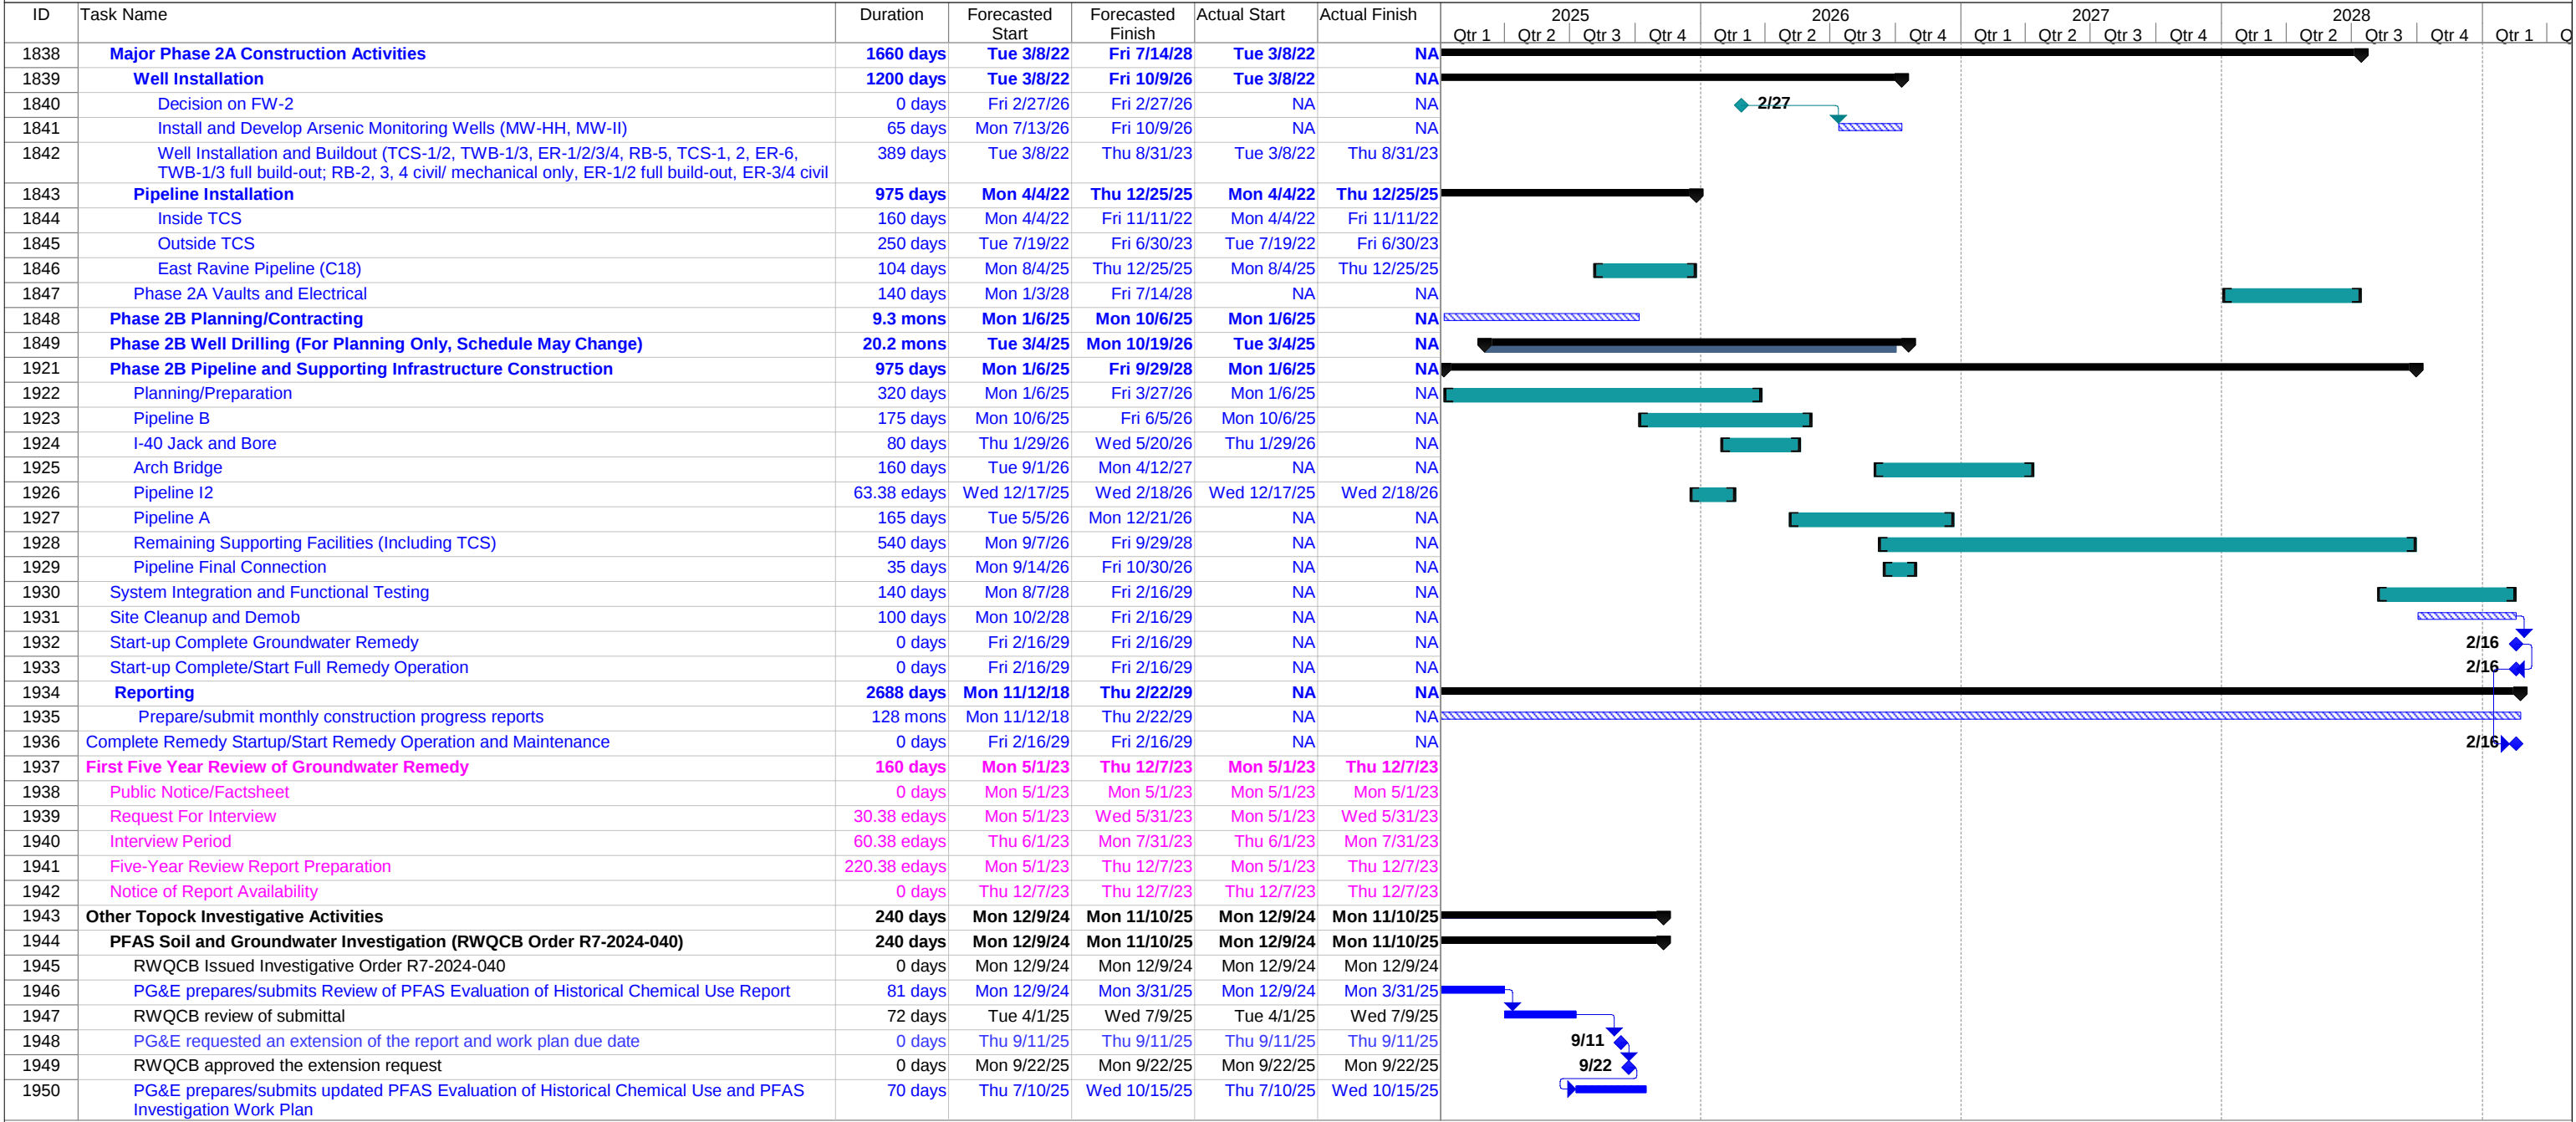

Project: PG&E Topock Remediation Project  
Date: Sun 2/22/26

Page 4 of 5

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

edays = calendar days; days = work days  
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).  
\*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:

PG&E Federal Agencies CWG/TWG Public  
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions

- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.  
- Actual dates may vary depending on field conditions.

HANDOUT 8A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 59)  
MARCH 4, 2026 CWG MEETING

| ID   | Task Name                                                              | Duration | Forecasted Start | Forecasted Finish | Actual Start | Actual Finish | 2025    |       |       |       | 2026  |       |       |       | 2027  |       |       |       | 2028  |       |       |       | Q |
|------|------------------------------------------------------------------------|----------|------------------|-------------------|--------------|---------------|---------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|---|
|      |                                                                        |          |                  |                   |              |               | Qtr 1   | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 | Qtr 1 | Qtr 2 | Qtr 3 | Qtr 4 |   |
| 1951 | PG&E resubmits the redacted PFAS Evaluation of Historical Chemical Use | 0 days   | Mon 11/10/25     | Mon 11/10/25      | Mon 11/10/25 | Mon 11/10/25  | 11/10 ◆ |       |       |       |       |       |       |       |       |       |       |       |       |       |       |       |   |

Project: PG&E Topock Remediation Project

Date: Sun 2/22/26

Page 5 of 5

Tasks Not Started/In Progress

Tasks Finished

Baseline Schedule

Milestone

Overall Task Duration

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

[

]
