HANDOUT 14A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 28)
OCTOBER 28, 2015 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish
1	**IM Installation (Note that IM3 is currently in operation and will remain in operation until directed otherwise by agencies)**	**512 days**	**Thu 1/22/04**	**Tue 12/20/05**	**Thu 1/22/04**	**Tue 12/20/05**
32	**IM3 Cultural Resources Management Plan (IM3 CRMP)**	**986 days**	**Thu 7/1/04**	**Mon 3/10/08**	**Thu 7/1/04**	**Mon 3/10/08**
37	**Extraction Well PE-1/Facilities**	**230 days**	**Mon 3/21/05**	**Fri 1/27/06**	**Mon 3/21/05**	**Fri 1/27/06**
47	**Supplemental Extraction Well and Facilities**	**127 days**	**Fri 7/29/05**	**Thu 1/19/06**	**Fri 7/29/05**	**Thu 1/19/06**
55	**Decommissioning of IM2 Batch Treatment**	**1182 days**	**Fri 8/5/05**	**Fri 1/29/10**	**Fri 8/5/05**	**Fri 1/29/10**
66	**Interim Measures and Treated Water Management**	**751 days**	**Mon 5/3/04**	**Fri 2/16/07**	**Mon 5/3/04**	**Fri 2/16/07**
210	**Public Participation Plan**	**578 days**	**Mon 12/20/04**	**Fri 2/9/07**	**Mon 12/20/04**	**Fri 2/9/07**
219	**Baseline Resources Assessments**	**897 days**	**Mon 11/1/04**	**Mon 3/10/08**	**Mon 11/1/04**	**Mon 3/10/08**
233	**Sitewide CEQA Documentation**	**586 days**	**Wed 5/17/06**	**Fri 8/1/08**	**Wed 5/17/06**	**Fri 8/1/08**
237	**Programmatic Biological Assessment (PBA)**	**1920 days**	**Tue 12/19/06**	**Tue 4/15/14**	**Tue 12/19/06**	**Tue 4/15/14**
250	**REMEDIAL FACILITY INVESTIGATION/REMEDIAL INVESTIGATION (RFI/RI)**	**5502 days**	**Sat 2/24/96**	**Thu 2/16/17**	**Sat 2/24/96**	**NA**
251	**Historical RFI/RI Reports (Feb. 2005 and Prior Versions)**	**2455 days**	**Sat 2/24/96**	**Fri 7/8/05**	**Sat 2/24/96**	**Fri 7/8/05**
269	**Prepare Site History Report (Vol 1)**	**466 days**	**Tue 11/15/05**	**Wed 8/15/07**	**Tue 11/15/05**	**Wed 8/15/07**
284	**Prepare RFI/RI Vol 1 Addendum**	**1829 days**	**Wed 7/11/07**	**Tue 7/8/14**	**Wed 7/11/07**	**Tue 7/8/14**
306	**Prepare Final Groundwater RFI/RI (Vol 2)**	**1948 days**	**Mon 6/27/05**	**Fri 11/16/12**	**Mon 6/27/05**	**Fri 11/16/12**
616	**ADEQ Topock Groundwater Study**	**475 days**	**Thu 11/18/04**	**Wed 8/23/06**	**Thu 11/18/04**	**Wed 8/23/06**
620	**Prepare Final Soil RFI/RI (Vol 3)**	**2775 days**	**Sat 7/15/06**	**Thu 2/16/17**	**Sat 7/15/06**	**NA**
621	**Implementation of Off-site Soil Sampling (Part A Phase 1) and Data Gaps Evaluation**	**1215 days**	**Sat 7/15/06**	**Fri 2/25/11**	**Sat 7/15/06**	**Fri 2/25/11**
770	**Draft On-site Soil Sampling (Part B) DQOs**	**1122 days**	**Wed 12/6/06**	**Fri 3/11/11**	**Wed 12/6/06**	**Fri 3/11/11**
825	**Soil RFI/RI Work Plan**	**1211 days**	**Tue 1/4/11**	**Mon 8/24/15**	**Tue 1/4/11**	**Mon 8/24/15**
922	**Work Plan Implementation/Data Gaps Analysis**	**136 days**	**Tue 8/25/15**	**Tue 3/1/16**	**Tue 8/25/15**	**NA**
923	Stakeholder Attending Kick-Off Meeting at Site*	0 days	Thu 10/29/15	Thu 10/29/15	NA	NA
924	Stakeholder Attending Kick-Off Meeting at Site*	0 days	Thu 10/29/15	Thu 10/29/15	NA	NA
925	Stakeholder Attending Kick-Off Meeting at Site*	0 days	Thu 10/29/15	Thu 10/29/15	NA	NA
926	Stakeholder Attending Kick-Off Meeting at Site*	0 days	Thu 10/29/15	Thu 10/29/15	NA	NA
927	Stakeholder Attending Kick-Off Meeting at Site*	0 days	Thu 10/29/15	Thu 10/29/15	NA	NA
928	Permitting/Access Agreements	65 days	Tue 8/25/15	Mon 11/23/15	Tue 8/25/15	NA
929	**Field Implementation (field duration is for planning purpose only and is subject to change)**	**86 days**	**Tue 11/3/15**	**Tue 3/1/16**	**NA**	**NA**
930	Surveys	83 days	Tue 11/3/15	Thu 2/25/16	NA	NA
931	Sample Location Access	27 days	Tue 11/3/15	Wed 12/9/15	NA	NA
932	Sample Collection	67 days	Mon 11/30/15	Tue 3/1/16	NA	NA
933	Data Gaps Analysis and Coordination	83 days	Mon 12/21/15	Wed 4/13/16	NA	NA
934	Final Determination that Additional Data Collection is Not Requried	0 days	Wed 4/13/16	Wed 4/13/16	NA	NA
935	**Reporting (RFI/RI Volume 3)**	**222 days**	**Wed 4/13/16**	**Thu 2/16/17**	**NA**	**NA**
936	Prepare Draft RFI/RI Vol 3 Report	3.1 mons	Wed 4/13/16	Wed 7/13/16	NA	NA
937	DTSC sends report to CWG/TWG and Tribes	3 days	Wed 7/13/16	Mon 7/18/16	NA	NA
938	CWG/TWG review/comment	31 edays	Mon 7/18/16	Thu 8/18/16	NA	NA
939	Tribes review/comment	31 edays	Mon 7/18/16	Thu 8/18/16	NA	NA
940	DTSC review/comment/provide direction to PG&E	45 edays	Mon 7/18/16	Thu 9/1/16	NA	NA
941	DOI review/comment/provide direction to PG&E	45 edays	Mon 7/18/16	Thu 9/1/16	NA	NA
942	Prepare RTCs (duration is estimated, to be verified after receipt of comments and direction)	32 edays	Thu 9/1/16	Mon 10/3/16	NA	NA
943	CWG/TWG review/comment	30 edays	Mon 10/3/16	Wed 11/2/16	NA	NA
944	Tribes review/comemnt	30 edays	Mon 10/3/16	Wed 11/2/16	NA	NA
945	DOI review/comment	47 edays	Mon 10/3/16	Sat 11/19/16	NA	NA
946	DTSC review/comment	47 edays	Mon 10/3/16	Sat 11/19/16	NA	NA

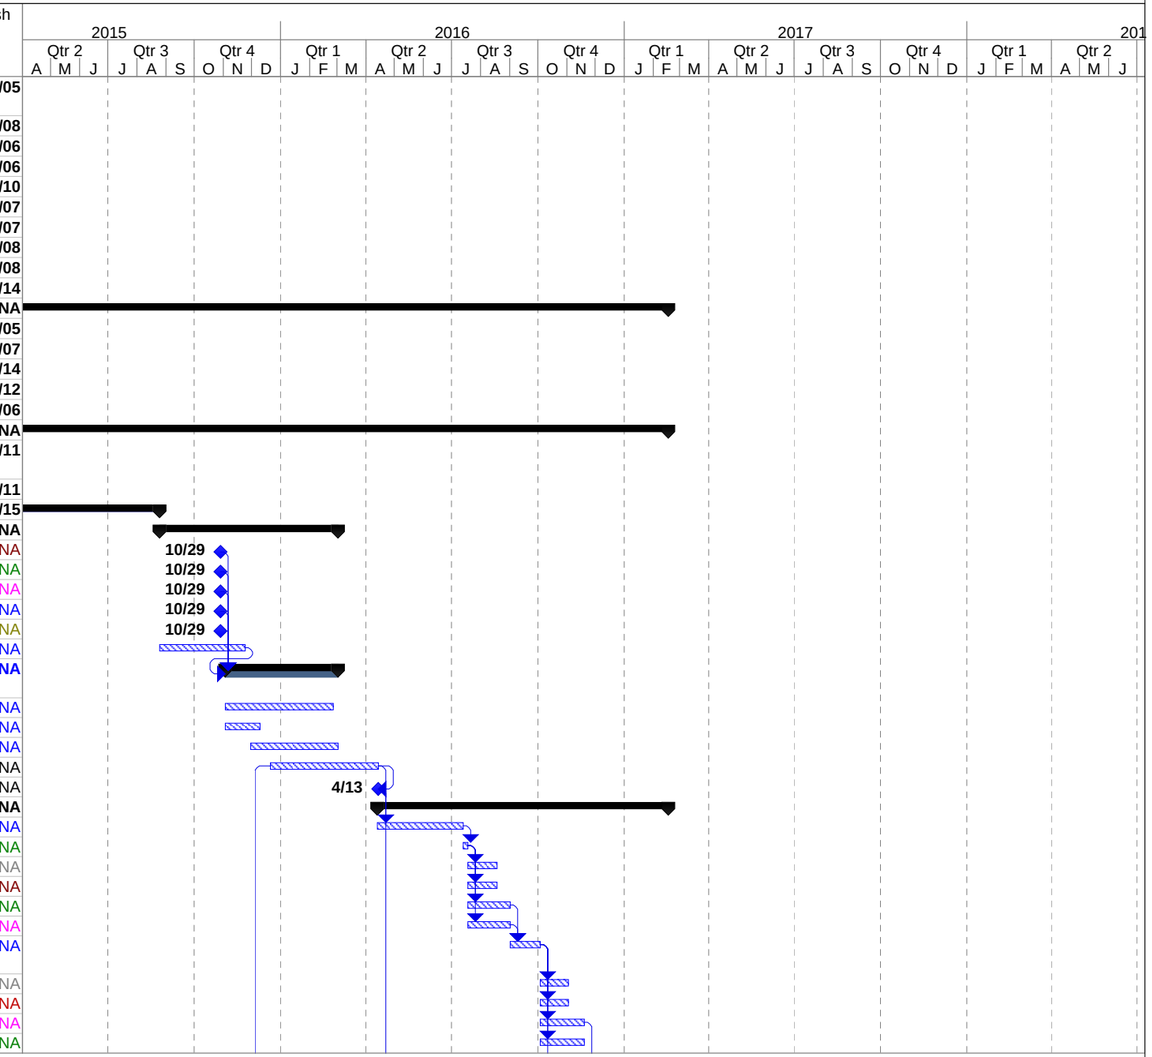

Project: PG&E Topock Remediation Project
Date: Fri 10/23/15

Tasks Not Started/In Progess
Tasks Finished
Baseline Schedule
Milestone
Overall Task Duration
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 14A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 28)
OCTOBER 28, 2015 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish
947	Meeting to discuss RTCs (approx. 2 wks after review by CWG/ TWG/Tribes/ Agencies)	0 days	Mon 10/17/16	Mon 10/17/16	NA	NA
948	Prepare Revised RFI Volume 3 (duration is estimated, to be verified after completion of RTCs)	2 mons	Tue 11/22/16	Wed 1/18/17	NA	NA
949	DTSC review/approve Revised RFI/RI Vol. 3	4 wks	Fri 1/20/17	Thu 2/16/17	NA	NA
950	DOI review/approve Revised RFI/RI Vol. 3 Report	4 wks	Fri 1/20/17	Thu 2/16/17	NA	NA
951	**CORRECTIVE MEASURES/REMEDIAL ALTERNATIVE DEVELOPMENT**	**1527 days**	**Mon 3/29/04**	**Thu 12/31/09**	**Mon 3/29/04**	**NA**
1099	**CORRECTIVE MEASURE STUDY/FEASIBILITY STUDY (CMS/FS) AND RISK ASSESSMENT**	**4022 days**	**Mon 12/16/02**	**Fri 4/6/18**	**Mon 12/16/02**	**NA**
1100	**CMS Work Plan**	**1465 days**	**Mon 12/16/02**	**Tue 6/24/08**	**Mon 12/16/02**	**Tue 6/24/08**
1119	**Risk Evaluation - Scoping and CSM**	**2764.5 days**	**Tue 10/31/06**	**Mon 5/22/17**	**Tue 10/31/06**	**NA**
1120	Soil Land Use and Pathway Analysis before Nov. 2007 Group Meeting	265 days	Tue 10/31/06	Fri 10/26/07	Tue 10/31/06	Fri 10/26/07
1121	**Scoping for Ecological Risk Assessment Work Plan**	**282 days**	**Mon 1/22/07**	**Fri 2/15/08**	**Mon 1/22/07**	**Fri 2/15/08**
1131	**Soil/Groundwater Risk Assessment Workplan (RAWP)**	**2061 days**	**Mon 10/29/07**	**Tue 9/15/15**	**Mon 10/29/07**	**Tue 9/15/15**
1132	**RAWP**	**334 days**	**Mon 10/29/07**	**Thu 2/5/09**	**Mon 10/29/07**	**Thu 2/5/09**
1158	**RAWP Addendum II**	**688 days**	**Fri 1/25/13**	**Tue 9/15/15**	**Fri 1/25/13**	**Tue 9/15/15**
1186	**Groundwater Evaluation**	**330 days**	**Wed 9/10/08**	**Tue 12/15/09**	**Wed 9/10/08**	**Tue 12/15/09**
1203	**Soil Evaluation**	**370.5 days**	**Mon 12/21/15**	**Mon 5/22/17**	**NA**	**NA**
1204	Prepare/Submit Draft Soil Risk Assessment Report	41 wks	Mon 12/21/15	Fri 9/30/16	NA	NA
1205	Calculate Exposure Point Concentrations (EPCs)	3 mons	Thu 4/14/16	Mon 7/11/16	NA	NA
1206	Meeting to discuss EPCs	0 days	Tue 6/28/16	Tue 6/28/16	NA	NA
1207	DTSC send Soil Risk Evaluation to CWG/TWG	3 days	Mon 10/3/16	Wed 10/5/16	NA	NA
1208	DTSC review/comment	46 edays	Thu 10/6/16	Mon 11/21/16	NA	NA
1209	DOI review/comment	46 edays	Thu 10/6/16	Mon 11/21/16	NA	NA
1210	CWG/TWG review/comment	32 edays	Thu 10/6/16	Mon 11/7/16	NA	NA
1211	Tribes review/comment	32 edays	Thu 10/6/16	Mon 11/7/16	NA	NA
1212	Prepare Response to Comments	1 mon	Tue 11/22/16	Tue 12/20/16	NA	NA
1213	DTSC review/comment	47 edays	Wed 12/21/16	Mon 2/6/17	NA	NA
1214	DOI review/comment	47 edays	Wed 12/21/16	Mon 2/6/17	NA	NA
1215	CWG/TWG review/comment	30 edays	Wed 12/21/16	Fri 1/20/17	NA	NA
1216	Tribal review/comment	30 edays	Wed 12/21/16	Fri 1/20/17	NA	NA
1217	Meeting to discuss response to comments (approx. 2 wks after review by CWG/TWG/Tribes/ Agencies)	0 days	Tue 1/10/17	Tue 1/10/17	NA	NA
1218	Finalize/Submit Soil Risk Assessment Report	2.5 mons	Tue 2/7/17	Thu 4/20/17	NA	NA
1219	DTSC review/approve	1 mon	Fri 4/21/17	Mon 5/22/17	NA	NA
1220	DOI review/approve	1 mon	Fri 4/21/17	Mon 5/22/17	NA	NA
1221	**CMS/FS Report**	**2519 days**	**Mon 8/18/08**	**Fri 4/6/18**	**Mon 8/18/08**	**NA**
1299	**STATEMENT OF BASIS**	**2267.6 days**	**Mon 1/4/10**	**Thu 9/6/18**	**Mon 1/4/10**	**NA**
1314	**RECORD OF DECISION**	**2368 days**	**Fri 12/18/09**	**Wed 1/9/19**	**Fri 12/18/09**	**NA**
1337	**Section 106 Programmatic Agreement (PA)**	**1858 days**	**Fri 10/10/08**	**Wed 11/18/15**	**Fri 10/10/08**	**NA**
1370	**EIR DOCUMENTATION**	**1449 days**	**Thu 9/1/05**	**Wed 3/2/11**	**Thu 9/1/05**	**Wed 3/2/11**
1443	**DESIGN, PERMITTING, AND CONSTRUCTION OF GROUNDWATER REMEDY**	**1599.5 days**	**Mon 1/31/11**	**Thu 3/16/17**	**Mon 1/31/11**	**NA**
1444	**Corrective Measure Implementation/Remedial Design (CMI/RD) Workplan**	**199 days**	**Mon 1/31/11**	**Thu 11/3/11**	**Mon 1/31/11**	**NA**
1458	**Remedial Design (Preliminary, Intermediate, and Pre-Final/Final)**	**1088 days**	**Tue 9/20/11**	**Wed 11/18/15**	**Tue 9/20/11**	**NA**
1459	**Preliminary Design**	**174 days**	**Tue 9/20/11**	**Thu 5/17/12**	**Tue 9/20/11**	**Thu 5/17/12**
1471	**Intermediate Design**	**501 days**	**Fri 5/18/12**	**Fri 4/18/14**	**Fri 5/18/12**	**Fri 4/18/14**
1500	**Implementation Plan for Evaluation of Alternative Freshwater Sources**	**422 days**	**Fri 11/16/12**	**Mon 6/30/14**	**Fri 11/16/12**	**Mon 6/30/14**
1539	Field Verification of Archaeological/Historical Sites in Groundwater Remedy Footprint	4 days	Tue 9/9/14	Fri 9/12/14	Tue 9/9/14	Fri 9/12/14
1540	Prepare/submit Field Verification Report	28 days	Mon 9/15/14	Wed 10/22/14	Mon 9/15/14	Wed 10/22/14
1541	Survey of Archaelogical/Historical Sites in Expanded Area at Park Moabi	1 day	Tue 12/2/14	Tue 12/2/14	Tue 12/2/14	Tue 12/2/14

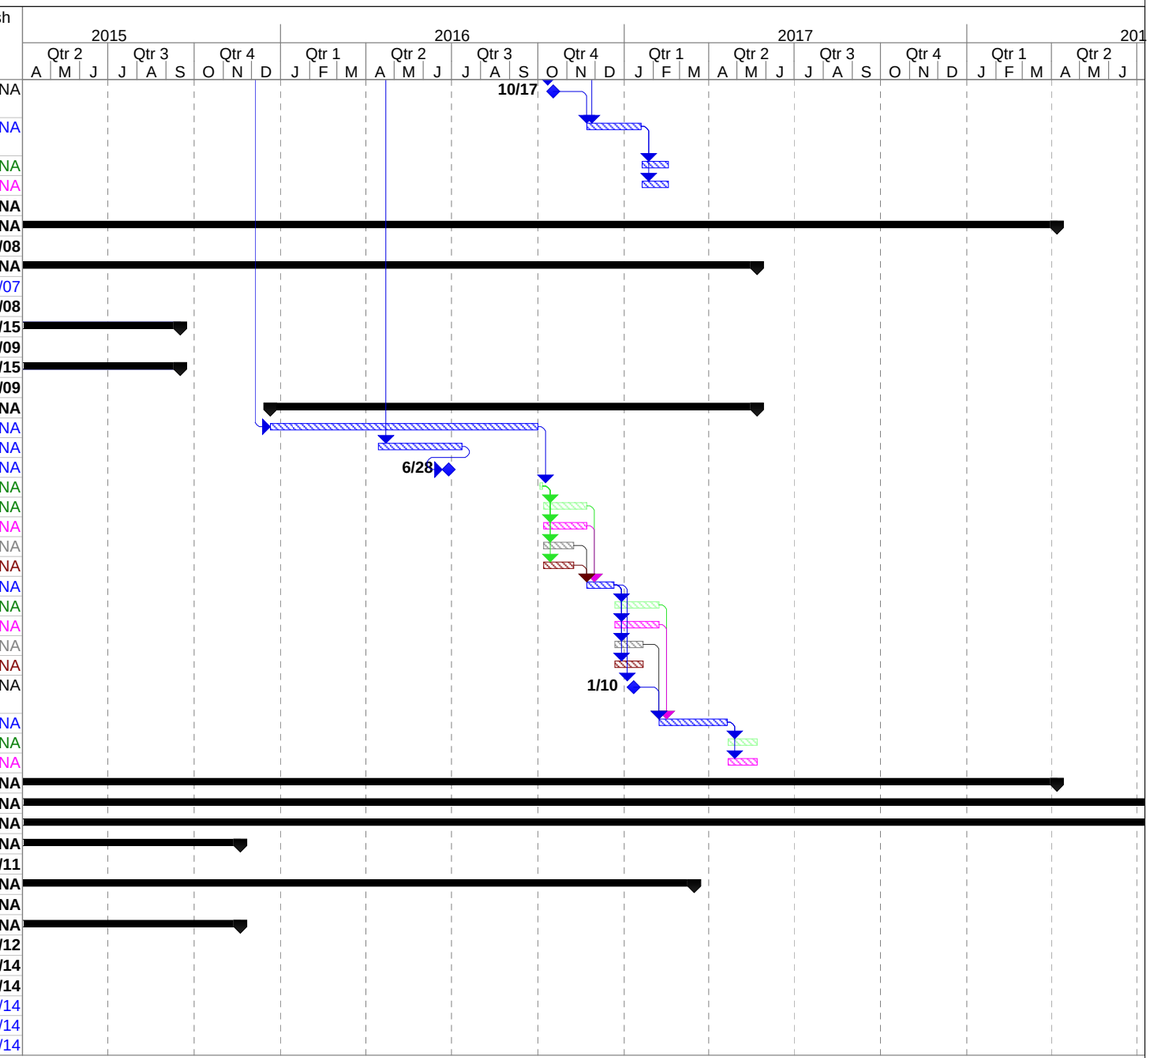

Project: PG&E Topock Remediation Project
Date: Fri 10/23/15

Tasks Not Started/In Progess
Tasks Finished
Baseline Schedule
Milestone
Overall Task Duration
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 14A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 28)
OCTOBER 28, 2015 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish
1542	Survey of Biological Resources in Expanded Area at Park Moabi	3 days	Wed 11/19/14	Fri 11/21/14	Wed 11/19/14	Fri 11/21/14
1543	Annual archeological monitoring and site condition assessments	7 days	Thu 12/11/14	Fri 12/19/14	Thu 12/11/14	Fri 12/19/14
1544	**Pre-Final/Final Design (include plan for decommissioning, removal, and restoration of IM3 facility)**	**385 days**	**Mon 4/7/14**	**Fri 9/25/15**	**Mon 4/7/14**	**NA**
1545	**Documents submitted in advance of 90%**	**140 days**	**Wed 4/30/14**	**Tue 11/11/14**	**Wed 4/30/14**	**NA**
1566	Prepare/submit Pre-Final Design Package	5.29 mons	Mon 4/7/14	Mon 9/8/14	Mon 4/7/14	Mon 9/8/14
1567	DTSC forward to CWG/TWG	1 day	Tue 9/9/14	Tue 9/9/14	Tue 9/9/14	Tue 9/9/14
1568	Agencies' direction #1 on Supplemental 90%	1 day	Tue 10/21/14	Tue 10/21/14	Tue 10/21/14	Tue 10/21/14
1569	Agencies' direction #2 on Supplemental 90%	1 day	Tue 12/23/14	Tue 12/23/14	Tue 12/23/14	Tue 12/23/14
1570	Prepare/submit Supplemental Pre-Final Design Package	104.38 edays	Tue 10/21/14	Mon 2/2/15	Tue 10/21/14	Mon 2/2/15
1571	CWG/TWG review/comment on Pre-Final Design Package	191.38 edays	Wed 9/10/14	Fri 3/20/15	Wed 9/10/14	Fri 3/20/15
1572	Tribal Consultation	163.38 edays	Wed 10/8/14	Fri 3/20/15	Wed 10/8/14	Fri 3/20/15
1573	BLM process after close of comment period	11.38 edays	Fri 3/20/15	Tue 3/31/15	Fri 3/20/15	Tue 3/31/15
1574	DTSC review/comment on Final Design Package	204.38 edays	Wed 9/10/14	Thu 4/2/15	Wed 9/10/14	Thu 4/2/15
1575	DOI review/comment on Final Design Package	202.38 edays	Wed 9/10/14	Tue 3/31/15	Wed 9/10/14	Tue 3/31/15
1576	**Response to Comments and Comment Resolution**	**126 days**	**Fri 4/3/15**	**Fri 9/25/15**	**Fri 4/3/15**	**Fri 9/25/15**
1590	DTSC issue direction on Final Design and Inputs on Final RTC Table	2 days	Mon 10/19/15	Tue 10/20/15	Mon 10/19/15	Tue 10/20/15
1591	DOI issue direction on Final Design and Inputs on Final RTC Table	2 days	Mon 10/19/15	Tue 10/20/15	Mon 10/19/15	Tue 10/20/15
1592	Prepare/submit Final Design Package	1 mon	Wed 10/21/15	Wed 11/18/15	Wed 10/21/15	NA
1593	**Construction/Remedial Action Work Plan**	**740.5 days**	**Mon 4/7/14**	**Mon 2/6/17**	**Mon 4/7/14**	**NA**
1594	Prepare/submit Draft Work Plan	5.29 mons	Mon 4/7/14	Mon 9/8/14	Mon 4/7/14	Mon 9/8/14
1595	DOI forward to DTSC/CWG/TWG	1 day	Tue 9/9/14	Tue 9/9/14	Tue 9/9/14	Tue 9/9/14
1596	CWG/TWG review/comment on Draft Work Plan	191.38 edays	Wed 9/10/14	Fri 3/20/15	Wed 9/10/14	Fri 3/20/15
1597	Tribal Consultation on Draft Work Plan	163.38 edays	Wed 10/8/14	Fri 3/20/15	Wed 10/8/14	Fri 3/20/15
1598	BLM process after close of comment period	11.38 edays	Fri 3/20/15	Tue 3/31/15	Fri 3/20/15	Tue 3/31/15
1599	DOI review/comment on Draft Work Plan	202.38 edays	Wed 9/10/14	Tue 3/31/15	Wed 9/10/14	Tue 3/31/15
1600	DTSC review/comment on Draft Work Plan	204.38 edays	Wed 9/10/14	Thu 4/2/15	Wed 9/10/14	Thu 4/2/15
1601	Response to Comments and Comment Resolution (see RTCs/Comment Resolution for Pre-Final Design)	126 days	Fri 4/3/15	Fri 9/25/15	Fri 4/3/15	Fri 9/25/15
1602	Prepare/submit Final Work Plan (duration to be confirmed after comment resolution)	1 mon	Wed 10/21/15	Wed 11/18/15	Wed 10/21/15	NA
1603	**State CEQA Evaluation**	**475.5 days**	**Mon 4/13/15**	**Mon 2/6/17**	**Mon 4/13/15**	**NA**
1604	Notice of Preparation	39 days	Mon 4/13/15	Thu 6/4/15	Mon 4/13/15	Thu 6/4/15
1605	Scoping Meetings	21 days	Tue 5/12/15	Tue 6/9/15	Tue 5/12/15	Tue 6/9/15
1606	**Preparation of Draft Subsequent EIR (SEIR)**	**302.5 days**	**Thu 8/6/15**	**Mon 10/3/16**	**Thu 8/6/15**	**NA**
1607	**Preparation of Project Description**	**97 days**	**Mon 9/7/15**	**Tue 1/19/16**	**Mon 9/7/15**	**NA**
1608	ESA Prepare Preliminary Project Description	8 wks	Mon 9/7/15	Fri 10/30/15	Mon 9/7/15	NA
1609	ESA Finalize Project Description	2 wks	Wed 11/18/15	Tue 12/1/15	NA	NA
1610	DTSC Review Project Description	3.5 wks	Wed 12/2/15	Fri 12/25/15	NA	NA
1611	ESA Revise Project Description	3.5 wks	Fri 12/25/15	Tue 1/19/16	NA	NA
1612	Tribal Input Process	4 mons	Thu 8/6/15	Tue 12/1/15	Thu 8/6/15	NA
1613	**Prepare Admin Draft SEIR**	**100 days**	**Mon 11/16/15**	**Fri 4/1/16**	**NA**	**NA**
1614	Aesthetic Site Visit and Analysis	9 wks	Tue 12/1/15	Mon 2/1/16	NA	NA
1615	Cultural Resources Evaluation	11.5 wks	Mon 11/16/15	Wed 2/3/16	NA	NA
1616	Noise Site Visit and Technical Evaluation	9 wks	Tue 12/1/15	Mon 2/1/16	NA	NA
1617	Traffic Site Visit and Technical Evaluation	6 wks	Mon 1/4/16	Fri 2/12/16	NA	NA
1618	ESA Prepare Admin Draft SEIR	17.6 wks	Wed 12/2/15	Fri 4/1/16	NA	NA
1619	DTSC Review Admin Draft SEIR	4 wks	Mon 4/4/16	Fri 4/29/16	NA	NA
1620	ESA Prepare 2nd Admin Draft SEIR	4 wks	Mon 5/2/16	Fri 5/27/16	NA	NA
1621	Tribal Meeting - Review Mitigation Concepts (date approximate)	0 days	Fri 5/27/16	Fri 5/27/16	NA	NA

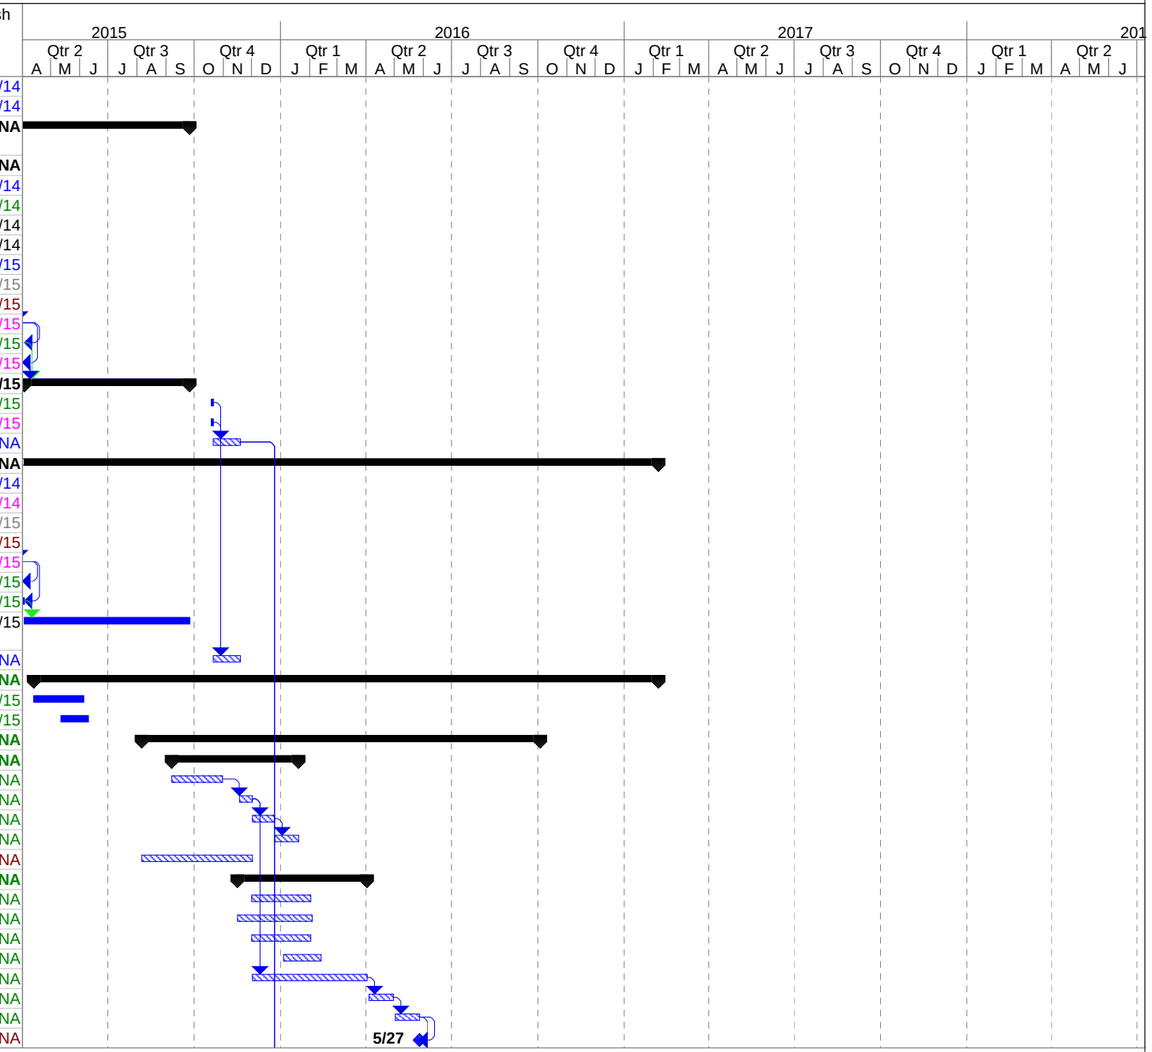

Project: PG&E Topock Remediation Project
Date: Fri 10/23/15

Tasks Not Started/In Progess
Tasks Finished
Baseline Schedule
Milestone
Overall Task Duration
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 14A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 28)
OCTOBER 28, 2015 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish
1622	DTSC Review 2nd Admin Draft SEIR	3 wks	Mon 5/30/16	Fri 6/17/16	NA	NA
1623	ESA Prepare Screencheck SEIR	2 wks	Mon 6/20/16	Fri 7/1/16	NA	NA
1624	DTSC Review Screencheck SEIR	2 wks	Mon 7/4/16	Fri 7/15/16	NA	NA
1625	ESA Address DTSC Comments on Screencheck SEIR	2.1 wks	Mon 7/18/16	Mon 8/1/16	NA	NA
1626	ESA Finalize/Print/Distribute Draft SEIR	2 wks	Tue 8/2/16	Tue 8/16/16	NA	NA
1627	**ESA Finalize Draft SEIR**	**33 days**	**Wed 8/17/16**	**Mon 10/3/16**	**NA**	**NA**
1628	**Draft SEIR Public Review**	**33 days**	**Wed 8/17/16**	**Mon 10/3/16**	**NA**	**NA**
1629	45-day Public Review	47 edays	Wed 8/17/16	Mon 10/3/16	NA	NA
1630	Public Meetings	5 days	Mon 9/5/16	Fri 9/9/16	NA	NA
1631	**Final EIR, Response to Comments (RTCs), Findings, MMRP**	**89 days**	**Tue 10/4/16**	**Mon 2/6/17**	**NA**	**NA**
1632	Draft SEIR Comment Review and FEIR Mod	2 wks	Tue 10/4/16	Tue 10/18/16	NA	NA
1633	ESA Compile/Prepare Admin Draft RTC/FEIR	5 wks	Tue 10/18/16	Tue 11/22/16	NA	NA
1634	DTSC Review Admin Draft RTC/FEIR/Findings	3 wks	Tue 11/22/16	Tue 12/13/16	NA	NA
1635	ESA Prepare Screencheck FEIR/Findings	3.4 wks	Tue 12/13/16	Thu 1/5/17	NA	NA
1636	DTSC Review Screencheck FEIR/Findings	2 wks	Fri 1/6/17	Fri 1/20/17	NA	NA
1637	ESA Produce FEIR for 10-day Circulation	1 wk	Fri 1/20/17	Fri 1/27/17	NA	NA
1638	10 Day FEIR Circulation	10 edays	Fri 1/27/17	Mon 2/6/17	NA	NA
1639	DTSC Certifies Final EIR/ESA Files NOD	0 days	Mon 2/6/17	Mon 2/6/17	NA	NA
1640	DTSC reviews/approves Final Design and Construction/Remedial Action Work Plan	291 days	Fri 12/25/15	Mon 2/6/17	NA	NA
1641	DOI reviews/approves Final Design and Construction/Remedial Action Work Plan	291 days	Fri 12/25/15	Mon 2/6/17	NA	NA
1642	**ROWs/Easements/Access Agreements/Approvals/Compliance**	**699.3 days**	**Tue 7/1/14**	**Mon 3/6/17**	**Tue 7/1/14**	**NA**
1643	Other Approvals and Compliance	33.3 mons	Tue 7/1/14	Mon 3/6/17	Tue 7/1/14	NA
1644	Landowner Agreements/Leasing/ROW Agreements	33.3 mons	Tue 7/1/14	Mon 3/6/17	Tue 7/1/14	NA
1645	**Community Outreach**	**1420.5 days**	**Fri 10/7/11**	**Thu 3/16/17**	**Fri 10/7/11**	**NA**
1646	Prepare/Issue Project Update Factsheet	4 mons	Fri 10/7/11	Tue 1/31/12	Fri 10/7/11	Tue 1/31/12
1647	**Community Outreach Activities (State)**	**1415.5 days**	**Fri 10/7/11**	**Thu 3/9/17**	**Fri 10/7/11**	**NA**
1648	Update mailing list	2.95 mons	Fri 10/7/11	Fri 12/30/11	Fri 10/7/11	Fri 12/30/11
1649	Conduct Community Survey	1.62 mons	Tue 1/31/12	Fri 3/16/12	Tue 1/31/12	Fri 3/16/12
1650	Conduct Community Interview	2 mons	Wed 4/25/12	Thu 6/21/12	Wed 4/25/12	Thu 6/21/12
1651	Prepare/Issue Community Outreach Plan	7.1 mons	Mon 3/19/12	Wed 1/16/13	Mon 3/19/12	Wed 1/16/13
1652	Prepare/Issue factsheet for Corrective Measures Implementation	30 edays	Tue 2/7/17	Thu 3/9/17	NA	NA
1653	**Outreach/Public Participation Activities (Federal)**	**27 days**	**Tue 2/7/17**	**Thu 3/16/17**	**NA**	**NA**
1654	Prepare/issue factsheet for Remedy Implementation	30 edays	Tue 2/7/17	Thu 3/9/17	NA	NA
1655	Open house (Multiple Locations)	1 wk	Thu 3/9/17	Thu 3/16/17	NA	NA
1656	Project Contracting	5 mons	Mon 1/23/17	Fri 6/16/17	NA	NA
1657	**Construction (this is a preliminary construction schedule for planning purposes only. See Section 3, Construction Approaches and Sequencing, of the Construction/Remedial Action Work Plan for details)**	**1009.5 days**	**Fri 6/16/17**	**Fri 4/30/21**	**NA**	**NA**
1658	**Pre-Construction**	**80 days**	**Fri 6/16/17**	**Sat 10/7/17**	**NA**	**NA**
1659	Mobilization	113 edays	Fri 6/16/17	Sat 10/7/17	NA	NA
1660	Site Preparation	70 edays	Sun 7/16/17	Sun 9/24/17	NA	NA
1661	Stakeholder Attending Kick-Off Meeting at Site	0 days	Fri 6/16/17	Fri 6/16/17	NA	NA
1662	Stakeholder Attending Kick-Off Meeting at Site	0 days	Fri 6/16/17	Fri 6/16/17	NA	NA
1663	Stakeholder Attending Kick-Off Meeting at Site	0 days	Fri 6/16/17	Fri 6/16/17	NA	NA
1664	Stakeholder Attending Kick-Off Meeting at Site	0 days	Fri 6/16/17	Fri 6/16/17	NA	NA
1665	Stakeholder Attending Kick-Off Meeting at Site	0 days	Fri 6/16/17	Fri 6/16/17	NA	NA
1666	**Construction Activities**	**941.8 days**	**Wed 8/16/17**	**Thu 3/25/21**	**NA**	**NA**
1667	Pipelines/Access Pathways Installation	18.5 mons	Wed 8/16/17	Mon 2/11/19	NA	NA
1668	Remediation and Monitoring Wells Installation	19 mons	Fri 9/15/17	Wed 3/27/19	NA	NA

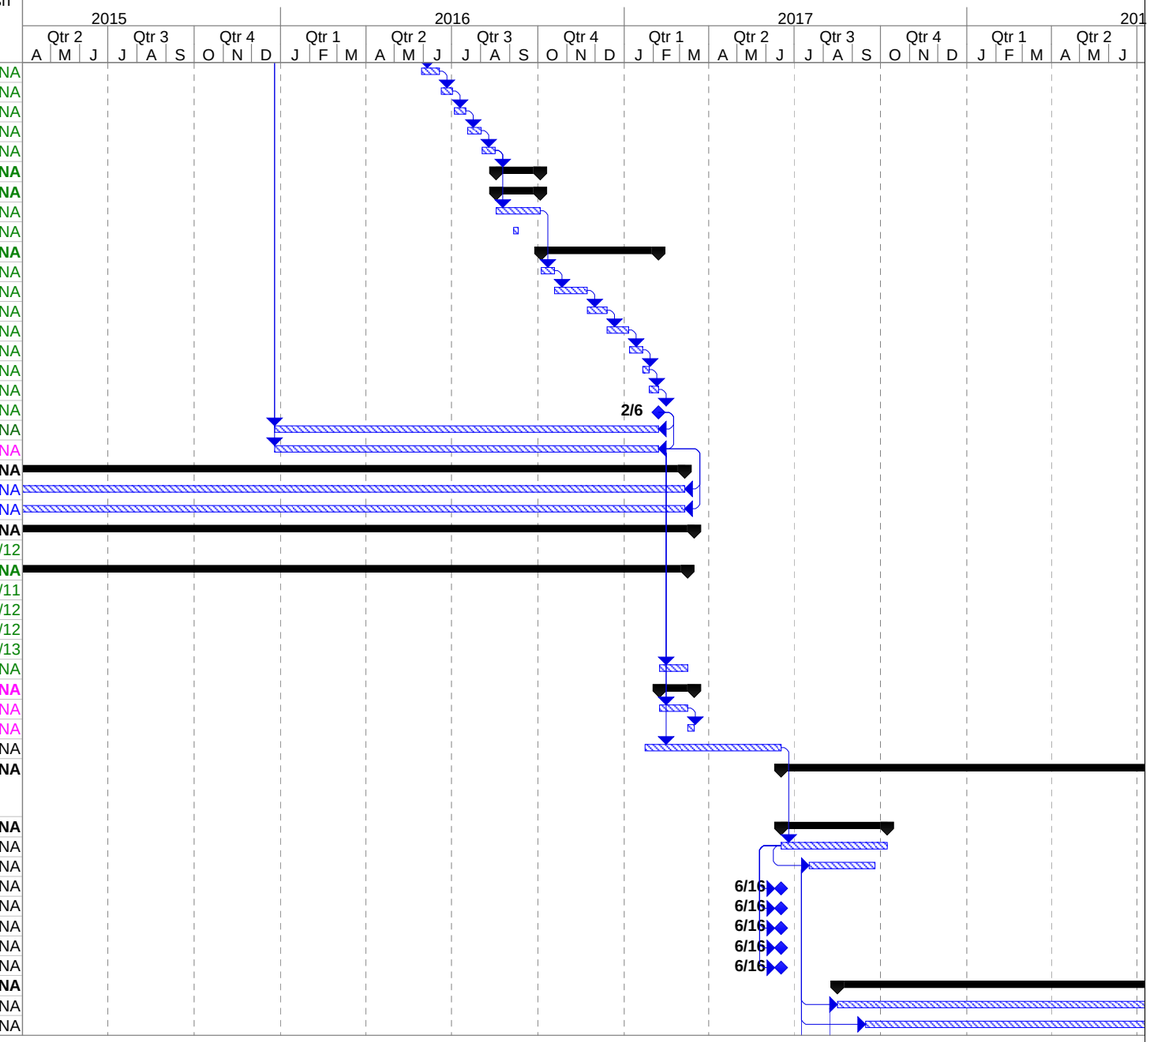

Project: PG&E Topock Remediation Project
Date: Fri 10/23/15

Tasks Not Started/In Progess
Tasks Finished
Baseline Schedule
Milestone
Overall Task Duration
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 14A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 28)
OCTOBER 28, 2015 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish
1669	Vertical Structures Installation	28 mons	Wed 8/16/17	Fri 11/15/19	NA	NA
1670	Commissioning	8.5 mons	Fri 5/24/19	Wed 1/29/20	NA	NA
1671	Construction Closeout	14.3 mons	Thu 1/30/20	Thu 3/25/21	NA	NA
1672	**Reporting**	**934.5 days**	**Mon 10/2/17**	**Fri 4/30/21**	**NA**	**NA**
1673	Prepare/submit monthly construction progress reports	44.5 mons	Mon 10/2/17	Fri 4/30/21	NA	NA
1674	**Startup**	**316 days**	**Wed 1/29/20**	**Thu 4/15/21**	**NA**	**NA**
1675	Shutdown IM extraction/treatment/injection	1 day	Wed 1/29/20	Thu 1/30/20	NA	NA
1676	Inject carbon/build NTH IRZ (6-12mons)	12 mons	Thu 1/30/20	Mon 1/18/21	NA	NA
1677	Inject freshwater(3-6mons)	6 mons	Fri 7/24/20	Mon 1/18/21	NA	NA
1678	Activate Inner recirculation loop (3-6mons)	6 mons	Wed 10/21/20	Thu 4/15/21	NA	NA
1679	Activate TCS recirculation loop (3-6mons)	6 mons	Wed 10/21/20	Thu 4/15/21	NA	NA
1680	Startup complete/start full remedy operations	0 days	Thu 4/15/21	Thu 4/15/21	NA	NA
1681	Start Operation and Maintenance	0 days	Thu 4/15/21	Thu 4/15/21	NA	NA

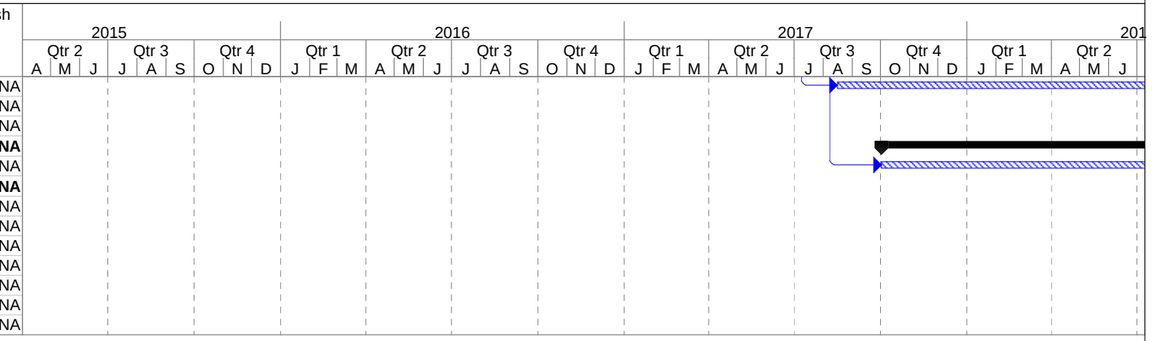

Project: PG&E Topock Remediation Project
Date: Fri 10/23/15

Tasks Not Started/In Progess
Tasks Finished
Baseline Schedule
Milestone
Overall Task Duration
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.
