HANDOUT 12A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 54)
DECEMBER 4, 2024 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish
1	**IM Installation (Note that IM3 is currently in operation and will remain in operation until directed otherwise by agencies)**	**512 days**	**Thu 1/22/04**	**Tue 12/20/05**	**Thu 1/22/04**	**Tue 12/20/05**
32	**IM3 Cultural Resources Management Plan (IM3 CRMP)**	**986 days**	**Thu 7/1/04**	**Mon 3/10/08**	**Thu 7/1/04**	**Mon 3/10/08**
37	**Extraction Well PE-1/Facilities**	**230 days**	**Mon 3/21/05**	**Fri 1/27/06**	**Mon 3/21/05**	**Fri 1/27/06**
47	**Supplemental Extraction Well and Facilities**	**127 days**	**Fri 7/29/05**	**Thu 1/19/06**	**Fri 7/29/05**	**Thu 1/19/06**
55	**Decommissioning of IM2 Batch Treatment**	**1182 days**	**Fri 8/5/05**	**Fri 1/29/10**	**Fri 8/5/05**	**Fri 1/29/10**
66	**Interim Measures and Treated Water Management**	**751 days**	**Mon 5/3/04**	**Fri 2/16/07**	**Mon 5/3/04**	**Fri 2/16/07**
210	**Public Participation Plan**	**578 days**	**Mon 12/20/04**	**Fri 2/9/07**	**Mon 12/20/04**	**Fri 2/9/07**
219	**Baseline Resources Assessments**	**897 days**	**Mon 11/1/04**	**Mon 3/10/08**	**Mon 11/1/04**	**Mon 3/10/08**
233	**Sitewide CEQA Documentation**	**586 days**	**Wed 5/17/06**	**Fri 8/1/08**	**Wed 5/17/06**	**Fri 8/1/08**
237	**Programmatic Biological Assessment (PBA)**	**1920 days**	**Tue 12/19/06**	**Tue 4/15/14**	**Tue 12/19/06**	**Tue 4/15/14**
250	**REMEDIAL FACILITY INVESTIGATION/REMEDIAL INVESTIGATION (RFI/RI)**	**7721 days**	**Sat 2/24/96**	**Wed 8/13/25**	**Sat 2/24/96**	**NA**
251	**Historical RFI/RI Reports (Feb. 2005 and Prior Versions)**	**2455 days**	**Sat 2/24/96**	**Fri 7/8/05**	**Sat 2/24/96**	**Fri 7/8/05**
269	**Site History Report (Vol 1)**	**466 days**	**Tue 11/15/05**	**Wed 8/15/07**	**Tue 11/15/05**	**Wed 8/15/07**
284	**RFI/RI Vol 1 Addendum**	**1829 days**	**Wed 7/11/07**	**Tue 7/8/14**	**Wed 7/11/07**	**Tue 7/8/14**
306	**Final Groundwater RFI/RI (Vol 2)**	**1948 days**	**Mon 6/27/05**	**Fri 11/16/12**	**Mon 6/27/05**	**Fri 11/16/12**
616	**ADEQ Topock Groundwater Study**	**475 days**	**Thu 11/18/04**	**Wed 8/23/06**	**Thu 11/18/04**	**Wed 8/23/06**
620	**Final Soil RFI/RI (Vol 3)**	**4994 days**	**Sat 7/15/06**	**Wed 8/13/25**	**Sat 7/15/06**	**NA**
621	**Implementation of Off-site Soil Sampling (Part A Phase 1) and Data Gaps Evaluation**	**1215 days**	**Sat 7/15/06**	**Fri 2/25/11**	**Sat 7/15/06**	**Fri 2/25/11**
770	**Draft On-site Soil Sampling (Part B) DQOs**	**1122 days**	**Wed 12/6/06**	**Fri 3/11/11**	**Wed 12/6/06**	**Fri 3/11/11**
825	**Soil RFI/RI Work Plan**	**1211 days**	**Tue 1/4/11**	**Mon 8/24/15**	**Tue 1/4/11**	**Mon 8/24/15**
922	**Work Plan Implementation/Data Gaps Analysis**	**594 days**	**Tue 8/25/15**	**Thu 11/30/17**	**Tue 8/25/15**	**Thu 11/30/17**
978	**Reporting**	**2131 days**	**Tue 6/20/17**	**Wed 8/13/25**	**Tue 6/20/17**	**NA**
979	**Soil Risk Assessment**	**770 days**	**Tue 6/20/17**	**Fri 5/29/20**	**Tue 6/20/17**	**Fri 5/29/20**
1002	**Soil Risk Assessment Addendum (After Completion of Soil NTCRA)**	**341 days**	**Wed 4/24/24**	**Wed 8/13/25**	**Wed 4/24/24**	**NA**
1003	Validated NTCRA Data Available for Risk Assessment Addendum	80 days	Wed 4/24/24	Tue 8/13/24	Wed 4/24/24	Tue 8/13/24
1004	PG&E prepares/submits Soil Risk Assessment Addendum Report	5 mons	Thu 6/6/24	Fri 12/13/24	Thu 6/6/24	NA
1005	DTSC review/comment	60 edays	Mon 12/16/24	Fri 2/14/25	NA	NA
1006	DOI review/comment	60 edays	Mon 12/16/24	Fri 2/14/25	NA	NA
1007	CWG/TWG review/comment	45 edays	Mon 12/16/24	Thu 1/30/25	NA	NA
1008	Tribes review/comment	45 edays	Mon 12/16/24	Thu 1/30/25	NA	NA
1009	Review/compile Comment Table	15 edays	Mon 2/17/25	Tue 3/4/25	NA	NA
1010	Prepare/send RTC Table (duration to be verified)	2 mons	Wed 3/5/25	Thu 5/1/25	NA	NA
1011	**RTC Meeting (Placeholder, Date to be confirmed)**	**12 days**	**Fri 5/16/25**	**Mon 6/2/25**	**NA**	**NA**
1012	Send agenda (2 wks prior to meeting)	1 day	Fri 5/16/25	Fri 5/16/25	NA	NA
1013	Hold Meeting	1 day	Mon 6/2/25	Mon 6/2/25	NA	NA
1014	Finalize/Submit Final Soil Risk Assessment Addendum with RTC Table	2 mons	Tue 6/3/25	Wed 7/30/25	NA	NA
1015	DTSC review/accept report	2 wks	Thu 7/31/25	Wed 8/13/25	NA	NA
1016	DOI review/accept report	2 wks	Thu 7/31/25	Wed 8/13/25	NA	NA
1017	**RFI/RI Volume 3**	**1807 days**	**Fri 7/28/17**	**Tue 6/25/24**	**Fri 7/28/17**	**Tue 6/25/24**
1018	**Draft RFI/RI Volume 3 Report**	**881 days**	**Fri 7/28/17**	**Thu 12/10/20**	**Fri 7/28/17**	**Thu 12/10/20**
1030	**Revised RFI/RI Volume 3 Report**	**312 days**	**Fri 12/11/20**	**Thu 2/17/22**	**Fri 12/11/20**	**Thu 2/17/22**
1044	Finalize RTC/Update Sections of Volume 3 Report	7.62 mons	Mon 2/21/22	Fri 9/30/22	Mon 2/21/22	Fri 9/30/22

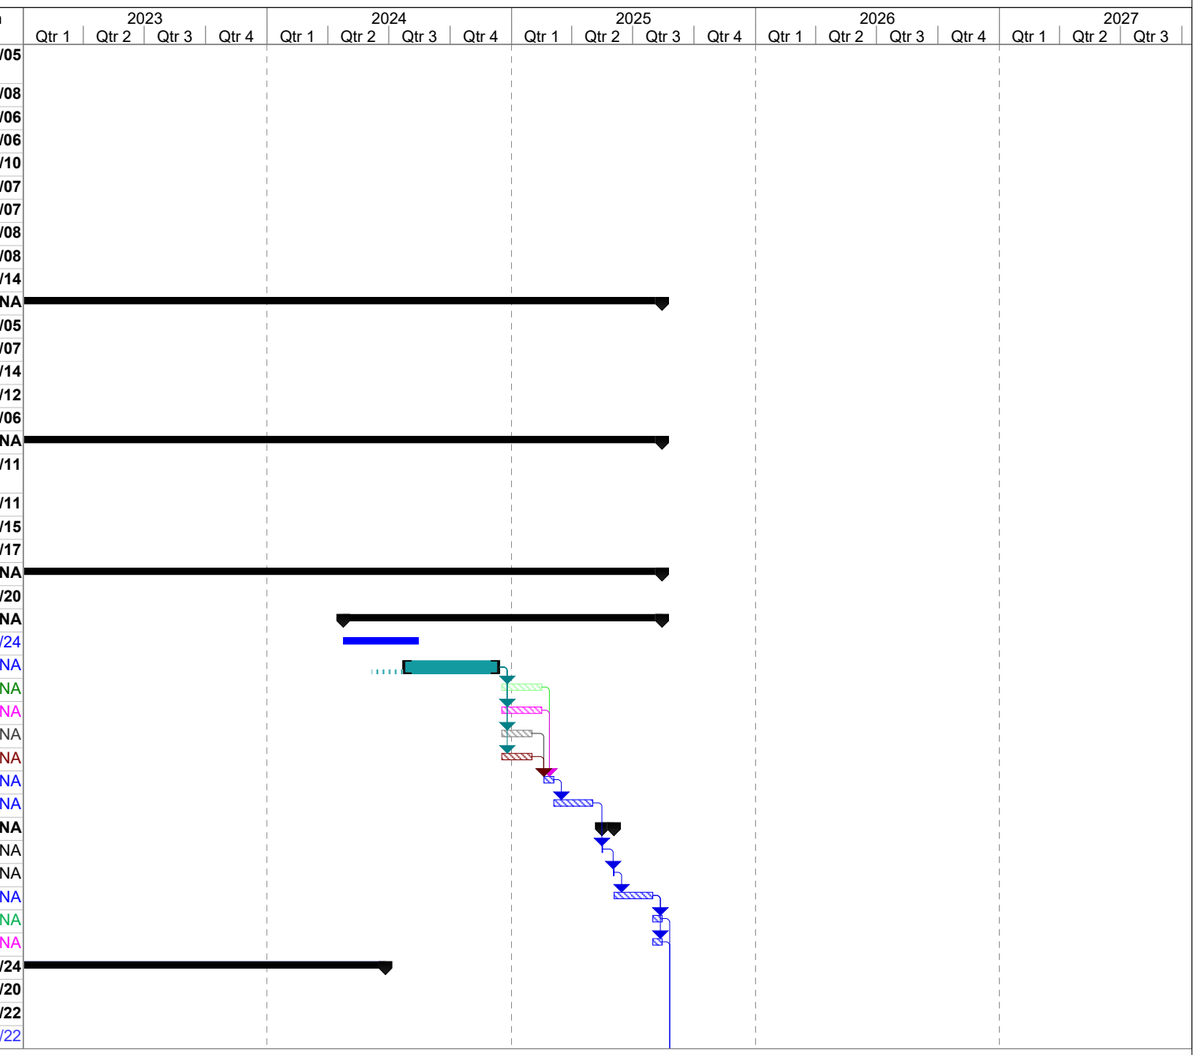

Project: PG&E Topock Remediation Project
Date: Fri 11/22/24

Tasks Not Started/In Progess
Tasks Finished
Baseline Schedule
Milestone
Overall Task Duration
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 12A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 54)
DECEMBER 4, 2024 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish
1045	CWG/TWG review/comment	120.38 edays	Mon 10/3/22	Tue 1/31/23	Mon 10/3/22	Tue 1/31/23
1046	DTSC review/comment	176.38 edays	Mon 10/3/22	Tue 3/28/23	Mon 10/3/22	Tue 3/28/23
1047	DOI review/comment	99.38 edays	Mon 10/3/22	Tue 1/10/23	Mon 10/3/22	Tue 1/10/23
1048	Prepare responses to comments	91.38 edays	Wed 3/29/23	Wed 6/28/23	Wed 3/29/23	Wed 6/28/23
1049	Comment resolution	14 days	Thu 7/13/23	Tue 8/1/23	Thu 7/13/23	Tue 8/1/23
1050	Prepare Final Report	2.1 mons	Wed 8/2/23	Mon 10/2/23	Wed 8/2/23	Mon 10/2/23
1051	DTSC review/approve	8.57 mons	Tue 10/3/23	Mon 6/10/24	Tue 10/3/23	Mon 6/10/24
1052	DOI review/approve	9.1 mons	Tue 10/3/23	Tue 6/25/24	Tue 10/3/23	Tue 6/25/24
1053	**SOIL NON-TIME CRITICAL REMOVAL ACTION (NTCRA)**	**1648.5 days**	**Tue 10/30/18**	**Mon 2/17/25**	**Tue 10/30/18**	**NA**
1054	DOI's Approval Memorandum for an Engineering Evaluation/Cost Analysis (EE/CA)	0 days	Tue 10/30/18	Tue 10/30/18	Tue 10/30/18	Tue 10/30/18
1055	PG&E prepares Draft Soil EE/CA	414 days	Wed 10/31/18	Fri 5/29/20	Wed 10/31/18	Fri 5/29/20
1056	BLM sends package to Tribes for Consultation	0 days	Wed 6/3/20	Wed 6/3/20	Wed 6/3/20	Wed 6/3/20
1057	Tribal Consultation	254.38 edays	Wed 6/3/20	Fri 2/12/21	Wed 6/3/20	Fri 2/12/21
1058	Public Review	63.38 edays	Wed 6/3/20	Wed 8/5/20	Wed 6/3/20	Wed 8/5/20
1059	DOI responds to comments received on the Draft Soil EE/CA	50 days	Mon 2/15/21	Fri 4/23/21	Mon 2/15/21	Fri 4/23/21
1060	DOI prepares Responsiveness Summary	67.38 edays	Mon 2/15/21	Fri 4/23/21	Mon 2/15/21	Fri 4/23/21
1061	PG&E finalizes EE/CA	67.38 edays	Mon 2/15/21	Fri 4/23/21	Mon 2/15/21	Fri 4/23/21
1062	DOI prepares Action Memorandum	8.14 mons	Mon 2/15/21	Mon 10/11/21	Mon 2/15/21	Mon 10/11/21
1063	DOI approved Action Memorandum	0 days	Tue 10/12/21	Tue 10/12/21	Tue 10/12/21	Tue 10/12/21
1064	PG&E submits Non-time Critical Removal (NTCRA) Work Plan	1 day	Fri 10/29/21	Fri 10/29/21	Fri 10/29/21	Fri 10/29/21
1065	BLM sends NTCRA Work Plan to Tribes	2 edays	Mon 11/1/21	Wed 11/3/21	Mon 11/1/21	Wed 11/3/21
1066	Tribal Consultation	48 edays	Wed 11/3/21	Tue 12/21/21	Wed 11/3/21	Tue 12/21/21
1067	DTSC and Stakeholders review/comment	57 edays	Mon 11/1/21	Tue 12/28/21	Mon 11/1/21	Tue 12/28/21
1068	DOI review/comment	49.38 edays	Mon 11/1/21	Mon 12/20/21	Mon 11/1/21	Mon 12/20/21
1069	PG&E compiles comments/prepares RTCs	87.38 edays	Tue 12/28/21	Fri 3/25/22	Tue 12/28/21	Fri 3/25/22
1070	Tribes review RTCs	2.6 wks	Fri 3/25/22	Wed 4/13/22	Fri 3/25/22	Wed 4/13/22
1071	DTSC and Stakeholders review RTCs	12 days	Fri 3/25/22	Tue 4/12/22	Fri 3/25/22	Tue 4/12/22
1072	Meeting to discuss RTCs	1 day	Tue 4/26/22	Tue 4/26/22	Tue 4/26/22	Tue 4/26/22
1073	Meeting to discuss RTCs	1 day	Thu 5/5/22	Thu 5/5/22	Thu 5/5/22	Thu 5/5/22
1074	PG&E Submits Redline RTCs	1 day	Tue 5/24/22	Tue 5/24/22	Tue 5/24/22	Tue 5/24/22
1075	FMIT provide input to RTC Table	1 day	Fri 6/3/22	Fri 6/3/22	Fri 6/3/22	Fri 6/3/22
1076	Quechan Tribe concur with FMIT comments	1 day	Mon 6/6/22	Mon 6/6/22	Mon 6/6/22	Mon 6/6/22
1077	PG&E addresses comments/finalizes NTCRA Work Plan	38 days	Wed 4/27/22	Fri 6/17/22	Wed 4/27/22	Fri 6/17/22
1078	DOI reviews/approves NTCRA Work Plan	0 days	Mon 6/27/22	Mon 6/27/22	Mon 6/27/22	Mon 6/27/22
1079	**PG&E implements NTCRA Work Plan**	**497 days**	**Mon 6/27/22**	**Mon 5/20/24**	**Mon 6/27/22**	**Mon 5/20/24**
1080	Stake corners of Target Action Areas	3 days	Mon 6/27/22	Wed 6/29/22	Mon 6/27/22	Wed 6/29/22
1081	Project Initiation Meeting - Online	1 day	Wed 7/6/22	Wed 7/6/22	Wed 7/6/22	Wed 7/6/22
1082	Project Initiation Meeting - Face-to-Face	1 day	Thu 7/14/22	Thu 7/14/22	Thu 7/14/22	Thu 7/14/22
1083	Collect Soil Samples for waste profiling, XRF/Lab Data comparison, and Dioxin Furan lab comparison	2 days	Fri 7/15/22	Mon 7/18/22	Fri 7/15/22	Mon 7/18/22
1084	Mobilization	8 days	Fri 7/15/22	Tue 7/26/22	Fri 7/15/22	Tue 7/26/22
1085	Soil Removal Activities (includes SPY restoration)	456 days	Tue 7/26/22	Mon 5/20/24	Tue 7/26/22	Mon 5/20/24
1086	PG&E prepares/submits the draft NTCRA Completion Report	23.8 wks	Tue 5/21/24	Fri 11/1/24	Tue 5/21/24	Fri 11/1/24
1087	Agencies review/comment on the draft report	7 wks	Mon 11/4/24	Fri 12/20/24	Mon 11/4/24	NA

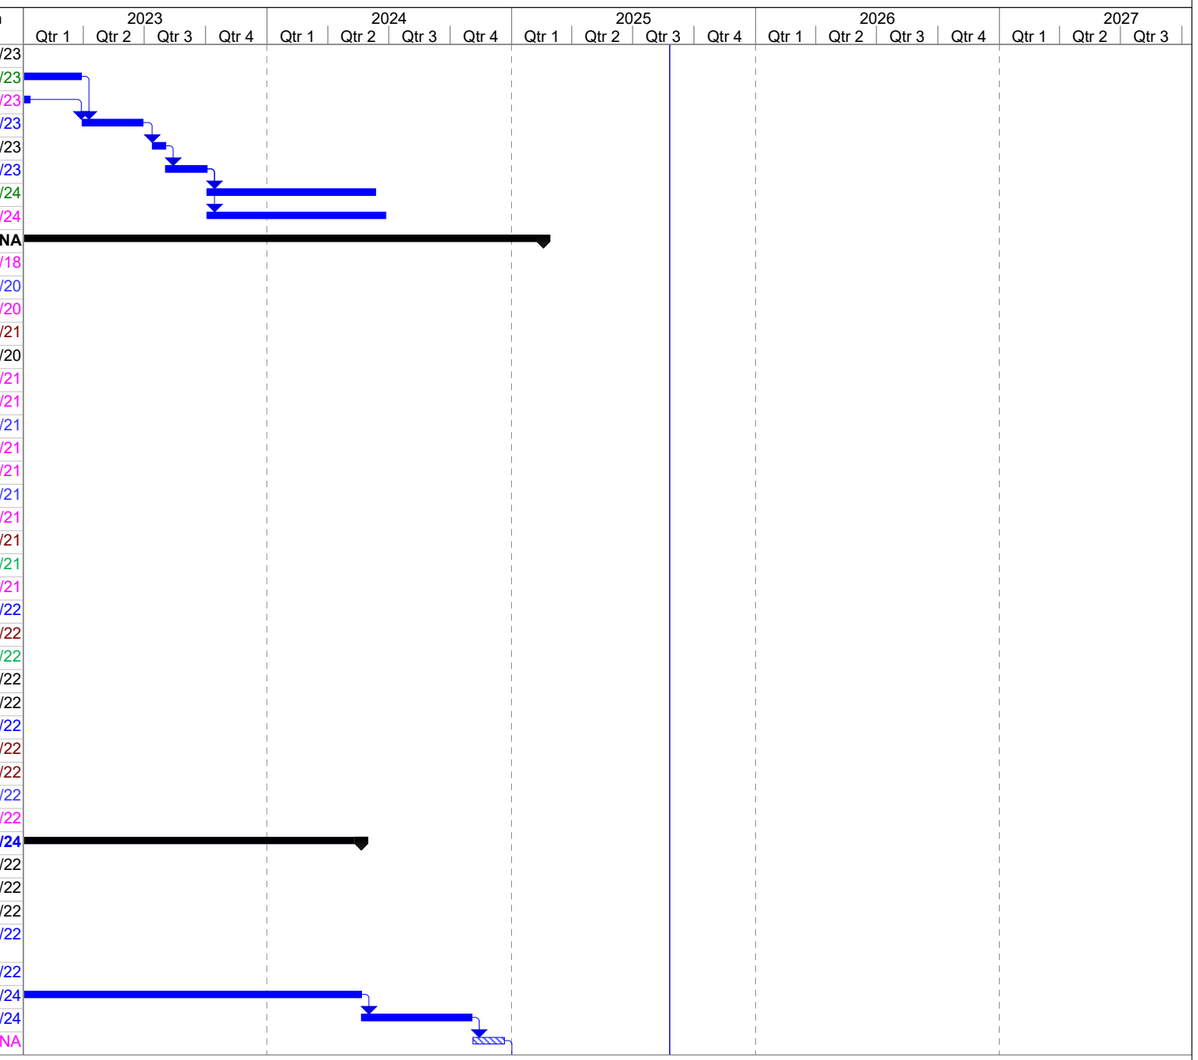

Project: PG&E Topock Remediation Project
Date: Fri 11/22/24

Tasks Not Started/In Progess
Tasks Finished
Baseline Schedule
Milestone
Overall Task Duration
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 12A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 54)
DECEMBER 4, 2024 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish
1088	PG&E address comments/finalized report	6.1 wks	Mon 12/23/24	Mon 2/3/25	NA	NA
1089	DOI review/accept report	2 wks	Mon 2/3/25	Mon 2/17/25	NA	NA
1090	**GROUNDWATER CORRECTIVE MEASURES/REMEDIAL ALTERNATIVE DEVELOPMENT**	**2835 days**	**Mon 3/29/04**	**Wed 12/31/14**	**Mon 3/29/04**	**Wed 12/31/14**
1238	**CORRECTIVE MEASURE STUDY/FEASIBILITY STUDY (CMS/FS) AND RISK ASSESSMENT**	**6379 days**	**Mon 12/16/02**	**Tue 4/13/27**	**Mon 12/16/02**	**NA**
1239	**CMS Work Plan**	**1465 days**	**Mon 12/16/02**	**Tue 6/24/08**	**Mon 12/16/02**	**Tue 6/24/08**
1258	**Risk Evaluation - Scoping and CSM**	**2326 days**	**Tue 10/31/06**	**Tue 9/15/15**	**Tue 10/31/06**	**Tue 9/15/15**
1342	**CMS/FS Report**	**4876 days**	**Mon 8/18/08**	**Tue 4/13/27**	**Mon 8/18/08**	**NA**
1343	**Groundwater**	**350 days**	**Mon 8/18/08**	**Fri 12/18/09**	**Mon 8/18/08**	**Fri 12/18/09**
1402	**Soil CMS/FS (duration to be verified after completion of RFI/RI)**	**434 days**	**Thu 8/14/25**	**Tue 4/13/27**	**NA**	**NA**
1403	**Prepare Draft Soil CMS/FS Report**	**264 days**	**Thu 8/14/25**	**Tue 8/18/26**	**NA**	**NA**
1404	Prepare Discussion Draft Soil CMS/FS Report	7 mons	Thu 8/14/25	Fri 3/6/26	NA	NA
1405	PG&E outreach with Tribes	1 mon	Mon 3/9/26	Mon 4/6/26	NA	NA
1406	PG&E submits Draft Soil CMS/FS	2 mons	Tue 4/7/26	Wed 6/3/26	NA	NA
1407	DTSC send Draft Soil CMS/FS to CWG/TWG	0 days	Wed 6/3/26	Wed 6/3/26	NA	NA
1408	BLM sends package to Tribes for Consultation	3 days	Thu 6/4/26	Mon 6/8/26	NA	NA
1409	DTSC review and comment	75 edays	Thu 6/4/26	Tue 8/18/26	NA	NA
1410	DOI review and comment	75 edays	Thu 6/4/26	Tue 8/18/26	NA	NA
1411	CWG/TWG review and comment	60 edays	Thu 6/4/26	Mon 8/3/26	NA	NA
1412	Tribal Consultation	60 edays	Tue 6/9/26	Sat 8/8/26	NA	NA
1413	SHPO for information only	1 day	Tue 6/9/26	Tue 6/9/26	NA	NA
1414	**Response to Comments/Prepare Final Soil CMS/FS Report (duration to be verified after receipt of comments)**	**86 days**	**Wed 8/19/26**	**Wed 12/16/26**	**NA**	**NA**
1415	Review/compile Comment Table	1 mon	Wed 8/19/26	Wed 9/16/26	NA	NA
1416	Comment clarification meeting	0 days	Tue 8/25/26	Tue 8/25/26	NA	NA
1417	Prepare/send RTC Table	2 mons	Thu 9/17/26	Fri 11/13/26	NA	NA
1418	**RTC Meeting**	**23 days**	**Fri 11/13/26**	**Wed 12/16/26**	**NA**	**NA**
1419	Send agenda (2 wks prior to meeting)	0 days	Fri 11/13/26	Fri 11/13/26	NA	NA
1420	Hold Multiple Meetings	13 days	Mon 11/30/26	Wed 12/16/26	NA	NA
1421	Prepare Final Soil CMS/FS Report	3 mons	Thu 12/17/26	Mon 3/15/27	NA	NA
1422	DTSC review and concur	1 mon	Tue 3/16/27	Tue 4/13/27	NA	NA
1423	DOI review and concur	1 mon	Tue 3/16/27	Tue 4/13/27	NA	NA
1424	CEQA Evaluation (Place Holder Item only. Details including duration will be provided after the prior steps are better defined))	3 mons	Wed 4/14/27	Fri 7/9/27	NA	NA
1425	**STATEMENT OF BASIS**	**4638 days**	**Mon 1/4/10**	**Thu 9/30/27**	**Mon 1/4/10**	**NA**
1426	**Groundwater**	**284 days**	**Mon 1/4/10**	**Mon 1/31/11**	**Mon 1/4/10**	**Mon 1/31/11**
1433	**Soil**	**121 days**	**Thu 4/15/27**	**Thu 9/30/27**	**NA**	**NA**
1434	Prepare fact sheet for proposed remedy	1 mon	Thu 4/15/27	Thu 5/13/27	NA	NA
1435	Prepare public notice package/Statement of Basis	2 mons	Wed 4/21/27	Thu 6/17/27	NA	NA
1436	Public Notice/Comment Period	46 edays	Fri 6/18/27	Tue 8/3/27	NA	NA
1437	Public Hearing	15 edays	Thu 7/1/27	Fri 7/16/27	NA	NA
1438	Prepare Responsiveness Summary	2 mons	Wed 8/4/27	Thu 9/30/27	NA	NA
1439	DTSC adopts final remedy	0 days	Thu 9/30/27	Thu 9/30/27	NA	NA
1440	**RECORD OF DECISION**	**4743 days**	**Fri 12/18/09**	**Wed 2/9/28**	**Fri 12/18/09**	**NA**

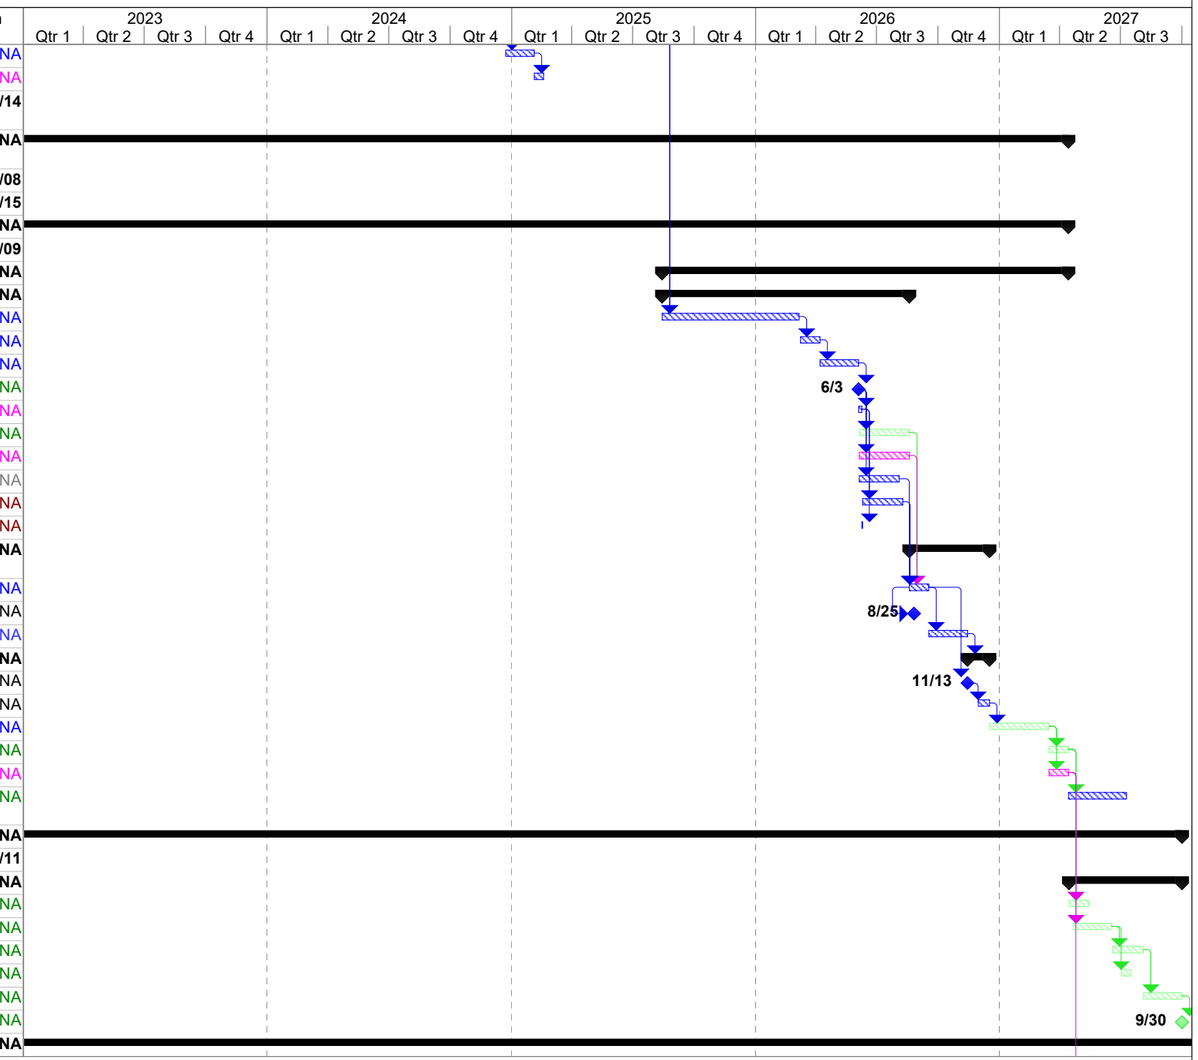

Project: PG&E Topock Remediation Project
Date: Fri 11/22/24

Tasks Not Started/In Progess
Tasks Finished
Baseline Schedule
Milestone
Overall Task Duration
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 12A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 54)
DECEMBER 4, 2024 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish
1441	**Groundwater**	**288 days**	**Fri 12/18/09**	**Thu 1/20/11**	**Fri 12/18/09**	**Thu 1/20/11**
1452	**Soil**	**216 days**	**Tue 4/13/27**	**Wed 2/9/28**	**NA**	**NA**
1453	Develop Proposed Plan	60 edays	Tue 4/13/27	Sat 6/12/27	NA	NA
1454	Prepare factsheet	60 edays	Tue 4/13/27	Sat 6/12/27	NA	NA
1455	Tribal Consultation	60 edays	Mon 6/14/27	Fri 8/13/27	NA	NA
1456	Public Review and Comment	45 edays	Mon 6/14/27	Thu 7/29/27	NA	NA
1457	CWG Review and Comment	45 edays	Mon 6/14/27	Thu 7/29/27	NA	NA
1458	PG&E Review and Comment	45 edays	Mon 6/14/27	Thu 7/29/27	NA	NA
1459	Prepare ROD and Responsiveness Summary	119 edays	Fri 8/13/27	Fri 12/10/27	NA	NA
1460	DOI Approval Process	60 edays	Fri 12/10/27	Tue 2/8/28	NA	NA
1461	Issue Soil ROD	1 day	Wed 2/9/28	Wed 2/9/28	NA	NA
1462	**Section 106 Programmatic Agreement (PA)**	**1858 days**	**Fri 10/10/08**	**Wed 11/18/15**	**Fri 10/10/08**	**NA**
1495	**EIR DOCUMENTATION**	**1449 days**	**Thu 9/1/05**	**Wed 3/2/11**	**Thu 9/1/05**	**Wed 3/2/11**
1496	Scoping of EIR needs	45 days	Thu 9/1/05	Tue 11/1/05	Thu 9/1/05	Tue 11/1/05
1497	DTSC/PG&E, MOU signed for EIR	40 days	Wed 11/2/05	Tue 12/27/05	Wed 11/2/05	Tue 12/27/05
1498	EIR Contractor Interviews and Contract Negotiations	47 days	Thu 7/27/06	Fri 9/29/06	Thu 7/27/06	Fri 9/29/06
1499	Project Initiation	1 day	Tue 1/2/07	Tue 1/2/07	Tue 1/2/07	Tue 1/2/07
1500	**Project and Remedy Alternatives Description and Technical Work Plan**	**376 days**	**Mon 9/10/07**	**Mon 2/16/09**	**Mon 9/10/07**	Mon 2/16/09
1515	**NOP and scoping**	**277 days**	**Thu 1/10/08**	**Fri 1/30/09**	**Thu 1/10/08**	**Fri 1/30/09**
1525	**Program EIR**	**680 days**	**Tue 7/29/08**	**Wed 3/2/11**	**Tue 7/29/08**	**Wed 3/2/11**
1568	**DESIGN, PERMITTING, AND CONSTRUCTION OF GROUNDWATER REMEDY**	**3210 days**	**Mon 1/31/11**	**Thu 5/11/23**	**Mon 1/31/11**	**Thu 5/11/23**
1569	**Corrective Measure Implementation/Remedial Design (CMI/RD) Workplan**	**199 days**	**Mon 1/31/11**	**Thu 11/3/11**	**Mon 1/31/11**	**Thu 11/3/11**
1583	**Remedial Design (Preliminary, Intermediate, and Pre-Final/Final)**	**1723 days**	**Tue 9/20/11**	**Tue 4/24/18**	**Tue 9/20/11**	**Tue 4/24/18**
1756	**Proposed Phase 2B Design Modification**	**116 days**	**Fri 12/2/22**	**Thu 5/11/23**	**Fri 12/2/22**	**Thu 5/11/23**
1757	Submit proposal to DTSC/DOI	1 day	Fri 12/2/22	Fri 12/2/22	Fri 12/2/22	Fri 12/2/22
1758	DTSC forward to CWG/TWG	1 day	Thu 12/22/22	Thu 12/22/22	Thu 12/22/22	Thu 12/22/22
1759	FMIT provided comments	0 days	Tue 3/7/23	Tue 3/7/23	Tue 3/7/23	Tue 3/7/23
1760	Quechan Indian Tribe provided concurrence with FMIT's comments	1 day	Tue 4/25/23	Tue 4/25/23	Tue 4/25/23	Tue 4/25/23
1761	DTSC provided comments	1 day	Mon 5/1/23	Mon 5/1/23	Mon 5/1/23	Mon 5/1/23
1762	DOI provided comments	1 day	Fri 5/5/23	Fri 5/5/23	Fri 5/5/23	Fri 5/5/23
1763	Site walk to view proposed locations	1 day	Thu 5/11/23	Thu 5/11/23	Thu 5/11/23	Thu 5/11/23
1764	**Community Outreach**	**1710 days**	**Fri 10/7/11**	**Tue 4/24/18**	**Fri 10/7/11**	**Tue 4/24/18**
1774	Project Contracting	2.9 mons	Wed 4/4/18	Wed 6/27/18	Wed 4/4/18	Wed 6/27/18
1775	**Construction**	**2015 days**	**Wed 6/27/18**	**Wed 3/11/26**	**Wed 6/27/18**	**NA**
1776	**Phase 1 Construction**	**1046 days**	**Wed 6/27/18**	**Fri 6/24/22**	**Wed 6/27/18**	**Fri 6/24/22**
1808	**Phase 2A Planning/Contracting**	**30 days**	**Mon 2/14/22**	**Fri 3/25/22**	**Mon 2/14/22**	**Fri 3/25/22**
1809	**Phase 2A Construction Mobilization**	**16 days**	**Mon 2/14/22**	**Mon 3/7/22**	**Mon 2/14/22**	**Mon 3/7/22**
1813	**Major Phase 2A Construction Activities**	**932 days**	**Tue 3/8/22**	**Tue 9/30/25**	**Tue 3/8/22**	**NA**
1822	**Phase 2B Planning/Contracting**	**9.3 mons**	**Wed 1/1/25**	**Wed 10/1/25**	**NA**	**NA**
1823	**Phase 2B Construction Mobilization**	**20 days**	**Wed 10/8/25**	**Wed 11/5/25**	**NA**	**NA**
1824	Stakeholder Attending Construction Kick-Off Meeting at Site	0 days	Wed 10/8/25	Wed 10/8/25	NA	NA
1825	Stakeholder Attending Construction Kick-Off Meeting at Site	0 days	Wed 10/8/25	Wed 10/8/25	NA	NA
1826	Stakeholder Attending Construction Kick-Off Meeting at Site	0 days	Wed 10/8/25	Wed 10/8/25	NA	NA
1827	Stakeholder Attending Construction Kick-Off Meeting at Site	0 days	Wed 10/8/25	Wed 10/8/25	NA	NA

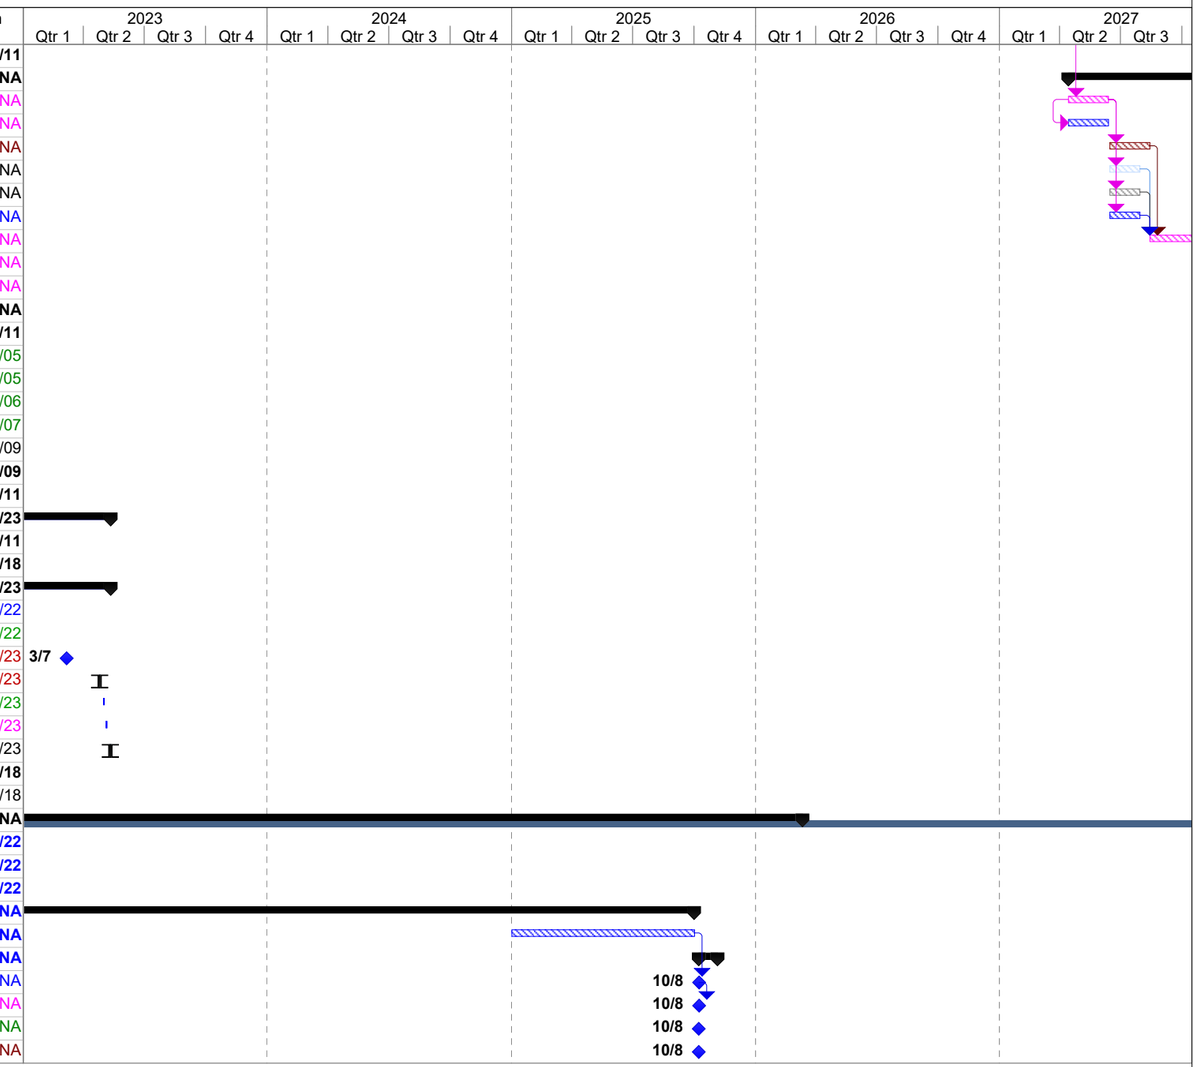

Project: PG&E Topock Remediation Project
Date: Fri 11/22/24

Tasks Not Started/In Progess
Tasks Finished
Baseline Schedule
Milestone
Overall Task Duration
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.

HANDOUT 12A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 54)
DECEMBER 4, 2024 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish
1828	Stakeholder Attending Construction Kick-Off Meeting at Site	0 days	Wed 10/8/25	Wed 10/8/25	NA	NA
1829	Mobilization	28 edays	Wed 10/8/25	Wed 11/5/25	NA	NA
1830	**Major Phase 2B Construction Activities**	**598 days**	**Wed 11/5/25**	**Fri 2/18/28**	**NA**	**NA**
1847	**Reporting**	**2247 days**	**Mon 11/12/18**	**Wed 6/16/27**	**NA**	**NA**
1848	Prepare/submit monthly construction progress reports	107 mons	Mon 11/12/18	Wed 6/16/27	NA	NA
1849	Complete Remedy Startup/Start Remedy Operation and Maintenance	0 days	Fri 2/18/28	Fri 2/18/28	NA	NA
1850	**First Five Year Review of Groundwater Remedy**	**160 days**	**Mon 5/1/23**	**Thu 12/7/23**	**Mon 5/1/23**	**Thu 12/7/23**
1851	Public Notice/Factsheet	0 days	Mon 5/1/23	Mon 5/1/23	Mon 5/1/23	Mon 5/1/23
1852	Request For Interview	30.38 edays	Mon 5/1/23	Wed 5/31/23	Mon 5/1/23	Wed 5/31/23
1853	Interview Period	60.38 edays	Thu 6/1/23	Mon 7/31/23	Thu 6/1/23	Mon 7/31/23
1854	Five-Year Review Report Preparation	220.38 edays	Mon 5/1/23	Thu 12/7/23	Mon 5/1/23	Thu 12/7/23
1855	Notice of Report Availability	0 days	Thu 12/7/23	Thu 12/7/23	Thu 12/7/23	Thu 12/7/23

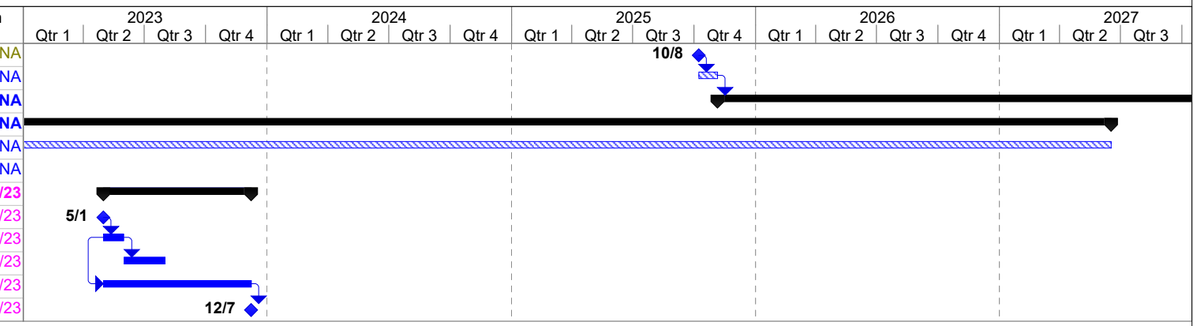

Project: PG&E Topock Remediation Project
Date: Fri 11/22/24

Tasks Not Started/In Progess
Tasks Finished
Baseline Schedule
Milestone
Overall Task Duration
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only

edays = calendar days; days = work days
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).
*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:
PG&E Federal Agencies CWG/TWG Public
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.
- Actual dates may vary depending on field conditions.
